

# OPERATIONS UPDATE



International Federation of Red Cross and Red Crescent Societies  
Fédération Internationale des Sociétés de la Croix-Rouge et du Croissant-Rouge  
Federación Internacional de Sociedades de la Cruz Roja y de la Media Luna Roja  
الاتحاد الدولي لجمعيات الصليب الأحمر والهلال الأحمر

## ALGERIA: EARTHQUAKE

23 September, 2003

**Appeal No. 14/03; Operations Update no. 03; Period covered: 1 June to 23 August, 2003.**  
(This Operations Update focuses particularly on the status of all relief goods received in response to the appeal).

**Appeal launched on 22 May 2003 for CHF 1,958,000 (USD 1,512,000 or EUR 1,293,000) for 3 months for 10,000-20,000 beneficiaries. Appeal revised 27 June 2003 for CHF 4,798,000 (USD or EUR for 40,000 beneficiaries, including an extension of the operation until May, 2004n.**

**Disaster Relief Emergency Funds (DREF) allocated: CHF 200,000 (has been reimbursed to the DREF)**

*The Federation's mission is to improve the lives of vulnerable people by mobilizing the power of humanity. It is the world's largest humanitarian organization and its millions of volunteers are active in over 180 countries.*

*For more information: [www.ifrc.org](http://www.ifrc.org)*

### ***In Brief***

**Appeal coverage: 122%; See the Contributions List on the Federation's website for details.**

**Outstanding needs: in view of the donor response to date the appeal is fully covered and there are no additional funding requirements. Any needs will be covered from the current funding; a revised appeal was issued on 27 June, 2003 following a more detailed Algerian Red Crescent (ARC) & FACT post-emergency assessment.**

**Related Emergency or Annual Appeals: 2003 North Africa Region Annual Appeal (01.92/2003)**

**Operational Summary:** Since the end of the search and rescue and emergency relief phases of the earthquake response operation, the Algerian Red-Crescent, supported by the Federation, has continued to address the needs of 5,000 (approximately 30,000 persons) of the most vulnerable families among an affected population of 175,661 living in the camps. Approximately 30,291 tents were erected in the emergency phase under the responsibility and direction of the Algerian Government. During that period, many families have returned to their original homes after some work on them to ensure they were habitable. However the majority of the affected population is expecting to be relocated from their current tent shelters into temporary pre-fabricated housing (see adjacent photograph) that will be their home until the construction of permanent housing is completed. This relocation and re-housing process will start in September but the full re-housing cycle is considered to be a relatively long-term process and the ARC and the Federation has make plans on the basis that they will be involved in relief support during that period of time.



**The ARC, supported by the Federation delegates assigned to the operation, retains its position as the primary operational humanitarian agency, particularly since many international agencies present during the**


first emergency weeks have now departed Algeria. With the added presence of the French and Spanish Red Cross, the Red Crescent and Red Cross is effectively providing ongoing relief support to the affected population and is focusing on the forthcoming relocation process. Indeed the case load and areas of responsibility for the ARC may increase in some sectors, and this will be reported on along with amended plans reflected in future updates. The complications encountered in previous operations regarding the role of the Protection Civile in disasters continues to pose challenges to the ideal relief management the Federation endeavours to maintain. However much progress has been made and in this operation a greater degree of accountability and control and reporting is evident though much still needs to be done with the ARC to advocate with the government for greater independent control of relief goods from international donors.

### Operational developments

The earthquake, measuring 6.7 on the Richter Scale, which struck an extensive area in northern Algeria at approximately 20:00 hours on Wednesday, May 21st 2003 was the biggest to hit North Africa since 1980. Its epicentre was located in the triangle formed by the urban centres Thenia, Boumerdes and Zemmouri. The impact and death toll was aggravated by the fact that, at the time at which the earthquake struck, a majority of people were at home watching a televised football match or the nightly news. The latest government figure at the end of June gives the number of deceased and injured at more than 2,268 and 10,261, respectively. Up to 27,371 families have been sheltered in 30,291 tents provided by the government and international donors (including the Red Crescent and Red Cross) in the following locations.

Location	# of Sites	# Tents	# of Persons
Alger	95	11,985	65,461
Boumerdes	125	17,796	108,493
Tizi-Ouzou	45	1,352	7,852
Blida	06	158	445

The plight of thousands of earthquake victims initiated a wave of solidarity among the local population and the international community. The response from the local population and industry was overwhelming including donations in kind, food, and the offer of active help. International response actually resulted in a surplus of goods in kind for the immediate response necessitating the Government coordinator, the Protection Civile to store the surplus in a central warehouse as their mandate demands. A relocation program for the disaster victims will focus on the set up by the government of 16,000 prefabricated houses located on the 2 affected willet of Algiers where 30 sites will accommodate 9,600 prefabricated houses and in Boumerdes 22 sites have been selected for 6,310 houses. The ARC have accepted a leading role supporting the government in providing essential social support services and the provision of goods and materials, household items, kitchen equipment and consumables to the population both in the tented camps and in the temporary pre-fabricated houses they are moving to. The map identifies the ARC areas of responsibility. For more details see the ARC web page <http://www.cra-dz.org/>

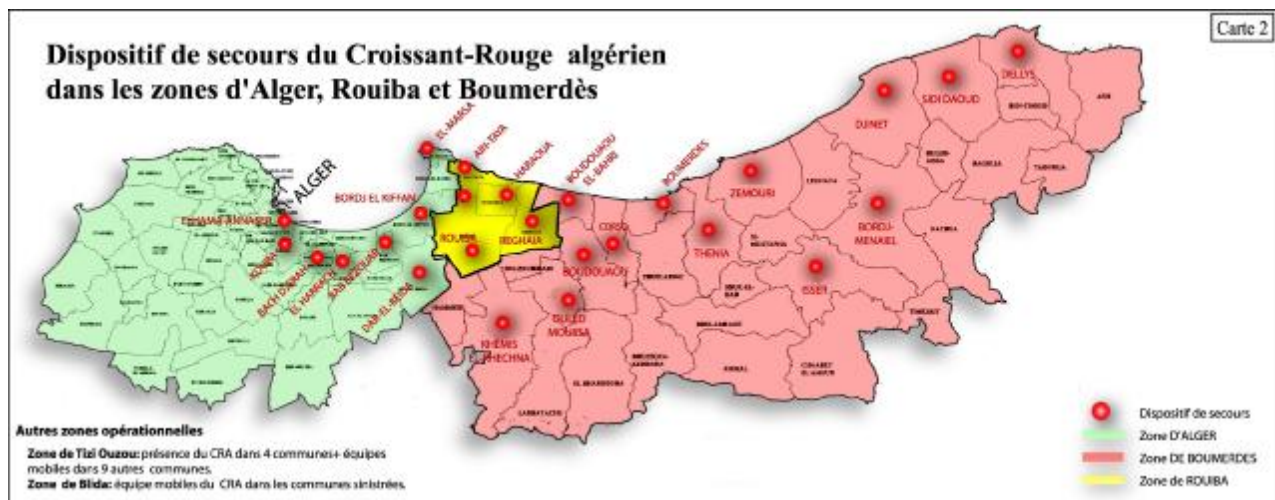

Given the present situation detailed above and the prognosis for an extended relief assistance operation during the re-location and re-housing phases ahead, the ARC and the Federation will need to review the Plan of Action, budget and the appeal objectives to reflect the added responsibility and activities the ARC will undertake. The generous response to the appeal does provide adequate funds to both extend the duration of the appeal period as well as the profile of the assistance and no further funds are requested. The amended PoA will be reported on and the appeal amended as needed in upcoming Operations Updates.

**Relief: distribution of food and basic non-food and medical items for up to 10,000-20,000 persons.**  
**Objective: Provide basic relief supplies, equipment and medical supplies to the affected area.**

*Camp Management:* The ARC continues to provide a daily service in relief distribution and camp management in the camps noted above. Through a well designed and efficiently functioning system of mobilization of all ARC branches in Algeria teams of volunteers rotate in a 10-day cycle passing through an Operations Center where they are equipped, briefed and transported to the camps they will support. The volunteers provide distribution, water and sanitation, health and social support and administrative support to the government agencies such as the Ministry of Health and Water. At the end of the mission the volunteers return to the Ops Centre for de-briefing and transportation back to their home regions. Detailed records of the management of each camp are included and these can be found on the ARC website. The Federation will support the core needs for this essential service as requested. This service is expected to be continued when the population starts to move into the pre-fabricated housing in September.

*Logistics:* Federation Logistics / Relief delegate was sent to Algeria towards the end of July on a two month mission to: a) verify and report on the status of all relief goods received in response to the Appeal, b) advise the ARC on continuing management, distribution and co-ordination of RC/RC support with the Protection Civile b) provide logistics training to ARC's staff and volunteers involved in the reception, transport, storage and distribution of relief goods, in order to improve the tracking of commodities, the management of warehouses and the production of reports, c) assist and advise the ARC in the local procurement of additional relief items to be distributed during the "relocation" phase to a targeted population of beneficiaries among the most needy.

**Objective: provide family tents, plastic sheeting, blankets, mattresses, bedding and generators.**

*Status of Red Cross and Red Crescent relief goods received:*

The table in annex 2 presents a preliminary consolidated report on all relief goods sent to Algeria in response to the Appeal, showing quantities received, distributed and in stock to date. During the initial phase of the emergency, as the bulk of the air-lifted relief supplies were entering the country, the Protection Civile under their government assigned mandate, was handling the reception and registration of all relief items, including RC/RC supplies. All in-coming goods, regardless of their origin, were handled through the Protection Civile "transit center" in El Hamiz, near the airport. Although the registration of goods was done in collaboration and co-ordination with ARC and the French RC Logistics ERU representatives, many RC/RC articles ended up being "taken over" by the Protection Civile and stored in their El Hamiz warehouses. Over the following weeks, relief supplies were released to the ARC and either stored in their own warehouses or distributed.

*Tents:* To date, all the tents that were taken over by the Protection Civile have been distributed and erected by them on various sites. This was carried out under strict government guidelines regarding the identification of beneficiaries and allocation of tents. The Protection Civile has explained that, given the huge international influx of goods over a very short period, it is impossible for them to indicate with complete accuracy where exactly on each site the RC/RC tents have been installed. Tents were recorded by country of origin when entering their warehouses, but subsequently were dispatched to the field "in bulk" according to the needs (on a total of more than 30,000 tents installed on 271 sites by the Algerian authorities, the Protection Civile received, dispatched and installed more than 20,000 of which 2,184 were RC/RC). To date, they have only 215 tents (non-RCRC) left in their warehouses. In some instances it is possible to identify RC/RC tents in the field (Swiss tents in Zemmouri, French tents in Boumerdes) but in most cases the tents bear no specific donor identification and cannot be specifically located to an individual site or beneficiary. As noted in the address by the President of the ARC to the governing board and donors during the first days of the earthquake response, the allocation of tents carries with it

### **Algeria: Earthquake; Appeal no. 14/03; Operations Update no. 3**

in Algeria the expectation of future permanent housing and as such is a highly political and sensitive issue the government insists must be coordinated by them.

*Kitchen sets:* To date only 17% of the kitchen sets received have been distributed. To minimize the risk of fire in the tents, ARC and the Protection Civile decided at the onset of the operation to install communal kitchens in most camps. The remaining sets will be distributed in Sep/Oct during the “relocation” phase.

*Blankets:* Approximately 25,000 RCRC blankets (including 10,000 outside the Appeal) are still in the Protection Civile warehouses however an agreement has now been made for the ARC to recuperate them prior to their distribution during the relocation phase (end of September and beginning of October). The majority of these blankets have not yet been distributed, as the weather is too hot during the summer. ARC feared that they would be used as carpets and be un-usable when the winter arrived. They will also be distributed in Sep/Oct during the relocation phase.

*Hygiene kits:* During the past two months the ARC has been distributing thousands of hygiene kits from “bulk” hygiene items received from private donors locally and internationally (adjacent picture). This represents a lot of



work as container-full of loose hygiene articles need to be sorted and put together as individual kits suited for men, women and children. ARC had decided to use these bulk articles first, so for the time being all the hygiene kits received in response to the Appeal are still in warehouses. It is planned to distribute them during the relocation as well and this has now commenced.

*Other distributions:* A significant amount of other (food and non-food) relief items were also received from local and international private donors. The ARC has been very active from the onset of the operation in until now in sorting and distributing these articles, many of which were perishable. Their decision was also to start with distribution of these relief goods, and keep most of the Appeal commodities to be distributed later (relocation phase) according to a planned schedule and targeted beneficiary population. Other RC/RC relief items that were under the management of the Protection Civile are either still in stock in their warehouses (plastic sheeting) and will also be recovered by ARC, or have already been distributed (jerry- cans, watsan tablets). At the request of the RC/RC and to ensure transparency, the Protection Civile has agreed to sign a “consolidated receipt” document indicating the nature and quantities of RC/RC relief supplies that they have taken over, distributed, and that they still have in stock. This will be reflected in the coming updates and reports.

#### *Logistics training:*

A basic logistics training seminar will take place during the last week of September. Using standard Federation training material, a program for a 3 day workshop is currently being prepared by the Logistics delegate, with a focus on commodity tracking, warehouse management, and reporting. Based on practical applications, the training aims at strengthening these key areas of the logistics chain, introducing Federation standards and procedures wherever appropriate and raising awareness on issues of reporting and accountability. Participants will be selected among ARC’s staff and volunteers. In order to encourage the collaboration and mutual understanding with the Protection Civile, it is planned to invite them to sent representatives to the workshop. It is hoped that this along with other planned DP and DR training will initiate an appropriate entry mechanism to advocate for greater autonomy for the ARC in the reception, warehousing and distribution of relief goods in future operations.

#### *Local procurement:*

The ARC will proceed with the local procurement of 1,500 refrigerators (160 litres capacity) and 1,500 two-burner gas stoves with tank and accessories. These items will be distributed to a first 1,500 households during the relocation phase. Beneficiaries will be selected among the most affected who will still be in need of these items (it is expected that many will have already acquired them through government or private donations or will already have been able to buy them). Kitchen sets and blankets from Red Cross and Red Crescent stocks as well as additional procurement (as needed) will be distributed during relocation, targeting the target 5,000 households.

### **Health and Care**

**Objective: Provide psychological, social and other support to effected population.**

Under their camp management functions described above, the ARC continues to provide psychological support and social services through both volunteers and professional counselors. To reinforce the ARC emergency services and to ensure adequate capacity to respond to routine emergencies in the affected population both now and in the next phase, the Federation will procure additional ambulances for the ARC existing service.

**Disaster Preparedness w**

**Objective: Disaster Preparedness- branch development.**

As intense periods of emergency and post emergency operational organization stabilizes the ARC are now turning to the need to address DP issues, not least of those that could impact on the population obliged to remain in temporary accommodation for some considerable period of time. Considerable donor fund have been allocated to the relief and rehabilitation phase and DP will play and important part of this. The next Operations Update will address the plans under discussion in more detail.

**Bilateral program**

*Spanish Red Cross*

As part of the hand over protocol of the Spanish Red Cross Basic Health care ERU a modular semi-permanent Health Centre (Picture right) has been constructed at Reghaïa. It is composed of 13 prefabricated modules each of them with their own electricity and telephone services. It is possible to transport the whole centre to a new site or to separate some of the modules and install them at different locations. Its 170-square-metre surface is divided in 6 consultation rooms, a pharmacy, a laboratory, a waiting room, and two toilets. It will give assistance to more than 40 patients/day. The prefabricated structure arrived to the port of Algiers on July 31<sup>st</sup>. The assembling of the centre was carried out in eight days



from the 3<sup>rd</sup> to the 11<sup>th</sup> of August. An agreement between the ARC, SRC and the Algerian Ministry of Health will be signed and the latter will be in charge of the centre. The funds for this centre come from the Autonomous Community of Madrid, the Council of Terrassa and SRC's own funds. A disaster-preparedness campaign aimed at the population of Reghaïa is being designed and will start within the next month. Other bilateral projects between ARC and SRC are being studied. A SRC delegate has been sent to support ARC in the assembling of the centre, the disaster-preparedness campaign and the identification of other projects.

*Swiss Red Cross*

A visit of the Swiss Red-Cross to the ARCS is linked to future bilateral co-operation in reconstruction and rehabilitation in addition to a program in favor of children and elderly living in "Zemmouri" camps.

*French Red Cross*

1. Summer camps by the sea for earthquake-affected children (*Colonies de vacances*)

A total of 8,500 vulnerable children are being sent for a 2-weeks vacation program organized by the ARC, aiming primarily at children affected and traumatized by the earthquake, but including also needy children from all over the country and victims of terrorism. A light ARC clothing outfit and hygiene products are distributed to each child at his arrival, basic health and sanitary education is provided every day, and psychological counsel is available in each camp. The ARC, which has a long experience in such operations, is in charge of selecting appropriate sites and obtaining all authorizations, recruiting experienced personnel, and organizing and managing completely the operational details of this operation. FRC provides technical support and funds 9 of these sites (all those receiving earthquake-affected children), including purchase of equipment (sanitary blocs, refrigerating storage equipment, gas stoves, educative and leisure material) and all running cost -except for staff wages. The FRC also contributes to the capacity building of the persons in charge of summer camps at the national committee and each participating ARC regional committee (budget construction and follow-up, reporting procedures, monitoring and evaluation, etc).

2. Cooking areas for families living in tent camps (*Espaces cuisine*)

**Algeria: Earthquake; Appeal no. 14/03; Operations Update no. 3**

Installation of 15 community cooking areas in tent camps to cook up to 300 meals per service, and a reserve of gas bottles to last for 2 months. The ARC has selected the sites most in need of such a space, and is in charge of the installation of the cooking areas.

3. Back to school (*Rentrée scolaire*)

Over 120 000 notebooks and a pack of school-year agendas, both printed on the inside covers with first aid recommendations and the humanitarian principles of the RC/RC movement, will be distributed to earthquake-affected children when they go back to school in October.

4. Hygiene products (*Produits hygiène*)

In coordination with other supplies from RC/RC donors the distribution of individual hygiene sets. Distributions are organized regularly by ARC volunteers to targeted families living in temporary tent camps.

**For further information please contact:**

- **DMC Head of Operations Iain Logan; email [iain.logan@ifrc.org](mailto:iain.logan@ifrc.org) phone: +41.22.730.4984 fax: +41.22.733.0395**
- **Federation regional office in Tunis: Anne Leclerc email [ifrctu01@ifrc.org](mailto:ifrctu01@ifrc.org); phone:+216.718.62485**
- **Regional Department: Evgeni Parfenov; email, [evgeni.parfenov@ifrc.org](mailto:evgeni.parfenov@ifrc.org) phone,+41.22.730.4325**

*All International Federation assistance seeks to adhere to the Code of Conduct and is committed to the Humanitarian Charter and Minimum Standards in Disaster Response (SPHERE Project) in delivering assistance to the most vulnerable.*

*For support to or for further information concerning Federation programmes or operations in this or other countries, please access the Federation website at <http://www.ifrc.org>*

# Algeria - Earthquake

ANNEX 1

APPEAL No. 14/2003

## PLEDGES RECEIVED

22.09.2003

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
-------	----------	----------	------	-----------	------	---------

### CASH

REQUESTED IN APPEAL CHF ----->	4'798'000		TOTAL COVERAGE 122.0%
AMERICAN - PRIVATE DONORS		7'734	03.06.03
AMERADA HESS LTD	25'000	USD	32'188 22.05.03
AUSTRALIAN - PRIVATE DONOR	85	USD	109 18.06.03
BELGIUM - GOVT	2'782	EUR	4'309 26.05.03
BP	400'000	USD	540'400 29.07.03
BRITISH - GOVT/DFID	93'137	GBP	207'136 30.06.03
BRITISH - RC	490'000	DZD	8'196 02.07.03
BRITISH - PRIVATE DONORS			33'733 30.05.03
ABACUS TSY	79'340	USD	107'188 14.07.03
CANADIAN - GOVT/RC	198'000	CAD	185'526 22.05.03
CANADIAN - RC	90'495	CAD	91'445 12.09.03
CHINESE - RC	50'000	USD	64'375 13.06.03
CROATIAN - RC	15'000	EUR	22'665 27.05.03
DANISH - GOVT	6'702	USD	8'629 16.06.03
FINNISH - RC	50'000	EUR	73'175 30.05.03
HELLENIC - RC	10'000	EUR	15'110 26.05.03
ICELANDIC - RC	1'000'000	ISK	17'898 22.05.03
IRISH - GOVT	500'000	EUR	771'500 26.05.03
JAPANESE - RC	49'900	USD	67'839 21.05.03
KOREA, REPUBLIC - RC			30'000 28.05.03
KUWAIT - RC	200'000	USD	272'000 28.05.03
LIBYAN - RC			10'000 24.05.03
LIECHTENSTEIN - PRIVATE DONORS			100 01.07.03
MEDICOR FOUNDATION	100'000	GBP	220'350 18.04.2503
MONACO - RC	15'000	EUR	22'838 03.06.03
MONACO - RC	29'719	EUR	45'856 04.07.03
NORWEGIAN - GOVT/RC	1'133'333	NOK	219'300 03.06.03
OPEC	500'000	USD	679'750 23.05.03
PRIVATE DONORS			25'906 03.07.03
SWEDISH - GOVT	1'000'000	SEK	168'000 23.05.03
WHO/VERF			2'000 26.05.03
SWISS - PRIVATE DONORS			100 18.06.03
WESTERN UNION FOUNDATION	50'000	USD	67'975 28.05.03
SUB/TOTAL RECEIVED IN CASH			4'023'330 CHF 83.9%

### KIND AND SERVICES (INCLUDING PERSONNEL)

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
AMERICAN - RC/BULGARIAN - RC				28'000	28.05.03	4000 HYGIENIC PARCELS
BELGIUM - RC		42'794	EUR	66'288	28.05.03	100 TENTS, 1020 BLANKETS, 10'0000 WAT.PURIF. TAB., 5 HEALTH KITS
BRITISH - RC				209'045	28.05.03	599 TENTS, 6030 BLANKETS, 2010 PLASTIC SHEET. 603 KITCHEN SETS, 1960 JERRY CANS

# Algeria - Earthquake

ANNEX 1

APPEAL No. 14/2003

## PLEDGES RECEIVED

22.09.2003

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
BRITISH - PRIVATE DONOR				15'500	28.05.03	900 BLANKETS, 500 PLASTIC SHEET.
CANADA	DELEGATE(S)			6'242		
DANISH - GOVT		103'113	USD	132'758	16.06.03	2400 TARPULINS, 5040 KITCHEN SETS
FRENCH - RC		255'000	EUR	385'305	26.05.03	LOGISTICS & WATSAN ERU FOR 1 MONTH
FRENCH - RC				346'000	28.05.03	1480 TENTS, 10'000 BLANKETS
GERMAN - RC				17'000	28.05.03	1000 BLANKETS, 480 KITCHEN SETS
IRANIAN - RC				70'000	28.05.03	200 TENTS, 4000 BLANKETS, 400 KITCHEN SETS
SLOVENIAN - RC				1'390	28.05.03	278 BLANKETS
SPANISH - RC		167'585	EUR	259'757	27.05.03	BASIC HEALTH CARE ERU FOR 1 MONTH
SPANISH - RC				10'102	28.05.03	586 HYGIENIC PARCELS, 600' WATER PURIFICATION TABLETS
SWISS - RC				142'600	28.05.03	215 TENTS, 1000 PLASTIC SHEET. , 2000 KITCHEN SETS, 10 GENERATORS
SYRIAN - RC				45'000	28.05.03	200 TENTS, 1000 BLANKETS
TURKISH - RC				40'000	28.05.03	200 TENTS
UAE - RC				35'000	28.05.03	150 TENTS, 1500 BLANKETS
YUGOSLAVIAN - RC				20'000	28.05.03	3000 BLANKETS, 200 KITCHEN SETS
SUB/TOTAL RECEIVED IN KIND/SERVICES				1'829'987	CHF	38.1%

## ADDITIONAL TO APPEAL BUDGET

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
HUNGARIAN - RC		20'675	USD	27'931	09.07.03	BILATERAL, MEDICAL RELIEF
SUB/TOTAL RECEIVED				27'931	CHF	

# Algeria Earthquake

## Preliminary Consolidated Report: Goods Arrived / Distributed / In Stock

Last Update: 26.aout.03

Commodity	Commodity Tracking Number	Quantity SENT	Unit	Quantity RECEIVED	Unit	Date Received	Donor	Delivered to	DISTRIBUTED				IN STOCK			Remarks	
									Quantity	Unit	Location (Site)	No. of Beneficiaries	Quantity	Unit	WAREHOUSE		
	Ref. Donor No.																
NHEK	DZ MED BE 03005	5	pce	5	pce	25-mai-03	Belgium RC	PC/ARC	2	pce	BHC ERU	n/a	3	pce	ERU (Boumerdes)	2 Kits used by BHC ERU	
Family tents	DZ SHE BE 03006	100	pce	100	pce	25-mai-03	Belgium RC	ARC	100	pce	Zemmouri	600	0	pce		See Note 1	
Blankets	DZ SHE BE 03007	1'020	pce	1'020	pce	25-mai-03	Belgium RC	ARC	0	pce			1'020	pce	ERU (Boumerdes)	34 Bales x 30 pces	
Wattablets	DZ WAT BE 03008	10'000	pce	10'000	pce	25-mai-03	Belgium RC	ARC	10'000	pce	Ouled Moussa	n/a	0	pce		Boumerdes / Ouled Moussa	
Tents	DZ SHE CH 03036	215	pce	215	pce	26-mai-03	Swiss RC	PC	215	pce	Zemmouri	1'300	0	pce		See Note 2	
Kitchen sets	DZ SHE CH 03019	2'000	pce	1'327	pce	26-mai-03	Swiss RC	ARC	1'315	pce	Zemmouri	7'890	0	pce		See Note 3	
Generator 4 kva	DZ VEH CH 03020	10	pce	10	pce	5-juin-03	Swiss RC	ARC	0	pce			10	pce	Diar Essaada		
Plastic Sheeting	DZ SHE CH 03037	1'000	pce	1'000	pce	5-juin-03	Swiss RC	ARC	0	pce			1'000	pce	Diar Essaada		
Blankets	DZ SHE DE 03022	1'000	pce	1'000	pce	6-juin-03	German RC	ARC	400	pce	Boudouaou el Bahri	400	600	pce	ERU (Boumerdes)		
Sleeping bags	DZ SHE DE 03024	500	pce	500	pce	23-mai-03	German RC	ARC	0	pce			500	pce	ERU (Boumerdes)		
Kitchen sets	DZ SHE DE 03025	480	pce	480	pce	23-mai-03	German RC	ARC	100	pce	Boudouaou el Bahri	600	380	pce	ERU (Boumerdes)		
Vehicle	DZ VEH DE 03026	1	pce	1	pce	23-mai-03	German RC	ARC	n/a	pce			n/a	pce		Allocated to ARC Ops in the field	
Kitchen sets	DZ SHE DK 03047	5'040	pce	5'040	pce	10-juin-03	Danish RC	ARC	0	pce			5'040	pce	Shaiba		
Plastic Sheeting	DZ SHE DK 03046	2'400	pce		pce		Danish RC			pce				pce		See Note 4	
Disco beds	DZ OTH ERU 03035	20	pce	20	pce	25-mai-03	Spanish RC	ARC	1	pce	Reghaia		1	pce	Diar Essaada		
Basic Health Care ERU	DZ ERU ES 03035	1	eru	1	eru	25-mai-03	Spanish RC	ARC	1	eru	Reghaia		1	eru	Diar Essaada	See Note 5	
Body bags	DZ SHE ES 03041	1'500	pce	1'500	pce	27-mai-03	Spanish RC	PC	1'500	pce	Various sites		0	pce			
Hygiene kit	DZ HYG ES 03029	586	pce	586	pce	24-mai-03	Spanish RC	ARC	0	pce			586	pce	Diar Essaada	Not distributed yet	
Sanitation kit	DZ HYG ES 03030	50	pce	50	pce	24-mai-03	Spanish RC	ARC	16	pce	Various sites		34	pce	Diar Essaada	See Note 6	
Watsan tablets	DZ WAT ES 03031	600'000	pce	562'500	pce	24-mai-03	Spanish RC	ARC	23%	pce	Reghaia		457'500	pce	Diar Essaada	See Note 7	
Waterfilter	DZ WAT ES 03032	100	pce	99	pce	24-mai-03	Spanish RC	ARC	0	pce			99	pce	Diar Essaada	Missing 1 filter on arrival	
Vehicle	DZ VEH ES 03033	1	pce	1	pce	24-mai-03	Spanish RC	ERU	n/a	pce	Reghaia			pce		Used by ERU. Sent back to Spain	
Rubbhall	DZ SHE ES 03058	2	pce	2	pce	2-juin-03	Spanish RC	ERU	n/a	pce	Reghaia	n/a	1	pce	Diar Essaada	See Note 8	
Sleeping bags	DZ SHE ES 03059	42	pce	42	pce	2-juin-03	Spanish RC	ERU	n/a	pce	Reghaia			pce		Used by BHC ERU	
Cholera kit	DZ MED ES 03057	1	pce	1	pce	?	Spanish RC	MoH		pce	Algiers			pce		See Note 9	

Commodity	Commodity Tracking Number				Quantity SENT	Unit	Quantity RECEIVED	Unit	Date Received	Donor	Delivered to	DISTRIBUTED				IN STOCK			Remarks
												Quantity	Unit	Location (Site)	No. of Beneficiaries	Quantity	Unit	WAREHOUSE	
Blankets	DZ	SHE	ES	03060	5'000	pce	5'000	pce	04.juin.03	Spanish RC	PC					5'000	pce	PC El Hamiz	In stock at Protection Civile
Hygiene kit	DZ	HYG	ES	03061	499	pce	499	pce	4-juin-03	Spanish RC	ARC	0	pce			499	pce	Diar Essaada	
Baby kit	DZ	HYG	ES	03062	300	pce	292	pce	4-juin-03	Spanish RC	ARC	0	pce			292	pce	Diar Essaada	8 kits missing on arrival
Sleeping bags	DZ	SHE	ES	03063	750	pce	750	pce	4-juin-03	Spanish RC	ARC	0	pce			750	pce	Diar Essaada	
Blankets	DZ	SHE	FED	03011	1'800	pce	1'800	pce	3-juin-03	Federation	ARC	0	pce			1'800	pce	ERU (Boumerdes)	60 bales x 30 pces
ERU Logistics	DZ	ERU	FR	03027	1	ERU	1	ERU	24-mai-03	French RC	ERU	1	ERU	Boumerdes	n/a		ERU		
ERU Watsan	DZ	ERU	FR	03028	1	ERU	1	ERU	25-mai-03	French RC	ERU	1	ERU	Boumerdes			ERU		
Tents	DZ	SHE	FR	03038	1'480	pce	1'480	pce	27-mai-03	French RC	ARC/PC	1'100	pce	Boumerdes		380	pce	Diar Essaada	See Note 10
Blankets	DZ	SHE	FR	03039	9'000	pce	9'000	pce	8-juin-03	French RC	ARC		pce			8'820	pce	Diar Essaada	See Note 11
Vehicles	DZ	VEH	FR	03040	2	pce	2	pce	5-juin-03	French RC	ARC		pce				pce		Vehicles currently used in the field
Kitchen sets	DZ	SHE	GB	03014	603	kit	603	kit	25-mai-03	British RC	ARC	0	kit			587	kit	Diar Essaada	Six sets damaged during transport to WH
Plastic sheeting	DZ	SHE	GB	03015	2'010	pce	2'010	pce	25-mai-03	British RC	PC	0	pce			2'010	pce	PC El Hamiz	In stock at Protection Civile
Jerrycans	DZ	WAT	GB	03016	1'960	pce	1'960	pce	25-mai-03	British RC	PC	1'960	pce	?	?	0	pce		See Note 12
Blankets	DZ	SHE	GB	03017	6'030	pce	6'030	pce	25-mai-03	British RC	PC	0	pce			6'030	pce	PC El Hamiz	In stock at Protection Civile
Tents	DZ	SHE	GB	03018	599	pce	423	pce	25-mai-03	British RC	PC	423	pce			0	pce		See Note 13
Blankets	DZ	SHE	GR	03010	3'000	pce	3'000	pce	3-juin-03	Hellenic RC	PC/ARC	0	pce			3'000	pce	ERU (Boumerdes)	
Tents	DZ	SHE	IR	03001	200	pce	200	pce	26-mai-03	Iran RC	PC	200	pce				pce		Distributed by Protection Civile
Blankets	DZ	SHE	IR	03002	2'000	pce	2'558	pce	26-mai-03	Iran RC	PC	0	pce			2'558	pce	PC El Hamiz	See Note 14
Kitchen sets	DZ	SHE	IR	03003	400	pce	400	pce	26-mai-03	Iran RC	ARC	0	pce			400	pce	Diar Essaada	See Note 15
Canned food	DZ	FOO	IR	03004	5'000	kg	5'000	kg	26-mai-03	Iran RC	ARC	5'000	kg	Various sites		0	kg		See Note 16
Plastic sheeting	DZ	SHE	PRI	03043	500	pce	500	pce	28-mai-03	Anadarko	PC	0	pce			500	pce	PC El Hamiz	In stock at Protection Civile
Blankets	DZ	SHE	PRI	03044	900	pce	900	pce	2/4-Jun-03	Anadarko	PC	0	pce			900	pce	PC El Hamiz	In stock at PC - See Note 17
Watsan tablets	DZ	WAT	PRI	03045	200'000	pce	200'000	pce	2-juin-03	Anadarko	PC	200'000	pce	Various sites		0	pce		See Note 18
Tents	DZ	SHE	QA	03055	136	pce	136	pce	29-mai-03	Qatar RC	PC	136	pce			0	pce		Distributed by Protection Civile
Blankets	DZ	SHE	QA	03056	244	pce	244	pce	29-mai-03	Qatar RC	PC	0	pce			244	pce	PC El Hamiz	In stock at Protection Civile
Blankets	DZ	SHE	SI	03012	278	pce	278	pce	31-mai-03	Slovenia RC	PC	0	pce			278	pce	PC El Hamiz	In stock at Protection Civile

Commodity	Commodity Tracking Number				Quantity SENT	Unit	Quantity RECEIVED	Unit	Date Received	Donor	Delivered to	DISTRIBUTED				IN STOCK		Remarks	
												Quantity	Unit	Location (Site)	No. of Beneficiaries	Quantity	Unit		WAREHOUSE
Tents, large (26 pers)	DZ	SHE	SI	03013	3	pce	3	pce	31-mai-03	Slovenia RC	PC					pce		See Note 19	
Tents	DZ	SHE	TR	03009	100	pce	100	pce	23-mai-03	Turkey RC	PC	100	pce			0	pce	Distributed by Protection Civile	
Kitchen Sets	DZ	SHE	YU	03048	200	pce	197	pce	?	Serbian RC	ARC	0	pce			197	pce	Diar Essaada	3 sets damaged on arrival
Bed covers	DZ	SHE	YU	03049	?	pce	1'100	pce	?	Serbian RC	ARC	0	pce			1'100	pce	Diar Essaada	44 boxes x 25 pces
Tents	DZ	SHE	BA	03068	?	pce	75	pce	?	Bahrein RC	ARC	10	pce	Boumerdes and Bejaia		65	pce	Diar Essaada	See Note 20
Generator 1.8 kva	DZ	VEH	BA	03066	24	pce	24	pce	?	Bahrein RC	ARC	0	pce			24	pce	Diar Essaada	
Blankets	DZ	SHE	BA	03065	4'340	pce	4'340	pce	?	Bahrein RC	ARC	0	pce			4'340	pce	Diar Essaada	

- 1.) No precise and up-to-date census is available at the moment. It is estimated one family of 6 people per tent, as an average.
- 2.) Same remark as above.
- 3.) Swiss RC representatives handled initial reception/entry of the goods in Algeria. ARC recuperated 1,327 sets left by the Swiss at the hippodrome in Boumerdes (out of which 12 had been damaged and were later given to ARC volunteers). 1,315 sets were distributed bc ARC on 10 sites in Zemmouri on 3 July 03. It is assumed that 637 sets would have been distributed by the Swiss RC on various sites around Zemmouri.
- 4.) The ship is still in quarantaine in the harbour.
- 5.) ERU was set up on Reghaia site until 24 June 03. After closure, some equipment was stored in Diar Essaada WH (see list attached) and the rest was taken back to Spain.
- 6.) Sanitation Kits: Distribution on various sites: 1 in Zemmouri, 1 in Thenia, 1 in Bordj-Menael, 1 in Dellys, 1 in Zemmouri-stade, 1 in Issers, 3 in Tizi Ouzou, 6 in Boumerdes, 1 in Ghardaia.
- 7.) Received 185 boxes of 2,500 tabs x 100mg = 46,250mg, and 100 boxes of 1,000 tabs x 500mg = 50,000gr (total 96,250gr). So far, 22,500gr were distributed/used (23%).
- 8.) One Rubbhall was taken by Spanish ERU and later sent to Diar Essaada WH We still need to confirm that the second Rubbhall was taken/used by the Protection Civile.
- 9.) The cholera kit was handed over to the Ministry of Health (within the National "Crisis Cell"
- 10.) 1,100 tents arrived on 27 May by air, and 380 arrived on 8 June by sea. 983 were installed in Boumerdes, and 117 given to "Crisis Cell" in Algiers
- 11.) The Bill of Lading indicates 300 bales sent (bales contain 30 pces) therefore 9,000 instead of 10,000 were sent. Apparently 6 bales (180 blankets) were missing on arrival at warehouse.
- 12.) PC showed us documents regarding distribution, but we have not had time to list the distribution sites
- 13.) Protection Civile has recorded 423 tents (??)
- 14.) Protection Civile has recorded 2,558 blankets (??)
- 15.) Received 200 with CTN and 200 sets without CTN (ie. Outside Appeal). Total stock is 400 sets
- 16.) Distribution on various sites: 16 kg in Thenia (to volunteers), 2,020 kg in Boumerdes, 1,212 kg in Oran, 646 kg in Zeralda and 646 kg in Bejaia, 460 kg ?
- 17.) Blankets arrived on 2 different flights: 450 on 2 Jun and 450 on 4 Jun.
- 18.) All watsan tablets were given by the Protection Civile to the "Societe Algerienne des Eaux" on 30 June 03. The requisition and handover is well documented.
- 19.) We have not been able yet to confirm with PC the reception / use of these 3 tents.
- 20.) 5 tents were installed in Boumerdes, 5 were used for children in Bejaia summer camp
