

OPERATIONS UPDATE



International Federation of Red Cross and Red Crescent Societies
Fédération internationale des Sociétés de la Croix-Rouge et du Croissant-Rouge
Federación Internacional de Sociedades de la Cruz Roja y de la Media Luna Roja
الاتحاد الدولي لجمعيات الصليب الأحمر والهلال الأحمر

PAKISTAN: EARTHQUAKE

22 February 2006

The Federation's mission is to improve the lives of vulnerable people by mobilizing the power of humanity. It is the world's largest humanitarian organization and its millions of volunteers are active in over 183 countries.

In Brief

Appeal No. 05EA022; Operations Update no. 23; Period covered: 25- 15 February 2006; Appeal coverage: 82.7%; ([click here to go directly to the attached Contributions List, also available on the website](#)).

Appeal history:

- Preliminary Emergency Appeal (launched as South Asia: Earthquake) on 9 October 2005 for CHF 10.8 million (USD 8.4 million or EUR 7 million) for four months to assist 30,000 families (some 120,000 beneficiaries).
- Operations Update No. 3 of 12 October 2005 increased the Preliminary Appeal budget to CHF 73,262,000 (USD 56,616,692 or EUR 47,053,307) to assist up to 150,000 families (some 750,000 beneficiaries) for six months, as an increasingly serious situation has unfolded.
- Operations Update No. 5 of 17 October 2005 revised down the number of targeted families to 70,000 (some 500,000 beneficiaries), based on the newly assessed delivery capacity and average family size of seven.
- Revised Emergency Appeal launched on 25 October 2005 for CHF 152 million (USD 117 million or EUR 98 million) to assist 81,000 families (some 570,000 beneficiaries) for six months.
- Disaster Relief Emergency Funds (DREF) allocated: CHF 200,000.

Outstanding needs: To date CHF 125.6 million has been received, of which CHF 71.7 million is in cash and CHF 53.9 million is in-kind contributions. Additional pledges – especially in cash – are still needed to fully cover the operational costs.

Related Emergency or Annual Appeals: [South Asia Regional Annual Appeal 05AA051](#)

Operational Summary:

Over the past few weeks, there have been a number of interruptions to the relief operation's distribution plan. These include road closures caused by landslides and avalanches, stoppages due to the observance of religious events and security concerns arising from protests at newspaper depictions relating to the Islamic faith. Despite ongoing challenges, however, more than 90,000 families have received relief assistance through the Federation and Pakistan Red Crescent Society (PRCS) operations. Since winter is not over, distributions will continue to be made to the most vulnerable for the coming few weeks. PRCS teams are being trained in monitoring and assessing beneficiaries, and will maintain contact with these vulnerable groups to obtain early indications of any unforeseen needs. Beneficiary families will also continue to receive materials and shelter repair kits to rebuild their homes.

Distributions continue as the situation permits, and the usual methods of delivery have been reinforced by the use of Norwegian Red Cross all-terrain vehicles (ATVs). The team of ATVs is able to deliver to small, remote communities that remain inaccessible through the usual means of delivery. Staff and volunteers of the Pakistan Red Crescent Society (PRCS) in particular remain the backbone of this operation, together with Federation delegates and members of the regional disaster response teams (RDRTs). Steps are also underway to manage the effective handover or prolongation of the basic health care and water and sanitation Emergency Response Units (ERUs). Concurrent with the relief operation is the integrated planning for recovery, in concert with the PRCS, to ensure a seamless transition from relief to recovery.

For further information specifically related to this operation please contact:

- In Islamabad: Khalid Kibriya (Secretary-General), Pakistan Red Crescent Society; email: hilal@isb.comsats.net.pk,

Phone: +92.51.925.0404; Fax: +92.51.925.0408

- In Islamabad: Azmat Ulla (Head of Delegation); email: azmat.ulla@ifrc.org; Phone: +92.300.850.3317; Fax: +92.51.443.0745; Mohammed Omer Mukhier (Head of Operations); email: mohammedomer.mukhier@ifrc.org; Mobile: +92.301.5321.8711;
- In Geneva: Jagan Chapagain (South Asia Regional Officer), email: jagan.chapagain@ifrc.org; Phone: +41.22.730.4316; Fax: +41.22.733.0395; Christine South (Pakistan Desk Officer); email: christine.south@ifrc.org; Phone: +41.22.730.4529;

All International Federation assistance seeks to adhere to the [Code of Conduct for the International Red Cross and Red Crescent Movement and Non-Governmental Organizations \(NGOs\) in Disaster Relief](#) and is committed to the [Humanitarian Charter and Minimum Standards in Disaster Response](#) in delivering assistance to the most vulnerable. For support to or for further information concerning Federation programmes or operations in this or other countries, or for a full description of the national society profile, please access the Federation's website at <http://www.ifrc.org>

Background

An earthquake with a magnitude of 7.6 on the Richter scale, centred 95 km northeast of Pakistan's capital, Islamabad, struck at 08:50 local time (03:50 GMT) on 8 October 2005, with tremors felt across the region from Kabul to Delhi. The quake has decimated northern Pakistan and northern India. In Pakistan alone, enormous numbers of people have been killed and injured. More than 3.5 million people have been made homeless. The immensity of the disaster is such that it remains one of the deadliest in the region in living memory.

Situation

The reporting period has seen some major challenges to the ongoing relief operation. Although the winter weather in Pakistan has been in general warm for the time of year, there have been a number of landslides and avalanches, which have blocked the distributions. In addition, recent religious celebrations and heightened security awareness, relating to the protests against the publication of cartoons in the European media, has limited delegates' movement and the level of relief distributions.



Distribution of non-food items in Allai Valley.

Parallel to meeting the needs of the vulnerable, the security of all staff involved in the Federation operation is of paramount importance. To date, there have been no untoward incidents directed against Red Cross Red Crescent staff; therefore there has been no need to limit operations for any extended period. However, as a precautionary step, travel in certain areas has and may continue to be restricted and all unnecessary travel is curtailed, dependent on daily reviews of security. Evaluation of the security situation is an ongoing process, with regular consultation with the military, police, the United Nations (UN) agencies, non-governmental organizations (NGOs) and community leaders to ascertain the appropriate steps.

Operational developments

Ongoing relief operations are reaching more and more vulnerable families, with the total numbers exceeding the appeal target of 81,000 (more than 90,000 families to date). Since winter is far from over, plans to refocus on the

most vulnerable are being developed, particularly those affected by the recent interruptions to the distribution plan. In anticipation of future needs, some planning has gone into assisting families who will be vacating camps to return to their former communities to rebuild homes and plant crops. Teams from the PRCS are being trained in monitoring and assessing beneficiaries, and will maintain contact with these vulnerable groups to obtain early indications of any unforeseen needs. Beneficiary families are also continuing to rebuild their homes, most of them in accordance with specifications for earthquake resistant structures, and the Federation / PRCS are working in cooperation with the Government of Pakistan and other agencies to provide corrugated galvanised iron (CGI) sheeting and shelter repair kits to support them in this.

In the meantime, the transfer of a Spanish health emergency response unit (ERU) to the PRCS has proceeded as planned and, alongside the mobile health clinics working with the water and sanitation teams, continues to provide valuable basic health care for the local community. The transfer of the ERU will also contribute to the capacity building of the national society.

The Federation is entering a new phase in the emergency operation. Although there will continue to be monitoring of the status and needs of a number of the remote mountain communities, the full-scale operation will begin to scale down the relief phase as the operation moves forward with the recovery planning. However, the operation, it will still remain essentially a relief operation until the peak of the winter is over. Owing to the changing nature of the operation, the reporting frequency of the operations update will now be reduced to once per month and it is foreseen that during the recovery phase, reporting will further reduce to a quarterly basis. There will be a consolidated report at the six month point.

Cooperation

To enhance consultation and cooperation, the Federation delegation recently engaged a liaison delegate for interagency coordination. Interagency coordination is growing in importance, as the transition from relief to recovery moves forward and the nature of the operation evolves over the coming months. The liaison delegate will play a key role in representing the Federation and PRCS at various meetings on behalf of the operations, the recovery team, the movement coordinator and the head of delegation. In addition, certain members of staff in Mansehra, together with their PRCS counterparts, will continue to participate in various cluster meetings and the joint recovery planning group at field level. The meetings have recently focused on identifying gaps and opportunities that can be filled by UN agencies, NGOs and the Red Cross Red Crescent Movement.

Red Cross and Red Crescent action - objectives, progress, impact

1. Emergency relief (food and non-food)

Objective: the basic shelter and household needs of 81,000 earthquake-affected families (approximately 570,000 people) in northern Pakistan are met over the next six months, enabling them to start rebuilding their future.

Progress/Achievements

As of 15 February, the Federation and PRCS relief teams have distributed non-food relief items to 91,485 beneficiary families - 10,485 families above the appeal target.

During the reporting period, the Federation and PRCS relief team have also continued to distribute corrugated galvanized iron (CGI) sheets and shelter repair kits (SRK) to families seeking to rebuild their homes. Each beneficiary family receives a standard package of ten CGI sheets and a shelter repair kit, comprising a hammer, a saw, a hand axe, a pick axe, a spade, a crowbar and nails, all packed in a canvas tool bag. In addition, a roll of metal wire and a bucket is part of the tool kit. Most families have already constructed wooden frames, which required ten CGI sheets to complete the frame structure. Unfortunately, the provider of shelter repair kits has not been able to keep up with the delivery of CGI sheets, creating a slight delay in the planned distribution. Nevertheless an increase in the daily provision of shelter repair kits is foreseen from mid-February onwards.



Relief distributions like this one help families survive the difficult times that follow a disaster.

The Norwegian Red Cross all-terrain vehicles and belt wagons have begun carrying relief items, including the CGI packages, to high-lying, remote mountain communities in Satbani and Balakot sub district. So far, the team, comprising 16 vehicles and a corresponding number of Norwegian rescue team members/drivers, has been able to provide relief items to 80 families daily using the Balakot Rubb Hall as a base for loading. Unfortunately the work of the Norwegian Red Cross volunteers has also been affected by the recent security situation, but the remaining team is continuing to assist with planned distributions.

A Rubb Hall warehouse has also been erected in Maira camp, close to Besham, to replace warehouse space in the basement of a hotel. The Rubb Hall was erected with assistance of four Norwegian rescue team members.

Four PRCS volunteers participated in the four-day, interagency “Rapid Needs Assessment of Service Delivery in Spontaneous Camps”. In addition, The Federation/PRCS placed a vehicle and a global positioning system (GPS) at the disposal of the team members.

As mentioned above, the Federation is working closely with PRCS to consolidate and then scale down its relief operation with a view to moving towards a new recovery phase. The Federation recently engaged a new relief administrator based in Mansehra, who will work with the relief and logistics coordinators to ensure effective distribution of relief items during the remaining relief period and will support the recovery coordinator in terms of any further relief needs that arise during the remainder of 2006. The relief administrator will also help with the crafting of a final report on the emergency operation for distribution to donors.

Federation relief distributions as of 18 February 2006

Location	No. of families	Tents	Blankets	Tarpaulins	S. Bags	Quilts	Jerry Cans	Kitchen Sets	Stoves
Shumlai	2,000	0	0	0	0	0	0	2,000	0
Battal/Chattar/Hill kot	8,983	710	4,854	16,850	24	31,372	7,889	7,841	199
Allai	7,227	581	36,715	13,110	306	16,963	6,278	6,094	3,043
Garhi Habibullah	15,929	13,559	86,418	18,242	2,429	38,687	4,965	6,228	3,986
Balakot	21,727	9,513	69,632	16,240	5,224	25,336	8,113	5,336	4,062
Batagram /Battal	11,504	8,921	65,854	12,094	2,981	30,044	1,111	3,360	2,940
Siran Valley	11,136	9,650	56,806	11,757	2,124	53,381	4,475	7,512	7,101
Kohistan	12,979	12,233	74,750	24,046	277	40,891	19,734	12,053	8,538
TOTAL	91,485	55,167	395,029	112,339	13,365	236,674	52,565	50,424	29,869

	Hygiene Kits	B. Sheets	Lamps	Buckets	Shawls	CGI Sheets	Shelter Repair Kits
Shumlai	0	14,080	0	0	0	0	0
Battal/Chattar/ Hill kot	8,041	1,414	7,841	0	600	2,290	229
Allai	5,709	0	0	0	4,860	0	0
Garhi Habibullah	5,849	16,288	2,657	0	2,069	11,280	1,128
Balakot Air/Land	8,218	12,017	7,084	1,354	2,485	9,690	969
Batagram/Battal	3,916	9,107	193	0	3,087	5,852	574
Siran Valley	9,153	46,727	4,383	0	11,105	15,171	1,509
Kohistan	11,418	1,000	8,134	0	3,706	0	0
TOTAL	52,304	100,633	30,292	1,354	27,912	44,283	4,409

2. Emergency health and care

Objective: Some 250,000 earthquake-affected people in northern Pakistan have access to appropriate quality health care, safe water and sanitation services in the next six months.

Progress/Achievements

Health activities continue providing health and care services to the affected population. The Federation, along with the PRCS and Red Cross Red Crescent partners have seen 202,866 patients to date in this operation.

The health situation remains stable this week, with no reported outbreaks of major diseases in the districts. The state of the weather and roads has been conducive to the operations, with only some small interruptions due to the precautions taken with regard to planned demonstrations. No direct security threats have been experienced.

The Ministry of Health (MOH) is finalizing its health strategy for the next six months, with the support of the United Nations and other organizations. Three organizations (Afghanistan Medical Relief Team, Abbasin Foundation and Life Care) requested assistance in providing drugs. Emergency health kits will be delivered to the organizations after verification.

In Abbotabad, the Ayub Medical Centre (AMC) is operating at less than 10 per cent of its capacity, as the number of in-patients has greatly reduced compared to those treated immediately after the earthquake. Further discussions will continue regarding the proper hand-over of the Norwegian Red Cross donated field hospital, including the appropriate use of the materials and other items. An action plan for the hand-over decisions has been made and future plans drawn up. A full inventory of the pharmacy, Rubb Hall, tents and all equipment associated with the hospital has also been drafted. These lists have been sent to the PRCS, ERUs/mobile clinics and other Federation/partner national society hospitals to see if they can be well used. The remaining stock will be packed, sealed and handed over to Aide Medicale Internationale (AMI), including parts of the unit that will be prepared for any future emergency responses.

A study has also been carried out to understand patients' perception of the Abbottabad field hospital, with 34 patients interviewed (the collected data has not yet been analyzed). Since it became functional, the hospital has admitted 273 patients and 205 operations have been performed. Up to 2,483 patients have received psychotherapy and 3,395 have received physiotherapy. The average bed occupancy rate throughout the operation has been approximately 70 per cent.

The two mobile health teams in Besham continue to provide good support in and around the areas. The two teams now include eight health professionals and two drivers. They are working in difficult mountainous terrain and providing much needed services to remote communities. In recent weeks there has been an increase in attendance at these mobile clinics. Most of the patients treated by the mobile teams are suffering from respiratory tract infections and asthma. Health education, using United Nations Children's Fund (UNICEF) posters, continues to be an integral part of the teams' work. In addition to hygiene promotion, lessons concerning the prevention of goitre

have also been included. Follow up was done regarding the use of female hygiene kits, and during home visits, it was found that people, especially children, have been using the soap dispensed the week before.

The chairman, secretary-general, and director of operations of the PRCS and the secretary of the North-West Frontier province (NWFP) visited the Spanish Red Cross ERU team in Balakot. A new team from the Spanish Red Cross arrived to support the process and the ERU handed over its facilities and equipment to the PRCS. To date, the Spanish Red Cross ERU has provided medical care to 7,115 patients. Local staff members will be employed to maintain the running of the facility.

At the French Red Cross ERU in Batagram, the previous team leader has left, however, the remaining French Red Cross staff is planning to stay on in Batagram for the coming months. The ERU team is operating two mobile teams that are supporting six different basic health units (BHUs) in the area of Batagram. The ERU team also visited Maidan camp on request of the World Health Organization (WHO) and the Ministry of Health and discussions were held with different actors working in the camp (e.g. Relief International) to establish a possibility for French Red Cross action. The work of the French Red Cross health team will continue after the ERU phase for the coming few months, and further assessments will be made to assess other needs in the area, access permitting. The ERU team is also engaged in the training of 12 health staff, covering topics such as immunization and mother and child health care. Further training will be provided in other agreed topics. Since the French ERU and its mobile teams became operational, the unit has treated 12,162 patients.

The Qatar Red Crescent (QRCS) basic health unit in Bagh (Dholi) is serving a population of 25,000 people, treating 250 – 300 patients daily. The unit has an inpatient turnover rate of two to three patients daily in their 20-bed inpatient service and QRCS is working to expand the BHU to 30 beds because of the demand for services. The BHU also has early psychological intervention (EPI) services and staff is planning to begin mobile health services. Extra staff for this mobile clinic service will arrive soon. QRCS is now looking for support to purchase a new vehicle for this service. Since becoming functional on 20 November 2005, the BHU has treated 14,818 patients.

The Turkish Red Crescent in Muzaffarabad has treated 35,548 patients, of which 385 surgeries have been performed and 561 patients have been admitted. Some 3,560 patients have also been treated by the TRCS's mobile health team.

Red Cross Red Crescent health figures as of 14 February 2006

Health units	Locations	Beneficiaries
PRCS mobile health unit	Pakistan administered Kashmir (various locations)	47,004
PRCS mobile health unit	NWFP (including Balakot, Garhi Habibullah)	7,187
PRCS/Korean Red Cross mobile health	NWFP (including Mansehra base camp, Besham)	4,382
Spanish Red Cross ERU	Balakot	7,115
French Red Cross ERU	Banna Alai, Batagram, Bateela, Pachtu, Rashang	12,162
RDRT/ Malaysian Red Crescent medical team	Mansehra base camp and Mang/Mountains	1,182
Federation multinational field hospital	Abbottabad	14,558
Italian Red Cross field hospital	Mansehra	686
Qatar Red Crescent	Bagh (Dholi)	14,818
Saudi Red Crescent field hospital	Mansehra	58,224
Turkish Red Crescent Society*	Muzaffarabad	35,548
TOTAL		202,866

Water and Sanitation:

Water and sanitation activities continue serving communities in Balakot and Batagram, and are expanding operations to Gari Habibullah. These activities are now focusing more on the transition to the recovery phase.

In Balakot, the Austrian/Swedish team continues to purify 150,000 litres of water for 15,000 beneficiaries each day. While in Batagram, the German/Austrian team is still producing 40,000 litres of purified water daily for 10,000 beneficiaries.

Water and sanitation teams are aiming to build 50 latrines per week. They finished 43 latrines in or around Batagram this past week, taking the total number of latrines in the area to 179. The total number of latrines built in the Balakot areas is also 179. The teams are now also starting to build bathing facilities and 29 bathing facilities have been built in Batagram so far. They will also build 18 water reservoirs (water tanks), of which ten are new and eight are old ones that will be recycled. The hygiene team is distributing one hygiene kit per family, serving 5,131 families (35,917 beneficiaries), with 3,200 kits distributed in Balakot and 1,931 in Batagram respectively.

Water and sanitation figures as of 6 February 2006

LOCATION	Beneficiaries	Water in litres (purified on daily basis)	No. of latrines	No. of bathing facilities	No. of hygiene kits distributed
Balakot	15,000	150,000	179	-	3,200
Batagram	10,000	40,000	179	29	1,931
Maira Camp	5,000	16,000	5	-	-
TOTAL	30,000	206,000	363	29	5,131

The main challenge for the Federation and PRCS is to continue motivating PRCS volunteers, who have been working hard since the emergency phase and to provide them with appropriate direction and support through the setting up of a water and sanitation department at provincial and national level.

Psycho-social programme (PSP):

In late January, Rozan (a national NGO) carried out supervision in all four locations where the Red Cross Red Crescent is working (Islamabad, Batagram/Besham, Abbotabad/ Balakot and Gari Habibullah). During the supervision, there were a number of psycho-education sessions with teachers and other professional groups. A final work plan for these activities will be worked out with Rozan by the end of February. A variety psycho-education material has also been developed and will be ready for distribution in the coming weeks.

The second phase of the training for PRCS field workers has been completed, providing psycho-education sessions and support for different groups of volunteers. Additional topics, such as looking at possible community mobilization tools were also addressed. All 16 field workers participated in the training and are committed to continue with this work. A system of surveillance forms has been developed, and statistics on activities, numbers and age groups of beneficiaries reached are being compiled.

Items like sewing machines, wool and knitting pins, kits with indoor and outdoor toys for children at different age groups, sports equipment, craft items and tools for different vocational training activities, have been purchased and delivered to different camps. Incentives for volunteers, such as hats, shawls, bags and torches, have been bought and will be delivered in the coming weeks with programme logos attached. Special “well-being” kits with underwear, shawls, washing powder, hair shampoo, body lotion, hair brush, combs, hair clips, mirrors etc. have been ordered and will be distributed broadly to beneficiaries to complement the ordinary hygiene kits. Possibilities of organizing a big distribution of shoes, fleece jackets, recovery kits and other useful items with the tools to support the rehabilitation phase in the communities have been discussed with the regional representative of the Danish Red Cross.



Children, who are among the target beneficiaries of the Federation operations, crowd around to pose with PRCS volunteers.

In all four camps, a large variety of activities have started and volunteers have been instructed on the management of these various psycho-social support activities. The PRCS field workers have created a large and stable network both in and around the camps, which make it possible to advise and refer beneficiaries to different services. In the coming weeks, the training of volunteers will be further strengthened and activities will be institutionalized in such a way that the volunteers will be able to run the activities by themselves, with frequent support and guidance from the PRCS staff.

A new section on the training of relief staff, carried out by Qatar Red Crescent in Bagh and Muzaffarabad has been proposed and discussed with the Muzaffarabad branch of PRCS and the Federation coordinator. A final programme will be developed shortly.

Furthermore, it has been decided that brochures developed by Turkish Red Crescent on stress management and traumatic stress reactions for adults and for children will be reprinted with programme logos and used as awareness/information tools in the PRCS and Danish Red Cross PSP programme. In the meantime, psychologists in Muzaffarabad working for TRCS have started three courses on vocational training in the last week.

A baseline study has been prepared in order to measure the impact of PSP activities in future. A draft to extend PSP activities for 12 months has been prepared and will be send to ECHO shortly.

3. Logistics/IT/Telecommunications

Overall Objective: The ongoing PRCS and Federation relief operation have effective logistical, IT and telecommunication infrastructure in the operational areas.

Progress/Achievements

IT/Telecommunications:

The Federation is in the process of migrating to a different email system. The IT department has been busy with account creation, user training and post office transfers in the past two weeks. There have been some delays with security clearance; nevertheless, standard daily support activities are taking place for the networks and delegate systems.

The programming of the HF radios continued. The IT department is also conducting coverage tests with the radio room in Mansehra in order to have better information about the actual operational range of the HF network. The radio room is issuing daily weather and road reports and, in coordination with the security delegate, they are also in charge of sending security-related reports. The VHF handheld radios have been handed out to the warehouse and fleet teams in Mansehra to improve communication and coordination during daily operations.

Logistics:

The operation is now becoming longer-term and the emergency phase is scaling down. This reduction in the relief operation will also mean a slow down of the logistics activities in the coming weeks. The logistics team is already looking for a longer-term plan and setup. It is presently working on closing down the main warehouse in Islamabad and finding a bigger warehousing space in Mansehra.

The two snow mobiles, four belt wagons and 12 all-terrain vehicles have been insured and performed their first distribution on February 6. Six new heavy vehicle drivers have also been hired for these new vehicles. However, in the longer-term the Federation will be reducing the number of vehicles in use in response to the scale down of the relief operation.

The Federation has not renewed the lease on the helicopter, due to a change in needs and a disagreement with the leasing company over some of their terms. From next week, the Federation will be using the air options of International Committee of the Red Cross (ICRC) and United Nations Humanitarian Air Service (UNHAS), who are able to provide larger tonnage helicopters to transport the CGI sheeting and repair kits now being distributed. Contracts for this support have been submitted to UNHAS and the ICRC.

The Federation received relief goods from a total of 198 aircrafts from various countries. It has sent 2,187 trucks of relief goods to the affected areas since the beginning of the operation.

4. Communication – Advocacy and Public Information

Objective: The needs of the earthquake-affected population in Pakistan are advocated for and the Red Cross and Red Crescent’s interventions profiled through national and international media coverage.

Progress/Achievements

A BBC crew visited Pakistan during the second half of January. They were provided with briefings, a power point presentation, photographs, and suggested Red Cross Red Crescent story angles. They were also provided with contact names and numbers for the ICRC and Turkish Red Crescent colleagues in Muzaffarabad/Kashmir region. Both teams were interviewed accordingly.

The information delegate is in constant contact with the national media, the UN, NGOs, and IRIN news. All were provided with new Red Cross Red Crescent photographs after the partnership meeting in January.

An article on PSP activities has been prepared and after input from the Federation, Danish Red Cross and Qatar Red Crescent teams, will be sent to Geneva to be published on both the Federation website and the Red Cross Red Crescent magazine as agreed with the media department in Geneva.

The ATV trials have also been closely followed up by the Norwegian Red Cross headquarters and the operations team in Pakistan. A press release on the ATVs and their contribution to the operation has been sent out and an information pack will be available shortly. The pack will include; a press release, a video footage for a VNR, and photographs of ATV’s in action.

Outstanding Needs

- Response to the appeal has been steady; however, there is still a need for cash to fully cover operational costs. Donors are urged to continue to support the appeal, to enable the Red Cross and Red Crescent to remain flexible to changing needs during the transition phase.
- The following longer-term positions need to be recruited internationally and regionally: recovery coordinator, finance delegate, hygiene promotion delegate, and logistics coordinator.

[Contributions list below; click here to return to the title page.](#)

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

21/02/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
-------	----------	----------	------	-----------	------	---------

CASH

REQUESTED IN APPEAL CHF ----->				152,033,929	TOTAL COVERAGE 82.7%	
AMERICAN - RC		850,000	USD	1,099,900	17.10.05	
AMERICAN - RC		1,000,000	USD	1,280,500	01.11.05	
AMERICAN - RC		362,100	USD	475,075	08.12.05	HELICOPTER OPERATIONS ONE MONTH
AMERICAN - RC		1,500,000	USD	1,968,000	29.12.05	CORRUGATED IRON SHEETS
AMERICAN - RC		1,500,000	usd	1,968,000	30.01.06	
AUSTRALIAN - GOVT		3,000,000	AUD	2,956,500	10.10.05	TENTS, BLANKETS, TARPULINS, KITCHEN SETS, AIRFREIGHT
AUSTRALIAN - RC		500,000	AUD	480,500	19.10.05	MEDICAL SUPPLIES, VACCINES, CHOLERA KITS
AUSTRALIAN - RC		500,000	AUD	480,500	25.10.05	NEW EMERGENCY HEALTH KITS
AUSTRALIAN - RC				300,000	15.11.05	56 NEW EMERGENCY HEALTH KITS
AUSTRIAN - RC		50,000	EUR	77,825	03.01.06	
AUTONOMOUS PROV. BOLSANO		50,000	EUR	77,825	08.01.06	
BARBADOS - RC		1,015	USD	1,305	07.02.06	
BRITISH - RC		250,000	GBP	569,500	09.10.05	
BRITISH - GOVT/DIFD		1,470,588	GBP	3,344,117	27.10.05	
BRITISH - RC		250,000	GBP	568,500	17.11.05	
BRITISH - GOVT/DEC		214,663	GBP	488,143	18.11.05	PROCUREMENT OF STOVES
BRITISH - GOVT/DEC		1,331,250	GBP	3,027,263	18.11.05	PROCUREMENT OF HYGIENE KITS
BRITISH - GOVT/DEC		692,250	GBP	1,574,176	18.11.05	PROCUREMENT OF SHELTER KITS
BRITISH - RC		500,000	GBP	1,129,500	20.12.05	CORRUGATED IRON
BRITISH - RC		490,197	GBP	1,114,732	06.02.06	
BRITISH - PRIVATE DONOR		405	GBP	918	05.01.06	
BRITISH - PRIVATE DONORS				15,857	03.11.05	
BRITISH PETROLEUM		500,000	USD	647,000	11.10.05	
BRITISH PETROLEUM FOUNDATION		75,726	USD	99,353	22.12.05	
CAMBODIAN - RC		15,000	USD	19,410	13.10.05	
CAMBODIAN - PRIVATE DONOR		100	USD	131	01.11.05	
CANADIAN - GOVT/CIDA/HAPS		990,000	CAD	1,093,455	13.10.05	
CANADIAN - GOVT/CIDA/HAPS		99,000	CAD	109,346	18.10.05	
CANADIAN - RC		1,000,000	CAD	1,088,200	19.10.05	PROCUREMENT 1300 WINTERISED TENTS
CANADIAN - RC		1,000,000	CAD	1,088,200	02.11.05	
CANADIAN - GOVT CIDA/HAPS		990,000	CAD	1,077,318	09.11.05	
CANADIAN - RC		750,000	USD	984,000	09.12.05	HELICOPTER OPERATIONS 2 MONTHS
CHINA - HONG KONG RC BRANCH		500,000	HKD	83,100	10.10.05	PROCUREMENT SHELTER KITS
CHINA - HONG KONG RC BRANCH		4,000,000	HKD	679,600	29.11.05	

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

21/02/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
CHINA - HONG KONG RC BRANCH		2,000,000	HKD	330,600	23.12.05	PURCHASE OF WINTERISED TENTS
CHINA - MACAU - RC BRANCH				25,000	10.10.05	PURCHASE OF MEDICINES, BLANKETS & TENTS
CHINA - MACAU - RC BRANCH				15,000	09.12.05	PURCHASE OF MEDICINES
CROATIAN - RC		20,000	EUR	30,950	30.11.05	
CYPRUS - RC				20,867	12.10.05	
CZECH - RC		10,000	USD	12,940	25.10.05	
DANISH - RC				95,920	14.10.05	
DANISH - GOVT through RC				492,769	20.10.05	
DANISH - GOVT through RC				294,069	16.11.05	
DANISH - GOVT through RC				196,842	28.11.05	
DANISH - PRIVATE DONORS				4,783	03.02.06	
ECHO (05004)		810,747	EUR	1,262,333	13.10.05	
ECUADORIAN - RC		5,702	USD	7,481	25.01.06	
FINNISH - PRIVATE DONORS		700	EUR	1,083	12.10.05	
FRENCH - RC		400,000	EUR	618,200	07.11.05	
FRENCH - PRIVATE DONORS				1,952	21.10.05	
GERMAN - RC		500,000	EUR	778,500	27.10.05	
GERMAN - RC		500,000	EUR	772,750	21.11.05	PURCHASE WINTERISED TENTS
GERMAN - PRIVATE DONORS				148	18.10.05	
HELLENIC - RC				50,000	11.10.05	PURCHASE 10'000 BLANKETS
ICELANDIC - GOVT		75,000	USD	97,050	09.10.05	
ICELANDIC - RC		17,000,000	ISK	357,000	14.11.05	
INDONESIA - PRIVATE DONOR				128	28.10.05	
IRISH - GOVT		300,000	EUR	467,100	13.10.05	
IRISH - GOVT		350,000	EUR	540,925	28.10.05	
IRISH - RC		100,000	EUR	154,550	16.11.05	
IRISH - RC		500,000	EUR	772,750	25.11.05	PROCUREMENT OF HYGIENE KITS
IRISH - RC		350,000	EUR	541,625	13.12.05	PURCHASE WINTERISED TENTS
IRISH - RC		400,000	EUR	622,600	13.12.05	
IRISH - PRIVATE DONOR				1,035	17.01.06	
ITALIAN - GOVT		200,000	EUR	311,400	17.10.05	
ITALIAN - RC		150,000	EUR	231,825	10.10.05	+ FOR INDIA, EUR 50'000 (DM , see AA047), FOR RELIEF SUPPLIES
JAPANESE - RC		262,513	USD	339,692	11.10.05	
JAPANESE -RC		2,800,000	USD	3,585,400	25.10.05	PROCUREMENT OF 10000 FAMILY TENTS, 10000 KEROSENE LAMPS, 10000 KEROSENE STOVE, 50000 BLANKETS
JAPANESE - RC		150,000,000	JPY	1,662,000	09.11.05	
JAPANESE - GOVT		2,800,000	USD	3,599,400	15.02.06	PROCUREMENT & DISTRIBUTION OF WINTERIZED TENTS, SHAWLS
KOREA, REPUBLIC - RC		50,000	USD	64,700	10.10.05	
LATVIAN - GOVT		100,000	USD	129,400	13.10.05	
LIBYAN - RC				10,000	10.10.05	
LICHTENSTEIN - PRIVATE DONOR				300,000	28.10.05	
LITHUANIAN - RC				3,567	13.01.06	

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

21/02/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
LUXEMBOURG - GOVT		200,000	EUR	311,400	24.10.05	
LUXEMBOURG - RC		40,000	EUR	61,900	21.12.05	PROCUREMENT OF CORRUGATED IRON SHEETS
MACEDONIA, FYR - RC		3,000	EUR	4,671	28.10.05	
MONACO - RC		30,000	EUR	46,710	17.10.05	
NETHERLANDS - GOVT		160,428	EUR	247,941	13.10.05	
NETHERLANDS - RC		213,904	EUR	330,588	03.11.05	
NETHERLANDS - RC		534,759	EUR	826,471	10.11.05	
NETHERLANDS - RC		855,615	EUR	1,324,064	28.11.05	
NETHERLANDS - RC		213,904	EUR	331,016	19.12.05	
NETHERLANDS - PRIVATE DONORS				825	28.10.05	
NETHERLANDS - PRIVATE DONOR				500	19.12.05	TENTS
NEW ZEALAND - RC		100,000	NZD	89,600	20.10.05	
NEW ZEALAND - GOVT		400,000	NZD	358,400	25.10.05	
NEW ZEALAND - GOVT		250,000	NZD	231,125	28.11.05	
NORTH CYPRUS - M.GOKHAN KODAK		25,000	USD	32,800	31.01.06	
NORWEGIAN - GOVT/RC		10,000,000	NOK	1,975,000	09.11.05	RELIEF ACTIVITIES INCL. CHILDREN & VULNERABLE GROUPS
NORWEGIAN - GOVT/RC		5,500,550	NOK	1,086,359	09.11.05	
NORWEGIAN - RC		1,748,067	NOK	339,125	15.12.05	TSU
OPEC FUND F.INTERNATIONAL DEV.		600,000	USD	768,300	13.10.05	+ INDIA (DM. 05AA047) AND AFGHANISTAN (DM. 05AA045), USD 200'000 EACH FOR RELIEF SUPPLIES
PHILIP MORRIS		30,000	USD	38,415	24.10.05	
PHILIPPINES - RC		10,000	USD	12,805	03.11.05	
POLAND - PRIVATE DONORS				3,235	17.10.05	
PRIVATE DONORS ON LINE				804,873	17.11.05	
PRIVATE DONORS ON LINE				39,341	26.01.06	
PRIVATE DONORS ON LINE				5,072	02.02.06	
SAUDI ARABIA - PRIVATE DONOR		10,344	USD	13,245	16.11.05	
SINGAPORE - GOVT & RC				100,000	26.10.05	PROCUREMENT OF RELIEF ITEMS
SINGAPORE - GOVT & RC				100,000	09.11.05	PROCUREMENT EMERGENCY RELIEF & MEDICAL
SINGAPORE - PRIVATE DONOR		50,000	EUR	77,850	11.10.05	
SLOVENIAN - GOVT		14,981	EUR	23,153	17.11.05	
SLOVENIAN - GOVT		27,737	EUR	42,924	07.12.05	
SOUTH AFRICA - PRIVATE DONOR		1,000	USD	1,280	27.10.05	
SPANISH - PRIVATE DONORS				4,467	14.11.05	
SWEDISH - GOVT through RC		2,000,000	SEK	334,000	11.10.05	
SWEDISH - GOVT through RC & RC		15,400,000	SEK	2,571,800	14.10.05	
SWEDISH - RC		25,000,000	SEK	4,050,000	08.11.05	
SWEDISH - RC		20,000,000	SEK	3,250,000	15.12.05	
SWISS - RC				100,000	28.11.05	
SWISS - PRIVATE DONORS				14,850	12.10.05	
SWISS - PRIVATE DONOR				25,000	09.12.05	

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

21/02/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
TAIWAN RED CROSS ORGANISATION		59,000	USD	77,408	05.12.05	PROCUREMENT OF MEDICAL SUPPLIES
TRINIDAD & TOBAGO - RC				3,370	30.12.05	
UNITED ARAB EMIRATES -RC		10,000	USD	12,805	01.11.05	
USA - COCA-COLA		1,000,000	USD	1,294,000	11.10.05	
SWISS WHO/VERF STAFF				4,000	09.11.05	
USA - ADC FOUNDATION		10,000	USD	12,805	31.10.05	
USA - ALTRIA KRAFT		50,000	USD	65,600	15.12.05	
USA - APPLIED MATERIALS		34,684	USD	45,505	15.12.05	
USA - EMC		36,000	USD	47,232	15.12.05	
USA - ENTERPRISE FOUNDATION		250,000	USD	328,000	15.12.05	
USA - HARRIS FOUNDATION		100,000	USD	131,200	15.12.05	
USA - INTEL FOUNDATION		500,000	USD	656,000	15.12.05	
USA - LEHMAN BROTHERS		165,279	USD	216,846	15.12.05	
USA - PRIVATE DONORS				86,289	25.10.05	
USA - PRIVATE DONORS		1,276	USD	1,674	09.12.05	
USA - PRIVATE DONORS		175	USD	225	13.02.06	
USA - SAMYATEX		2,500	USD	3,280	15.12.05	
SUB/TOTAL RECEIVED IN CASH				71,737,427	CHF	47.2%

IN-KIND AND SERVICES

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
in kind list updated					31.1.06	
AMERICAN - RC				5,669,973		30518 BEDSHEETS, 28000 BUCKETS, 70000 BLANKETS, 3000 TARPAULINS, 5000 FAMILY TENTS , 18000 KITCHEN SETS, 3200 WINTERISED FAMILY TENTS, 18000 HYGIENIC PARCELS, 50000 SHAWLS, 2000 TENTS GAMMAX, 152900 BLANKETS QUILTS, SHIPPING/TRANSPORT
AUSTRIAN - RC				2,019,212		21000 HYGIENIC PARCELS, 7 EMERGENCY HEALTH KITS, 300 FAMILY TENTS, 1800 WINTERISED FAMILY TENTS, 76000 BLANKETS, 18000 BLANKETS QUILT, SHIPPING/TRANSPORT
AUSTRIAN - RC				463,650		ERU WATER TREATMENT & SUPPLY LINE, PERSONNEL
BELGIAN - RC/FL				3,251,428		60000 BEDSHEET, 11720 BLANKETS, 95305 BLANKETS QUILT, 20060 JERRYCANS, 2275 WINTERISED FAMILY TENTS, 3500 KITCHEN SETS, 20000 CORRUGATED IRON SHEET, SHIPPING/TRANSPORT
BELGIAN - RC/FR				546,759		12500 BLANKETS, 1250 KITCHEN SETS, 1552 FAMILY TENTS, 1250 TARPAULINS, SHIPPING/ TRANSPORT

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

21/02/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
BRITISH - RC				2,755,426		600 KITCHEN SETS, 6000 WINTERISED FAMILY TENTS, 2000 JERRYCANS 10L., 20060 JERRYCANS 20L., 504000 WATER PURIFICATION TABLETS, 25000 HURRICANE LAMPS, 600 FAMILY TENTS, 41300 TARPULINS 4X6M, 300 TARPULINS 4X60M., 21700 BLANKETS, 50 KITS TAPSTAND & PIPEWORK WAT/SAN
CANADIAN - RC				3,585,575		3000 WINTERISED FAMILY TENTS, 2000 GAMMAX TENTS, 3300 BLANKETS HIGH LOFT, 12000 BLANKETS 80%, 5 EMERGENCY HEALTH KITS, 94 SHEETING TARPULINS, 11000 TARPULINS, TRANSPORT/SHIPPING
DANISH - RC				1,025,320		1.5, BASE CAMP, 30 EMERGENCY HEALTH KITS, 50 DELEGATE HEALTH KITS, 8000 KITCHEN SETS, 9000 TARPULINS, 750 WINTERISED FAMILY TENTS
DANISH - RC				563,850		ERU TELECOM & LOGISTICS UNITS
EGYPTIAN - RC				78,716		2000 BLANKETS, 20 FAMILY TENTS, TRANSPORT/SHIPPING
FINNISH - RC				3,871,778		10000 KEROSENE STOVES, 5500 HURRICANE LAMPS, 6607 WINTERISED FAMILY TENTS, 10000 CORRUGATED IRON SHEET , TRANSPORT/SHIPPING
FRENCH - RC				582,247		4791 KITCHEN SETS, 20910 JERRYCANS, 1440 HURRICANE LAMPS, 15000 SHAWLS, 2300 TARPULINS, TRANSPORT/SHIPPING
FRENCH - RC				261,791		ERU BASIC HEALTH CARE UNIT (ECHO FUNDED)
GERMAN - RC				787,278		ERU SPECIALISED WATSAN MODULE (ECHO FUNDED)
GERMAN - RC				5,906,761		10000 SLEEPING BAGS, 30000 TARPULINS, 10000 HURRICANE LAMPS, 10000 BLANKETS, 8000 WINTERISED FAMILY TENTS, 200 HOSPITAL BEDS, 1 MOBILE KITCHEN, TRANSPORT/SHIPPING
IRISH - RC				936,500		7300 BLANKETS, 2250 WINTERISED FAMILY TENTS
LUXEMBURG - RC				215,594		6000 BLANKETS, 10 EMERGENCY HEALTH KITS,
NEPAL - RC				5,000		1000 BLANKETS
NETHERLANDS - RC				4,757,846		573 FAMILY TENTS, 27 EMERGENCY HEALTH KITS, 20000 TARPULINS, 51516 BLANKETS 80 %, 30000 BLANKETS 50%, 7000 KEROSENE HEATERS, 182900 BEDSHEETS, 72000 BLANKETS QUILTS, 45000 HYGIENIC PARCELS, 2427 WINTERISED TENTS, 16000 KITCHEN SETS, 10 SUPPL.UNITS OF NEHK,

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

21/02/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
NORWEGIAN - RC				2,902,452		11320 BLANKETS, 1 DIATHERMY, 2 DOCTORS OFFICE MODULES, 9 HEATERS, 3 CHOLERA KITS, 1 LABORATORY MODULE, VARIOUS MEDICAL ITEMS, 2 PROPAC ECG MONITORS, 7355 SLEEPING BAGS, 95 SURGICAL SUPPLY KITS, 2 MOTHER AND CHILD CARE MODULE, 1620 TARPULINS, 5 TENTS ALFA, 29 TENTS DELTA, 870 TENTS GAMMAX 24M2, 21 TENTS 90M2, 50 FAMILY TENTS 16M2, 8 TENTS WAREHOUSE, 40 TRUCKS M6, 4 WATER PURIFICATION UNITS, 2 WATERTANKS 10M3, 2 WATERTANK 5M3, 1 X-RAY MODULE
NORWEGIAN - RC				730,000		ERU REFERRAL HOSPITAL
QATAR - RC				2,312,371		20000 AMOXYCILLIN, 6158 FAMILY TENTS, 1170 BEDS RIGID FRAME, 6582 BEDSHEETS, 34881 BLANKETS QUILT, 45960 BLANKETS 50%, 2200 BODY BAGS, 700 BUCKETS, 44 GENERATORS, 12569 HYGIENIC PARCELS, 1998 JERRYCANS 10L, 1200 JERRYCANS 20 L., 40 FIRST AID KITS FOR CAR, 1001 KITCHEN SETS, 300 HURRICANE LAMPS, 925 SHAWLS, 92 VARIOUS MEDICINE, DATES, LENTILS, ASSORTED FOOD
SINGAPORE - RC				1,123,621		13900 FOOD RATION MRS, SHIPPING/TRANSPORT
SLOVENIAN - RC				404,690		5 MEDICAL ITEMS VARIOUS, 10000 SLEEPING BAGS
SPANISH - RC				119,225		8125 BLANKETS, 504 SLEEPING BAGS, 2400 TARPULINS, 150 FAMILY TENTS
SPANISH - RC				415,580		1 ERU BASIC HEALTH CARE UNIT (ECHO FUNDED)
SWEDISH - RC				593,220		ERU WAT-SAN, MASS SANITATION MODULE UNIT
SWEDISH - RC				303,442		904 WINTERISED TENTS, 3000 SLEEPING BAGS, TRANSPORT/ SHIPPING
SWISS - RC				2,681,514		4000 AMOXYCILLIN, 40000 BEDSHEETS, 4500 TARPULINS, 200 FAMILY TENTS, 2 EMERGENCY HEALTH KITS, 12500 BLANKETS QUILT, 6140 BLANKETS, 80%, 20000 BLANKETS 50%, 1562 KEROSENE HEATERS, 2500 KITCHEN SETS, 10000 SHAWLS, 18000 CORRUGATED IRON SHEETS, 2000 WINTERISED TENTS, TRANSPORT/SHIPPING
AUSTRALIA	DELEGATES			80,200		
CANADA	DELEGATES			24,600		
DENMARK	DELEGATES			65,800		
FINLAND	DELEGATES			50,600		

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

21/02/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
FINLAND	DELEGATES			50,600		
GERMANY	DELEGATES			8,800		
GREAT BRITAIN	DELEGATES			56,800		
ICELAND	DELEGATES			58,600		
NETHERLANDS	DELEGATES			45,000		
NORWAY	DELEGATES			169,400		
SWEDEN	DELEGATES			37,200		
SWISS RC	DELEGATES			100,600		
VARIOUS DONORS				4,349,377		ESTIMATED INTERNATIONAL TRANSPORT/INSURANCE COSTS (30% OF TOTAL VALUE OF RELIEF ITEMS)
SUB/TOTAL RECEIVED IN KIND/SERVICES				53,968,396	CHF	35.5%


ADDITIONAL TO APPEAL BUDGET

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
SUB/TOTAL RECEIVED				0	CHF	



Pakistan: Earthquake

Situation map
 Issued 17 February 2006

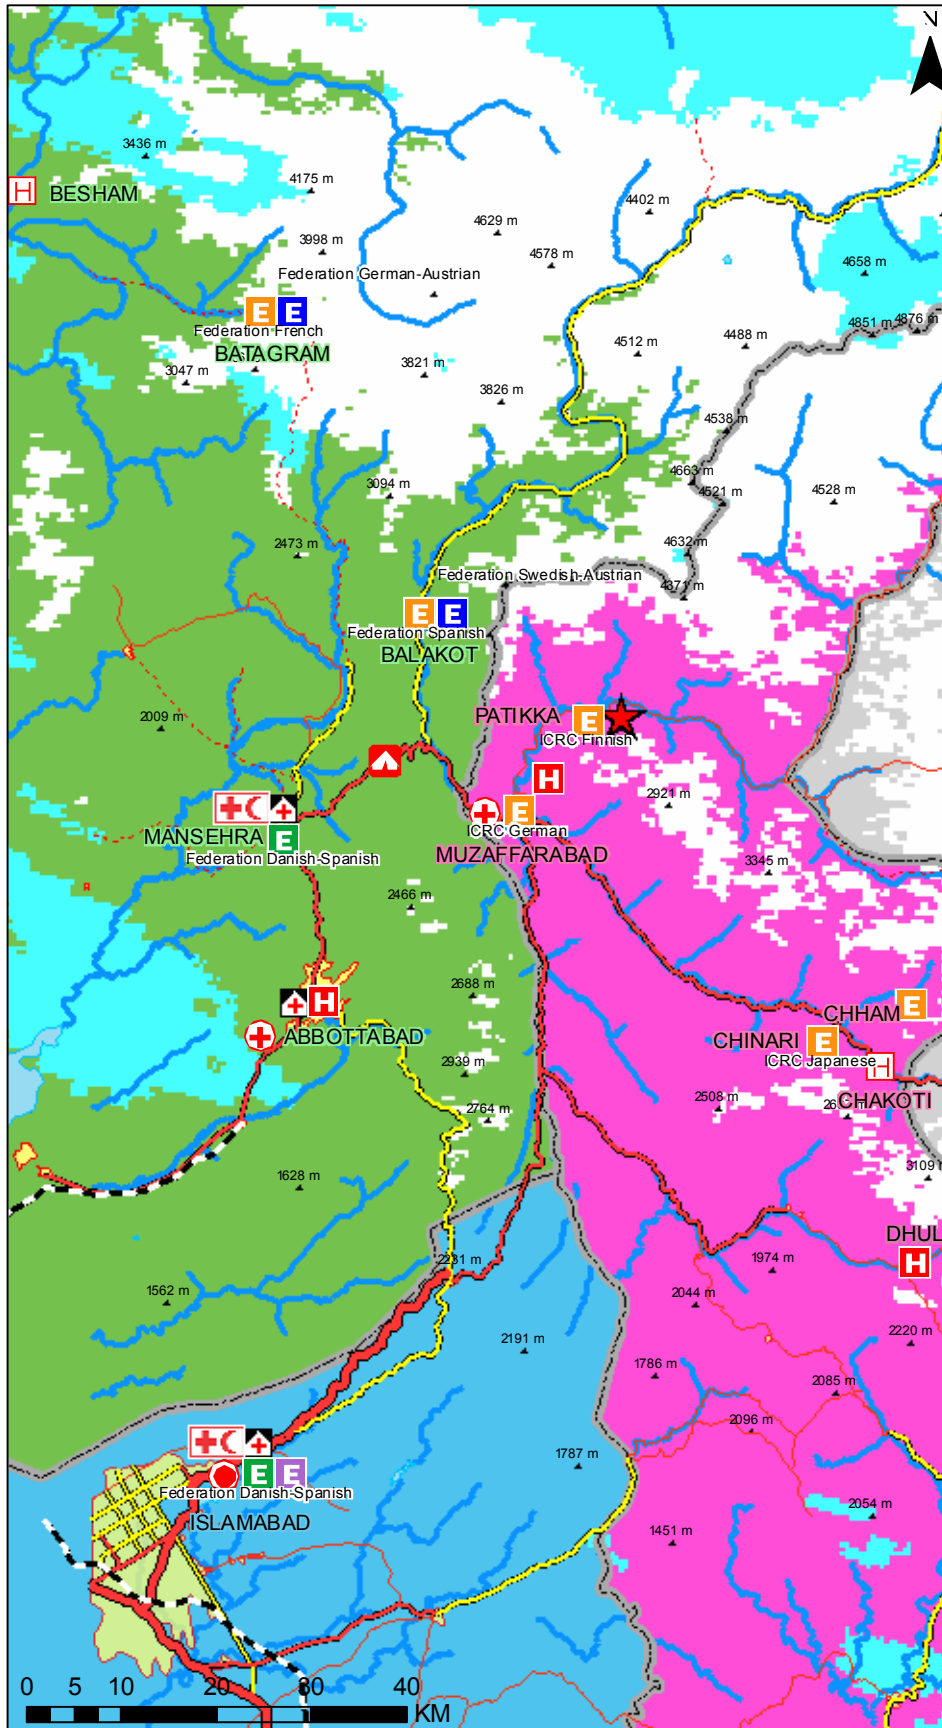

- Earthquake epicenter
 - Federation delegation or hub
 - Federation base camp (provided by Danish RC)
 - Federation and/or ICRC logistics center
 - ICRC delegation
 - ICRC sub-delegation
 - Hospital
 - PRCS and/or Federation Basic Health Unit (BHU)
- Emergency Response Unit (ERU)**
- Basic Health Care (BHC)
 - IT/Telecom
 - Logistics
 - Water & Sanitation (WATSAN)
- Administrative boundaries
- Provinces**
- Indian Jammu & Kashmir
 - North-west Frontier
 - Pakistan-administered Kashmir
 - Punjab
- Railroads
 - Highway, Hard, All weather
 - Main road, Hard, All weather
 - Secondary road, Loose, All weather
 - Local road, Loose, Dry weather
 - Track, Loose, Dry weather

Snow extend (in white) as of February 10, 2006
 Light blue: clouds

The maps used do not imply the expression of any opinion on the part of the International Federation of Red Cross and Red Crescent Societies or National Societies or the ICRC concerning the legal status of a territory or of its authorities.
