

OPERATIONS UPDATE



International Federation of Red Cross and Red Crescent Societies
Fédération Internationale des Sociétés de la Croix-Rouge et du Croissant-Rouge
Federación Internacional de Sociedades de la Cruz Roja y de la Media Luna Roja
الاتحاد الدولي لجمعيات الصليب الأحمر والهلال الأحمر

PAKISTAN: EARTHQUAKE

11 November 2005

The Federation's mission is to improve the lives of vulnerable people by mobilizing the power of humanity. It is the world's largest humanitarian organization and its millions of volunteers are active in over 181 countries.

In Brief

Appeal No. 05EA022; Operations Update no. 12; Period covered: 8-10 November 2005; Appeal coverage: 58.2%; ([click here to go directly to the attached Contributions List, also available on the website](#)).

Appeal history:

- Preliminary Emergency Appeal (launched as South Asia: Earthquake) on 9 October 2005 for CHF 10.8 million (USD 8.4 million or EUR 7 million) for four months to assist 30,000 families (some 120,000 beneficiaries).
- Operations Update No. 3 of 12 October 2005 increased the Preliminary Appeal budget to CHF 73,262,000 (USD 56,616,692 or EUR 47,053,307) to assist up to 150,000 families (some 750,000 beneficiaries) for six months, as an increasingly serious situation has unfolded.
- Operations Update, No. 5, revised down the number of targeted families to 70,000 (some 500,000 beneficiaries) based on the newly assessed delivery capacity and average family size of seven.
- Revised Emergency Appeal launched on 25 October 2005 for CHF 152 million (USD 117 million or EUR 98 million) to assist 81,000 families (some 570,000 beneficiaries) for six months.
- Disaster Relief Emergency Funds (DREF) allocated: CHF 200,000.

Outstanding needs: To date CHF 88.4 million has been received, of which CHF 37.3 is in cash and CHF 51.1 is in kind contributions. More pledges are in the pipeline and will be reflected in the next operations update. Additional pledges – especially in cash – are very urgently needed.

Related Emergency or Annual Appeals: [Pakistan Annual Appeal 05AA049](#), [South Asia Regional Annual Appeal 05AA051](#)

Operational Summary:

Hundreds of thousands of people are still homeless after the 8 October earthquake, and with many mountain roads still blocked by landslides, aid has yet to reach some remote regions of Pakistan. According to United Nations officials, an outbreak of acute diarrhoea affecting hundreds of people in some of the tented camps has raised fears of cholera. Dropping temperatures, coupled with forecasted rain and snow, could pose a real threat of waterborne disease that could potentially lead to a second wave of deaths. A key priority in the coming weeks is to improve sanitation, water supply and health care conditions particularly in the camps.

To combat the outbreak of cholera and other diseases, the Federation's water sanitation emergency response units (ERUs) continue to supply and distribute clean drinking water and establish sanitation facilities to quake survivors. Hygiene promotion will start in combination with the setting up of latrines, in the coming days.

Relief distributions by the Federation and Pakistan Red Crescent Society (PRCS), including special relief missions by helicopter to the remote Kagan Valley, have now reached over 14,000 quake-affected families or some 98,000 beneficiaries. As a result of an assessment by helicopter by the regional disaster response teams (RDRT), a new emergency health kit and paediatric medications have been dispatched to the village of Jared where health problems including scabies and upper respiratory tract infections, especially in children, have been

identified.

More than 30,000 people have been treated by the Federation and PRCs since operations began just over one month ago. In Batagram, the Federation will continue and expand outreach health services that the French ERU has started in areas north of the town. Meanwhile, the Spanish health ERU in Balakot will now refocus its mobile outreach services to destinations further into the Kagan Valley to avoid duplication with other agencies which have recently arrived in the town.

The Federation Secretariat would like to thank all the national societies and governments which have responded to the Pakistan Emergency Appeal to date and encourage donors to continue with their fundraising efforts. These national societies are: Australia Red Cross, Austrian Red Cross, Belgian Red Cross, British Red Cross, Cambodian Red Cross, Canadian Red Cross, the Red Cross Society of China - Hong Kong and Macau Branches, Cyprus Red Cross, Czech Red Cross, Danish Red Cross, Egyptian Red Crescent, Finnish Red Cross, French Red Cross, German Red Cross, Hellenic Red Cross, Icelandic Red Cross, Irish Red Cross, Italian Red Cross, Japanese Red Cross, Republic of Korea Red Cross, Latvian Red Cross, Libyan Red Crescent, Luxemburg Red Cross, Macedonian Red Cross, Monaco Red Cross, Netherlands Red Cross, New Zealand Red Cross, Nepal Red Cross, Norwegian Red Cross, Philippines Red Cross, Qatar Red Crescent, Singapore Red Cross, Spanish Red Cross, Swedish Red Cross and Swiss Red Cross. In addition, contributions have been received from ECHO, the OPEC Fund, and several corporate donors.

For further information specifically related to this operation please contact:

- *In Islamabad: Pakistan Red Crescent, Khalid Kibriya (Secretary General), phone +92 51 9250 404; fax: +92 51 925 0408*
- *In Islamabad: Irja Sandberg (Head of Delegation), email; ifrcpk08@ifrc.org; phone + 92 51 925 0416, fax +92 51 443 0745; Azmat Ulla (Acting Head of Delegation), email azmat.ulla@ifrc.org, phone +92 301 522 6903; Flemming Nielsen (Head of Operations), email: flemming.nielsen@ifrc.org, mobile: +92 0300 555 4522 (Pakistan) + 41 79 217 3343 (Geneva)*
- *In Geneva: Jagan Chapagain (South Asia Regional Officer), jagan.chapagain@ifrc.org, phone +41 22 730 4316, fax +41 22 733 0395; Christine South (Pakistan Desk Officer), christine.south@ifrc.org, phone +41 22 730 4529; Penny Elghady (Asia Pacific Department), penny.elghady@ifrc.org, phone: +41 22 730 4864.*
- *For logistics /mobilization and coordination of consignments, in-kind donations and shipping instructions please contact: Victoria Tattersfield (Logistics Department), victoria.tattersfield@ifrc.org, phone +4122 730 4852; mobile: +41 79 308 9820; fax +41 22 730 4906.*

All International Federation assistance seeks to adhere to the [Code of Conduct for the International Red Cross and Red Crescent Movement and Non-Governmental Organizations \(NGO's\) in Disaster Relief](#) and is committed to the [Humanitarian Charter and Minimum Standards in Disaster Response](#) in delivering assistance to the most vulnerable. For support to or for further information concerning Federation programmes or operations in this or other countries, or for a full description of the national society profile, please access the Federation's website at <http://www.ifrc.org>

Background

An earthquake with a magnitude of 7.6 on the Richter scale, centered 95 kilometres north-east of Pakistan's capital, Islamabad, struck at 0350 GMT (0850 local time) on 8 October 2005, with tremors felt across the region from Kabul to Delhi. The quake has decimated northern Pakistan and northern India. In Pakistan alone, enormous numbers of people have been killed and injured. More than 3.5 million people have been made homeless. The immensity of the disaster is one of deadliest in the region in a century.

Situation

United Nations officials announced that hundreds of earthquake survivors in tented villages in Muzaffarabad, the regional capital of Pakistan administered Kashmir (PAK), have been affected with acute diarrhoea and doctors are investigating whether they are cases of cholera. Snowfall, rain and freezing winds are all set to multiply the challenges faced by aid workers to control the further spread of waterborne diseases, which could pose an added threat to survivors. The need to scale up efforts to provide a safe water supply, adequate sanitation facilities and emergency health care is now a priority.

United Nations officials announced that hundreds of earthquake survivors in tented villages in Muzaffarabad, the regional capital of Pakistan administered Kashmir (PAK), have been affected with acute diarrhoea and doctors are investigating whether they are cases of cholera. Snowfall, rain and freezing winds are all set to multiply the challenges faced by aid workers to control the further spread of waterborne diseases, which could pose an added threat to survivors. The need to scale up efforts to provide a safe water supply, adequate sanitation facilities and emergency health care is now a priority.



Improving water supplies and sanitation in densely populated tent villages is crucial to keeping cholera and other serious waterborne diseases at bay

The Pakistan government announced that the reconstruction of earthquake devastated areas would take five years but the government was determined to complete a substantive part in three years. The damage assessment report and final figures, now being compiled by the newly formed Earthquake Reconstruction and Rehabilitation Authority (ERRA), will be presented on 19 November at a donors' conference in Islamabad. The government is targeting the distribution of PKR 20 billion (CHF 440 million) among quake survivors to help them rebuild their lives, with compensation provided for the injured, for family members that have died and for damaged houses.

On 9 November, Pakistan and Indian officials exchanged relief goods for earthquake victims in the two parts of Kashmir as the second crossing on the Line of Control dividing the disputed region opened. More relief aid will be exchanged in the coming days.

Operational Development

To date, the Federation has delivered relief supplies to over 98,000 beneficiaries in North West Frontier Province (NWFP), including special relief missions by helicopter to remote villages in the Kagan Valley. The coming weeks should see continued distribution of tents and non-food item (NFI) packages to families that have not received any assistance, upgrading of summer tents, and the provision shelter repair kits to affected families.

As a result of an assessment by the helicopter RDRT teams, a new emergency health kit and paediatric medications have been dispatched to the village of Jared in the Kagan Valley. Besides diarrhoea, health problems that have been identified include scabies and upper respiratory tract infections, especially in children. Health efforts in some areas of NWFP, including Balakot, are now being duplicated as new agencies flood into town. Mobile health teams are now looking at expanding outreach services to more remote areas to avoid this overlap. More than 30,000 people have been treated by the Federation and PRCS since operations began one month ago.

The Federation water sanitation ERUs in Batagram and Balakot, run by Swedish/Austrian and German/Austrian Red Cross Societies continue to supply and distribute clean drinking water and establish sanitation facilities to quake survivors. Hygiene promotion will start in combination with the setting up of latrines in the coming days.

Coordination

Red Cross and Red Crescent Movement

Since operations began over one month ago, the PRCS has distributed over 8,000 tents and 50,000 blankets to quake survivors in NWFP and Pakistan administered Kashmir. The PRCS/Federation and its partners are preparing for a recovery planning process, outlining how the Movement will contribute to the long-term plans of the government in different sectors, including shelter, health and water sanitation.

A coordination meeting with participating national societies, organized by the PRCS on 8 November, was attended by Red Cross Red Crescent representatives from Denmark, Germany, Iraq, Japan, Kuwait, Qatar, Turkey and the United Arab Emirates as well as the Federation and the International Committee of the Red Cross (ICRC). The participating national societies reported distribution and delivery figures to date in relief and health, as well as their relief and health plans for the coming months. Nothing significant was shared about the rehabilitation and recovery phase of the operation at this stage but this will be discussed in future. A mapping exercise will soon be completed by the Federation to track activities of all sectors of the Movement.

External partners

The Federation attended a cluster meeting on the reconstruction and recovery phase of the disaster on behalf of the PRCS. This was attended by representatives of the Pakistan government, high-level bilateral lending agencies, notably the World Bank and Asian Development Bank, non-governmental organizations, and several heads of mission. The government announced that a preliminary needs assessment had been carried out and a full report would be released by 15 November, prior to the 19 November international donors' conference. The report will include details of implementation (to be based at the provincial level), as well as the strategic directions and guiding principles for construction. The relief phase of the operation is expected to take six to 18 months, while the reconstruction process three to five years. A number of questions were raised at the meeting pertaining to environmental issues, procedural harmonization with the various agencies involved and other plans.

A number of clear gaps and priorities are being pinpointed during the health cluster meetings and are emerging as key concerns for the Federation health programme. During a recent meeting, the Ministry of Health (MoH) called for organizations to assist with spinal patients, some 76 of whom are in a government hospital in poor condition; an additional 13 are reported to be in Muzaffarabad. The Federation health sector strategic plan has been submitted to the MoH to assist them with overall planning for the next six months. This has provided constructive advice and support to the ministry and has helped cement the relationship with the authorities on health.

Good relations have been established with Federation relief teams and the local military authorities in Mansehra, who are now well informed at all levels of the Federation's activities in NWFP.

Red Cross and Red Crescent action - objectives, progress, impact

1. Emergency relief (food and non-food)

Objective: the basic shelter and household needs of 81,000 earthquake-affected families (approximately 570,000 people) in northern Pakistan are met over the next six months, enabling them to start rebuilding their future.

Progress/Achievements

The Federation's relief distribution plan is in the process of being revised. Over the next few days, the team will be consolidating assessment processes and information and analyzing what has been achieved to date. The coming weeks should see continued distributions of tents and NFI packages to families who have not received any assistance, the upgrading of summer tents to ensure winterization and the provision of shelter repair kits to affected families. Distribution of tents will be dependent on weather and is expected to continue until mid-December, though it will still be possible to distribute tents during the winter months.

Federation relief distributions as of 10 November

Location	Tents	Blankets	Tarpaulins	No. of Families	No. of beneficiaries
Garhi Habibullah	5,503	35,926	5,334	5,531	38,717
Balakot	3,967	27,349	3,967	3,967	27,769
Batagram/Battal	4,523	32,434	4,527	4,523	31,661
Kagan Valley		5,980			
Total	13,993	101,689	13,828	14,021	98,147

To date, the Federation has delivered relief supplies to over 14,000 earthquake-affected families, or some 98,000 beneficiaries. Special relief missions have continued by helicopter to remote locations in the Kagan Valley. During the reporting period, nearly 6,000 blankets and 240 tarpaulins were delivered to the villages of Kawai and Shogran. Some 90,000 blankets, 5,000 tarpaulins and 2,000 jerry cans are today en route to Jared village and over 800 jerry cans and 800 20-litre buckets will be distributed to Paras village. Assessments will be conducted from 13 to 15 November in and around eight remote villages north and east of Lari, with distributions to follow.

Constraints

Temperatures have started to drop and weather conditions are expected to deteriorate in the coming days, with slippery roads causing some problems for trucks distributing relief supplies. Due to the lack of tents in the pipeline distributions today will be limited. Further road operations are not likely to start again until 14 November, when the next shipment comes through.

2. Emergency health and care

Objective: Some 250,000 earthquake-affected people in northern Pakistan have access to appropriate quality health care, safe water and sanitation services in the next six months.

Progress/Achievements

Basic health care:

More than 30,000 people have been treated by the Federation and PRCS since operations began just over one month ago.

Watery diarrhoea cases have been reported across all primary health units and suspected diphtheria identified in Ghari Dopati. Two cases of meningitis and small cases of measles and mumps were also reported, though it is unclear if these are similar to pre-earthquake numbers. The Federation has made a request from the epidemiology department of the World Health Organization (WHO) for media culture to be supplied to ERUs and field hospitals so that samples can be sent back for analysis.



The Federation mobile health clinics continue to treat people injured as a result of the earthquake

As a result of an assessment by the helicopter RDRT teams, a new emergency health kit and paediatric medications have been dispatched to the village of Jared, in the Kagan Valley. Besides diarrhoea, health problems that have been identified include scabies and upper respiratory tract infections, especially in children.

In Balakot, reports show that the different agencies in town are duplicating health efforts. With the addition of another field hospital in this area (bringing the total to three) the Federation will increasingly concentrate its efforts, in coordination with the Spanish ERU, on mobile outreach services particularly to destinations further into the Kagan Valley. People living in the remote higher areas of the valley have a migration pattern to the lowlands during the winter, normally with designated areas leased or owned for keeping livestock. Since the earthquake, these areas have been destroyed and people forced to find any available space to camp. What is clear is that they will not be able to camp in government tent villages with animals. The mobile teams will therefore aim to bring primary health care to these groups in the lowlands. In addition, the Federation will support the MoH basic health care units in these areas with an accessible static facility.

In Batagram, the Federation will continue and expand outreach services that the French ERU has started in areas north of the town. The Federation's transport support unit, provided by the Norwegian Red Cross, will begin test runs into these areas with six-wheel trucks to provide road support where appropriate.

In Shanla and Kohistan districts, north of Batagram, the Federation will support 60 women health workers with tents for health houses and basic drugs. Kohistan, population 500,000, has been identified as the most neglected

and underserved district in the earthquake affected area. Out of 37 health facilities, 23 were partially damaged in the earthquake and only three medical officers are working in the district.

Responding to the needs identified by the MoH and specific hospitals that have been treating thousands of surgical cases since the earthquake, the Federation delivered ten surgical kits (disposable equipment for approximately 1,000 surgical cases) containing 500 tetanus vaccines and 500 tetanus immunoglobulin to Rawalpindi Hospital and a further ten surgical kits to Ayub Medical Centre in Abbottabad.

In Abbottabad, the multi-national field hospital continues to run smoothly and a very good relationship has been developed with the Ayub Medical Centre. At this stage, patient numbers have been capped at 100 patients until the arrival of additional nursing staff.

In Mansehra, the Federation is supplying basic drugs and tents for health houses to 140 women health workers. In line with the medium-term strategic plan developed by the NWFP health department, the Federation has expressed interest in supporting the following strategic components:

Ensuring survival through winter

The overall Federation priority is to ensure the survival of affected people throughout winter. Focus will then move on recovery interventions.

Serving remote villages first, especially those cut off from support during winter

By road or helicopter, combining relief efforts with health needs assessments and direct interventions, remote villages will be targeted with emphasis of restoring health centres and services provided by women health worker services.

Health teams will accompany special relief teams to carry out assessments in targeted areas. Based on identified needs and gaps, the Federation will provide essential medicines, equipment and supplies for women health workers or to selected primary health care facilities/centres. More seriously ill patients will be referred to nearby hospitals, for instance in Abbottabad.

Restoration of services at PHC facilities and health houses

Health houses have been one of the effective community-based health programmes previously in existence in Pakistan. Besides providing materials and medicines, the Federation intends to support the resumption of services by providing 200 winterised tents and possible heating for women health workers/supervisors in selected under/un-served communities.

Continued provision of essential primary health care and secondary services

The Federation's two basic health care units in Batagram and Balakot are committed to cover basic health service needs for some 20,000 persons each for the next six months, and can be expanded to 20-bed in-patient services if necessary. The ERUs also have good outreach capability. The French Red Cross ERU has, for example, sent a mobile health unit to Pachtu, Rashang, Bateela and Banna. The Federation will continue to work alongside district health authorities, focusing on efforts to whose efforts in the town are being duplicated by other agencies integrate with local staff and services so as to expand services further and ensure smooth handover of facilities.

Provision of mobile health care support services at selected sites

Eight PRCS mobile health teams have been delivering essential health services at Jehlum Valley, Upper Chattar, Garhi Dopatta and areas of NWFP. Together with the Republic of Korea National Red Cross (KNRC), a PRCS team also served patients in Besham.

Considering that the rehabilitation/reconstruction of damaged static health facilities will take time and many organizations have already seen cases which have outbreak/epidemic potential, the Federation will continue to expand the operation of mobile services in the next six months, and gradually include mobile support to static basic PHC facilities and other services.

Work with and coordinate with MoH to implement district health plan through UN/WHO coordination cluster mechanisms.

The Federation, and its Red Cross Red Crescent member societies, will work closely with the Pakistan government-designated coordinating body to ensure that proposed contributions are in line with the overall components and directions of the government's health strategy. The PRCS/Federation and its partners are preparing for a recovery planning process which will outline how the Movement will contribute to the long-term plans of the government in different sectors, including health.

Psychosocial support:

Three Pakistan mental health workers have begun an assessment in the multi-national field hospital in Abbottabad to identify trauma counselling needs and give recommendations on how to manage these patients. The team speak both Urdu and Pashtu which is vital to ensure all patient needs are met. Planning is underway for a play tent and area for the children.

Water and sanitation:

In Balakot, the Swedish/Austrian water sanitation ERU has continued with production and distribution. However, a shortage of transportation for trucking water has interrupted distribution services. Limited supplies have been distributed by tractor trailer but the low capacity has meant several distribution points are empty.

In Batagram, water production and consumption has increased and is now reaching some 7,000 to 8,000 beneficiaries. The construction of 25 latrines by the German/Austrian ERU for use by the hospital and French Red Cross clinic, as well as near by populations has been completed. More latrines will be constructed for the local population once trucks become available to purchase materials.

In Maira, water supply is now reaching up to 4,000 people in the tented camps. Only five emergency latrines are currently available to service the growing number of people and more sanitation facilities are urgently needed. Construction of permanent latrines will begin soon, led by another agency. The hygiene promotion team has been establishing contacts in the field with the government and other agencies. In the coming days, hygiene promotion will start in combination with the setting up of latrines.

Constraints

The lack of transport for trucking water and materials is hampering the distribution of water and construction of sanitation facilities in both Batagram and Balakot. The Federation transport support unit has been requested to assist until longer-term solutions are found.

3. Logistics/IT/Telecommunications

Objective: The ongoing PRCS and Federation relief operation have efficient logistical, IT and telecommunication infrastructure in the operational areas.

Progress/Achievements

Logistics:

Air and sea freighted Federation relief goods and equipment continue to flow into Islamabad, Peshawar and Karachi, with 80 flights received and over 270 truck loads of goods dispatched so far. Together with PRCS, some 540 trucks loads of aid have been dispatched to date for distribution to earthquake survivors.

The Federation fleet currently comprises 26 vehicles, 13 operational in Mansehra and seven in Islamabad. The rest of the vehicles will be allocated and transferred to Mansehra once drivers have been recruited. Additionally, ten rental vehicles including two minibuses are being used by the Federation in Mansehra, Abbottabad and Islamabad. The five cars donated by Telenor for use at the start of the emergency will be returned in the coming days.

The last of the M6 trucks donated by Norwegian Red Cross have been deployed to Mansehra by the transport support unit (TSU). Two team members, based in Mansehra for the past week, have been recruiting drivers and of the ten to be recruited in the first stage, four have been hired together with one translator. Parking and workshop facilities have also been secured for six months, located close to the British Red Cross warehouse. Requests for support from the TSU have come from the two water sanitation ERUs in Batagram and Balakot to provide transport for trucking water. Furthermore, the French Red Cross basic health unit ERU in Batagram, which until

recently was able to conduct mobile clinics in remote areas using military helicopters, has requested support from the TSU to continue to access these areas.

IT/Telecommunications:

Programming cables for the PRCS-donated VHF handsets have now been located. Programming of all handsets will commence this weekend and training is planned for early next week. The new IT telecom delegate is now running operations in Mansehra. Dial-up connections have been installed at the multi-national field hospital in Abbottabad.

4. Communications – Advocacy and Public Information

Objective: The needs of the earthquake-affected population in Pakistan are advocated for and the Red Cross and Red Crescent's interventions profiled through national and international media coverage

Progress/Achievements

A video news release (VNR) marking one month after the earthquake, broadcast through the APTN network on 7 November, was shown on BBC World, Sky News, ABC (Australia) and ran on GTO, the local TV station, all day on 8 November. All major newspapers, TV and radio stations in Pakistan covered the press briefing of the Federation secretary general and the PRCS chairman. Interviews were given by Federation delegates to ABC (Australia), BBC radio on health issues, and Vatican Radio and Radio Mediterranean International on the general situation.

On 10 November, a VNR on water sanitation ran on APTN, following reports of an outbreak of cholera in Muzaffarabad; a web story on the same issue was submitted to the Federation's media department. The VNR ran in full length on the BBC Asia Today programme, together with an interview with the Federation's senior health officer in Geneva.

Information delegates are working on facilitating media trips for Reuters and Dagens Nyheter, one of the largest Swedish dailies, in the coming days. A visit to Pakistan administered Kashmir to profile the work of the PRCS is being discussed with the PRCS information officer and may take place next week.

Outstanding Needs

- There is still a long way to go to cover the Emergency Appeal. Cash contributions are still urgently needed to allow the Red Cross and Red Crescent to rapidly scale up emergency operations.
- The detailed mobilization table is available and updated on [Disaster Management Information System \(DMIS\)](#). The Federation is still working on mobilizing relief items, but is simultaneously reviewing the situation in the pipeline to ensure they are coherent with distribution plans. Where possible, relief items will be procured locally. A message has gone out to all donor national societies to encourage them to inform the Federation Logistics Department of all shipping details on any outstanding pledges. This will enable us to plan receipt, clearance, storage and transportation of all goods and will enable us to plan relief distributions more effectively.
- The following longer-term positions need to be sought internationally and regionally: head of operations, deputy head of operations, head of support services, finance delegate, legal delegate, information coordinator, IT/telecom coordinator, logistics delegate, procurement delegate, warehouse manager, security coordinator, shelter coordinator, recovery coordinator, health coordinator, health delegates, general surgeon, orthopaedic surgeon, anaesthetist, operating theatre and surgical ward nurses.

[Contributions list below; click here to return to the title page.](#)

[The map of the operation is attached to this report as Annex 2 and will be updated on a weekly basis.](#)

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

11/11/2005

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
-------	----------	----------	------	-----------	------	---------

CASH

REQUESTED IN APPEAL CHF ----->	152,033,929	TOTAL COVERAGE 58.2%	
ADC FOUNDATION	10,000 USD	12,805 31.10.05	
AMERICAN - RC	850,000 USD	1,099,900 17.10.05	
AMERICAN - PRIVATE DONORS		45,149 25.10.05	
AUSTRALIAN - GOVT	3,000,000 AUD	2,956,500 10.10.05	TENTS, BLANKETS, TARPAULINS, KITCHEN SETS, AIRFREIGHT
AUSTRALIAN - RC	500,000 AUD	480,500 19.10.05	MEDICAL SUPPLIES, VACCINES, CHOLERA KITS
AUSTRALIAN - RC	500,000 AUD	480,500 25.10.05	NEW EMERGENCY HEALTH KITS
BRITISH - RC	250,000 GBP	569,500 09.10.05	
BRITISH - GOVT/DIFD	1,470,000 GBP	3,342,780 27.10.05	
BRITISH PETROLEUM	500,000 USD	647,000 11.10.05	
CAMBODIAN - RC	15,000 USD	19,410 13.10.05	
CANADIAN - GOVT/CIDA/HAPS	990,000 CAD	1,093,455 13.10.05	
CANADIAN - GOVT/CIDA/HAPS	99,000 CAD	109,346 18.10.05	
CANADIAN - RC	1,000,000 CAD	1,088,200 19.10.05	PROCUREMENT 1300 WINTERISED TENTS
CANADIAN - RC	1,000,000 CAD	1,088,200 02.11.05	
CHINA - HONG KONG RC BRANCH	500,000 HKD	83,100 10.10.05	PROCUREMENT SHELTER KITS
CHINA - MACAU - RC BRANCH		25,000 10.10.05	PURCHASE OF MEDICINES, BLANKETS & TENTS
CYPRUS - RC		13,354 12.10.05	
CZECH - RC	10,000 USD	12,940 25.10.05	
DANISH - RC		95,920 14.10.05	
DANISH - RC		492,769 20.10.05	
ECHO (05004)	810,747 EUR	1,262,333 13.10.05	
FINNISH - PRIVATE DONORS	200 EUR	311 12.10.05	
FRENCH - RC	400,000 EUR	618,200 07.11.05	
FRENCH - PRIVATE DONORS		467 21.10.05	
GERMAN - RC	500,000 EUR	778,500 27.10.05	
GERMAN - PRIVATE DONORS		148 18.10.05	
HELLENIC - RC		50,000 11.10.05	PURCHASE 10'000 BLANKETS
ICELANDIC - GOVT	75,000 USD	97,050 09.10.05	
INDONESIA - PRIVATE DONOR		128 28.10.05	
IRISH - GOVT	300,000 EUR	467,100 13.10.05	
IRISH - GOVT	350,000 EUR	540,925 28.10.05	
ITALIAN - GOVT	200,000 EUR	311,400 17.10.05	
ITALIAN - RC	150,000 EUR	231,825 10.10.05	FOR INDIA, EUR 50'000 (DP , see AA047)
JAPANESE - RC	262,513 USD	339,692 11.10.05	
JAPANESE - RC	2,800,000 USD	3,585,400 25.10.05	PROCUREMENT FOR MOB TABLE: 10000 FAMILY TENTS, 10000 KEROSENE LAMPS, 10000 KEROSENE STOVE, 50000 BLANKETS
JAPANESE - RC	150,000,000 JPY	1,662,000 09.11.05	

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

11/11/2005

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
KOREA, REPUBLIC - RC		50,000	USD	64,700	10.10.05	
LATVIAN - GOVT		100,000	USD	129,400	13.10.05	
LIBYAN - RC				10,000	10.10.05	
LICHTENSTEIN - PRIVATE DONOR				300,000	28.10.05	
LUXEMBOURG - GOVT		200,000	EUR	311,400	24.10.05	
MACEDONIA, FYR - RC		3,000	EUR	4,671	28.10.05	
MONACO - RC		30,000	EUR	46,710	17.10.05	
NETHERLANDS - GOVT		160,428	EUR	247,941	13.10.05	
NETHERLANDS - RC		213,904	EUR	330,588	03.11.05	
NETHERLANDS - PRIVATE DONORS				825	28.10.05	
NEW ZEALAND - RC		100,000	NZD	89,600	20.10.05	
NEW ZEALAND - GOVT		400,000	NZD	358,400	25.10.05	
NORWEGIAN - GOVT/RC		10,000,000	NOK	1,975,000	09.11.05	RELIEF ACTIVITIES INCL. CHILDREN & VULNERABLE GROUPS
OPEC FUND F.INTERNATIONAL DEV.		600,000	USD	768,300	13.10.05	+ INDIA (DP, 05AA047) + AFGHANISTAN (DP, 05AA045), USD 200'00 EACH
PHILIP MORRIS		30,000	USD	38,415	24.10.05	
PHILIPPINES - RC		10,000	USD	12,805	03.11.05	
POLAND - PRIVATE DONORS				3,235	17.10.05	
PRIVATE DONORS ON LINE				390,000	14.10.05	
SINGAPORE - GOVT & RC				100,000	26.10.05	PROCUREMENT OF RELIEF ITEMS
SINGAPORE - GOVT & RC				100,000	09.11.05	PROCUREMENT EMERGENCY RELIEF & MEDICAL
SINGAPORE - PRIVATE DONOR		50,000	EUR	77,850	11.10.05	
SOUTH AFRICA - PRIVATE DONOR		1,000	USD	1,280	27.10.05	
SWEDISH - GOVT through RC		2,000,000	SEK	334,000	11.10.05	
SWEDISH - GOVT through RC & RC		15,400,000	SEK	2,571,800	14.10.05	
SWEDISH - RC		25,000,000	SEK	4,050,000	08.11.05	
SWISS - PRIVATE DONORS				15,600	12.10.05	
USA - COCA-COLA		1,000,000	USD	1,294,000	11.10.05	
WHO STAFF- VERF				4,000	09.11.05	
SUB/TOTAL RECEIVED IN CASH				37,332,327	CHF	24.6%

KIND AND SERVICES (INCLUDING PERSONNEL)

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
A number of in-kind contributions are on their way to Pakistan. The list will be updated as soon as all details are avail:					10.11.05	
AMERICAN - RC				2,665,700		3000 TARPULINS, 18000 KITCHEN SETS, 3000 BUCKETS, 5000 FAMILY TENTS, 70000 BLANKETS, 1000 WINTERISED FAMILY TENTS, 18000 HYGIENIC PARCELS. 1600 TENTS GAMMAX, 42900 BLANKETS, QUILTS, TRANSP./INS. ,

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

11/11/2005

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
AUSTRIAN - RC				908,960		10500 HYGIENIC PARCELS, 7 EMERGENCY HEALTH KITS, 306 FAMILY TENTS, 76000 BLANKETS, TRANSP./INS.
BELGIAN - RC/FL				167,180		11720 BLANKETS, 20000 JERRYCANS, 275 WINTERISED FAMILY TENTS, 3500 KITCHEN SETS, TRANSP./INS.
BELGIAN - RC/FR				522,405		12500 BLANKETS, 1250 KITCHEN SETS, 1478 FAMILY TENTS, 1250 TARPAULINS, TRANSP./INS.
BRITISH - RC				3,939,897		600 KITCHEN SETS, 6000 WINTERISED FAMILY TENTS, 2000 JERRYCANS, 30000 HURRICANE LAMPS, 11300 TARPAULINS 4X6M, 300 TARPAULINS 4X60M., 21700 BLANKETS, 600 FAMILY TENTS, TRANSP./INS.
CANADIAN - RC				3,137,571		12000 BLANKETS, 3300 BLANKETS HIGH LOFT, 94 TARPAULINS, 2000 GRAMMAX TENTS, 3000 WINTERISED FAMILY TENTS, 5 EMERGENCY HEALTH KITS, TRANSP./INS.
DANISH - RC				663,769		1, BASE CAMP, 15 EMERGENCY HEALTH KITS, 50 DELEGATE HEALTH KITS, 9000 TARPAULINS, TRANSP./INS.
DANISH - RC				460,625		ERU TELECOM & LOGISTICS UNITS
EGYPTIAN - RC				18,200		2000 BLANKETS, 20 FAMILY TENTS, TRANSP./INS.
FINNISH - RC				3,459,885		5798 WINTERISED FAMILY TENTS , 5500 HURRICANE LAMPS, 10'000 STOVES, 59 DOUBLE FLY TENTS, TRANSP./INS.
FRENCH - RC				318,379		1440 HURRICANE LAMPS, 13940 JERRYCANS, 2300 TARPAULINS, 2856 KITCHEN SETS, TRANSP./INS.
FRENCH - RC				415,580		ERU BASIC HEALTH CARE UNIT
GERMAN - RC				778,500		ERU SPECIALISED WATSAN MODULE
GERMAN - RC				2,898,450		10000 BLANKETS, 4000 WINTERISED FAMILY TENTS, 10000 SLEEPING BAGS, 10000 HURRICANE LAMPS, 200 HOSPITAL BEDS, TRANSP./INS.
IRISH - RC				1,217,450		7300 BLANKETS, 2250 WINTERISED FAMILY TENTS, TRANSP./INS.
LUXEMBURG - RC				166,400		6000 BLANKETS, 10 EMERGENCY HEALTH KITS, TRANSP./INS.
NEPAL - RC				6,500		1000 BLANKETS, TRANSP./INS.
NETHERLANDS - RC				4,521,972		30000 BLANKETS QUILT, 20000 TARPAULINS, 1000 FAMILY TENTS , 16000 KITCHEN SETS, 27 EMERGENCY HEALTH KITS, 814905 BLANKETS, 153000 BEDSHEETS, 2000 WINTERISED FAMILY TENTS, 7000 KEROSENE HEATERS, 20500 HYGIENIC PARCELS, TRANSP./INS.

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

11/11/2005

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
NORWEGIAN - RC				17,259,688		11320 BLANKETS, 8 RUBHALL TENTS, 50 FAMILY TENTS, 1620 TARPAULINS, 21 TENTS 90M2, 4 WATERTANKS, 40 TRUCKS, 1 LABORATORY MODULE, 1 X-RAY MODULE, 95 SURGICAL SUPPLY KITS, 4 WATER PURIFICATION UNIT, 1 MOTHER & CHILD CARE MODULE, 120 TENTS GAMMAX, TRANSP./INS.
NORWEGIAN - RC				500,000		ERU REFERRAL HOSPITAL
QATAR - RC				3,556,799		6299 FAMILY TENTS, 1170 BEDS RIGID FRAME, 48480 BLANKETS, 92 VARIOUS MEDICINE, DATES, LENTILS, ASSORTED FOOD, TRANSP./INS.
SINGAPORE - RC				68,042		13900 FOOD RATION MRS, TRANSP./INS.
SPANISH - RC				125,613		8125 BLANKETS, 2400 TARPAULINS, 100 FAMILY TENTS, TRANSP./INS.
SPANISH - RC				415,580		1 ERU BASIC HEALTH CARE UNIT, 1 ERU WATSAN, TTT, DISTRIB. TUCKING, MASS SANITATION MODULE
SWEDISH - RC				593,220		ERU WAT-SAN, MASS SANITATION MODULE
SWEDISH - RC				314,746		976 WINTERISED TENTS, 3000 SLEEPING BAGS, TRANSP./INS.
SWISS - RC				1,839,539		7220 BLANKETS, 3896 KITCHEN SETS, 2 EMERGENCY HEALTH KITS, 20000 BLANKETS, 4500 TARPAULINS, 1200 FAMILY TENTS , 1562 KEROSENE HEATERS, 2000 WINTERISED TENTS, TRANSP./INS.
VARIOUS DONORS	DELEGATES	12		144,000	12.10.05	
SUB/TOTAL RECEIVED IN KIND/SERVICES				51,084,650	CHF	33.6%


ADDITIONAL TO APPEAL BUDGET

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
SUB/TOTAL RECEIVED				0	CHF	



Pakistan: Earthquake

Situation map
 Issued 8 November 2005

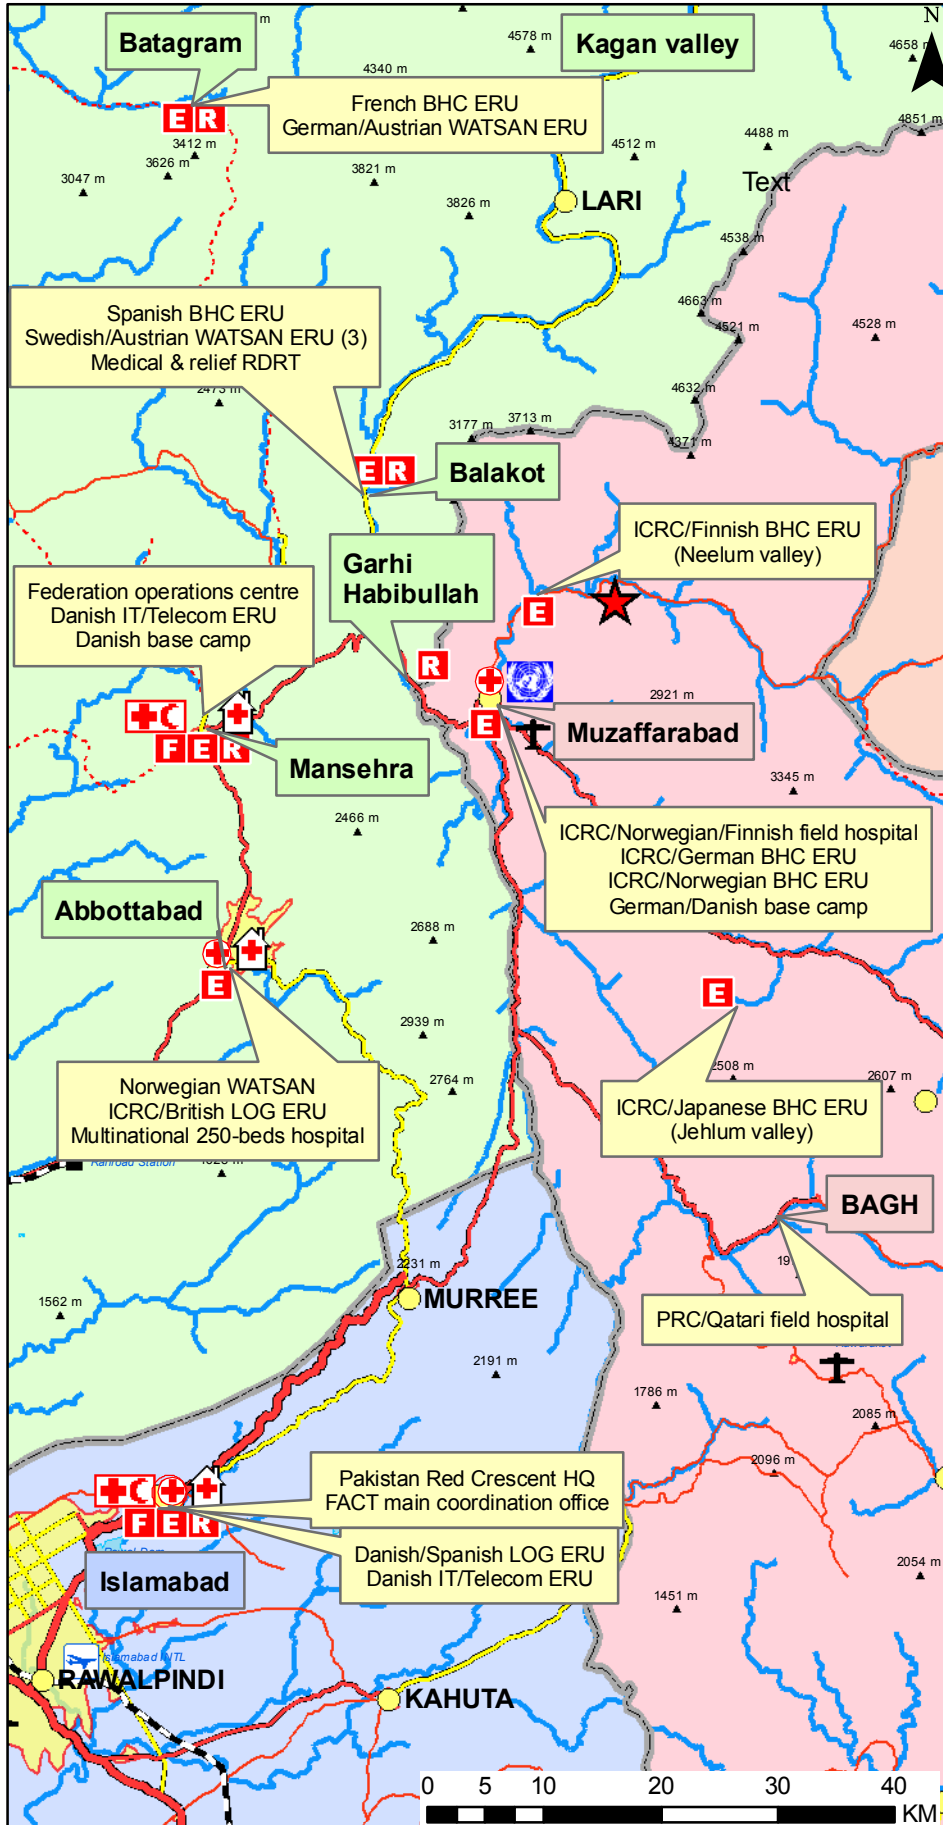

- Earthquake epicenter
 - Federation delegation or hub
 - ICRC delegation or sub-delegation
 - Field Assessment Coordination Team (FACT)
 - Emergency Response Unit (ERU)
 - Regional Disaster Response Team (RDRT)
 - Federation and/or ICRC logistics center
 - UN operations centre
- Provinces**
- Indian Jammu & Kashmir
 - North-west Frontier
 - Pakistan-administered Kashmir
 - Punjab
- Administrative boundaries
 - Capital
 - City
 - City extension
 - Highway, Hard, All weather
 - Main road, Hard, All weather
 - Secondary road, Loose, All weather
 - Local road, Loose, Dry weather
 - Track, Loose, Dry weather
 - Airport
 - Airfield
 - railroad station
 - Mountain tops
 - Lakes
 - Main rivers

The maps used do not imply the expression of any opinion on the part of the International Federation of Red Cross and Red Crescent Societies or National Societies or the ICRC concerning the legal status of a territory or of its authorities.

Map data sources: ESRI, Keyobs, Federation, ICRC
