

OPERATIONS UPDATE



International Federation of Red Cross and Red Crescent Societies
Fédération Internationale des Sociétés de la Croix-Rouge et du Croissant-Rouge
Federación Internacional de Sociedades de la Cruz Roja y de la Media Luna Roja
الاتحاد الدولي لجمعيات الصليب الأحمر والهلال الأحمر

PAKISTAN: EARTHQUAKE

8 December 2005

The Federation's mission is to improve the lives of vulnerable people by mobilizing the power of humanity. It is the world's largest humanitarian organization and its millions of volunteers are active in over 183 countries.

In Brief

Appeal No. 05EA022; Operations Update no. 18; Period covered: 29 November -5 December 2005; Appeal coverage: 63.3%; ([click here to go directly to the attached Contributions List, also available on the website](#)).

Appeal history:

- Preliminary Emergency Appeal (launched as South Asia: Earthquake) on 9 October 2005 for CHF 10.8 million (USD 8.4 million or EUR 7 million) for four months to assist 30,000 families (some 120,000 beneficiaries).
- Operations Update No. 3 of 12 October 2005 increased the Preliminary Appeal budget to CHF 73,262,000 (USD 56,616,692 or EUR 47,053,307) to assist up to 150,000 families (some 750,000 beneficiaries) for six months, as an increasingly serious situation has unfolded.
- Operations Update No. 5 of 17 October 2005 revised down the number of targeted families to 70,000 (some 500,000 beneficiaries), based on the newly assessed delivery capacity and average family size of seven.
- Revised Emergency Appeal launched on 25 October 2005 for CHF 152 million (USD 117 million or EUR 98 million) to assist 81,000 families (some 570,000 beneficiaries) for six months.
- Disaster Relief Emergency Funds (DREF) allocated: CHF 200,000.

Outstanding needs : To date CHF 96.1 million has been received, of which CHF 50.9 million is in cash and CHF 45.2 million is in-kind contributions. More pledges are in the pipeline and will be reflected in the next operations update; updates are now being issued on a weekly basis. Additional pledges – especially in cash – are still urgently needed.

Related Emergency or Annual Appeals: [Pakistan Annual Appeal 05AA049](#), [South Asia Regional Annual Appeal 05AA051](#)

Operational Summary:

The need for shelters to protect earthquake survivors from the onslaught of a harsh winter is urgent and a huge aid effort involving the Federation/Pakistan Red Crescent Society (PRCS), the International Committee of the Red Cross (ICRC), the Pakistan authorities, the United Nations and numerous aid organizations is underway.

To date, the Federation/PRCS have provided emergency relief by land and air to more than 200,000 beneficiaries. More than 64,000 people have had access to health services provided by the Red Cross Red Crescent. The Federation/PRCS continue to expand operations further to the north and west of the country. Water and sanitation operations have by now reached some 39,000 beneficiaries and numbers are expected to increase as additional structures are installed. Again, the Federation's support here has extended to isolated and remote regions in the north/west of Pakistan.

The joint logistics agreement between the Federation and the ICRC will end in mid-December, with the ICRC reducing its activities in Islamabad and Abbottabad and concentrating efforts in Muzaffarabad. As part of the ongoing good cooperation between the different elements of the Movement in Pakistan, management of the warehouse in Mansehra, currently run by the British Red Cross Society emergency response unit (ERU) under the ICRC, will come directly under the Federation's logistics set up. After mid-January the Federation will take over the management and running of the warehouse from the ERU.

For further information specifically related to this operation please contact:

- In Islamabad: Khalid Kibriya (Secretary-General), Pakistan Red Crescent Society; email: hilal@isb.comsats.net.pk, Phone: +92.51.925.0404; Fax: +92.51.925.0408
- In Islamabad: Per Jensnaes (Acting Head of Delegation); email: pakistaneg02@ifrc.org; Phone: +92.300.555.4502; Fax: +92.51.443.0745; Flemming Nielsen (Head of Operations); email: flemming.nielsen@ifrc.org; Mobile: +92.0300.555.4522 (Pakistan); +41.79.217.3343 (Geneva)
- In Geneva: Jagan Chapagain (South Asia Regional Officer), email: jagan.chapagain@ifrc.org; Phone: +41.22.730.4316; Fax: +41.22.733.0395; Christine South (Pakistan Desk Officer); email: christine.south@ifrc.org; Phone: +41.22.730.4529; Penny Elghady (Asia Pacific Department); email: penny.elghady@ifrc.org; Phone: +41.22.730.4864.
- For logistics/mobilization and coordination of consignments, in-kind donations and shipping instructions please contact: Victoria Tattersfield (Logistics Department); email: victoria.tattersfield@ifrc.org; Phone: +41.22.730.4852; Mobile: +41.79.308.9820; Fax: +41.22.730.4906.

All International Federation assistance seeks to adhere to the [Code of Conduct for the International Red Cross and Red Crescent Movement and Non-Governmental Organizations \(NGOs\) in Disaster Relief](#) and is committed to the [Humanitarian Charter and Minimum Standards in Disaster Response](#) in delivering assistance to the most vulnerable. For support to or for further information concerning Federation programmes or operations in this or other countries, or for a full description of the national society profile, please access the Federation's website at <http://www.ifrc.org>

Background

An earthquake with a magnitude of 7.6 on the Richter scale, centred 95 km northeast of Pakistan's capital, Islamabad, struck at 08:50 local time (03:50 GMT) on 8 October 2005, with tremors felt across the region from Kabul to Delhi. The quake has decimated northern Pakistan and northern India. In Pakistan alone, enormous numbers of people have been killed and injured. More than 3.5 million people have been made homeless. The immensity of the disaster is such that it remains one of the deadliest in the region in living memory.

Situation

Health officials have reported hundreds of pneumonia cases in earthquake-stricken areas of Pakistan-administered Kashmir (PAK), most of them children. With a more intense winter season and most quake-survivors without adequate shelter, the number of patients suffering from pneumonia and other cold-related diseases has increased dramatically this year. The first large outbreak of measles has killed one child and affected 14 others in a town outside Muzaffarabad. Authorities have reported that more than 700,000 children in camps and isolated populations have so far been vaccinated against measles, polio, tetanus, typhoid and cholera.

The World Food Programme (WFP) reported that it has enough supplies to feed thousands of Pakistan earthquake survivors through the winter, but more money is needed to maintain food distribution through until spring. Meanwhile, the prices of essential goods, including wood and iron sheeting, have spiralled in quake-devastated areas.

On 1 December, a missile attack on a house in North Waziristan, near the Afghan border, killed five people, amongst them reportedly an Al Qaeda operative. Agencies are monitoring security in the area. On the same day, an earthquake measuring 5.1 on the Richter scale jolted the region, however, no casualties or damage has been reported.



With a more intense winter than usual, hundreds of children in quake-stricken areas have succumbed to pneumonia

Operational developments

A survey by the Pakistan military has identified that some 324,000 people (about 46,000 families) will remain in inaccessible areas during the winter period. This includes about 15,000 families in the Allai Valley and around

10,000 in the Kagan Valley. Of this figure 150,000 people (22,000 families) are targeted for “Operation Winter Race: the last mile.” The military currently has five engineering battalions divided into 192 teams implementing the “one warm room” strategy in the highland areas. The operation has so far constructed more than 2,000 shelters and requires some 2.7 million corrugated iron (CGI) sheets (ten per house). The logistical challenges and the amounts of CGI sheeting required for this operation raise serious challenges for this plan.

The WFP estimates that some one million people will face food shortages during the winter. Of this number, its own caseload will be 460,000 persons. There are currently discussions whether the government will be able to cover the gap. Based on these figures, WFP has asked the United Nations Joint Logistics Centre (UNJLC) to prepare a pre-positioning plan for the winter period. The plan is based on the idea of forward area support sites (FASS), small dumps for food and non-food items, which will serve a ten kilometre radius. The main target groups will be camp populations (both official and “spontaneous” camps) and people in inaccessible areas. There is, however, still some question among agencies as to the level of the problem and the issues relating to food security.

Shelter/protection against the winter is and will remain the Federation’s first priority and is aimed to enable people to remain in their villages if they so desire. The Federation/PRCS will continue to distribute winterized tents to the lowland areas and shelter repair kits to communities remaining in higher mountainous terrain. To date, the emergency relief items, including tents, blankets, tarpaulins, quilts and sleeping bags have reached more than 29,000 families, or more than one-third of the earthquake-affected people targeted under the Federation’s appeal.

Red Cross Red Crescent medical teams have provided more than 83,000 people with access to quality health care in the past two months. The French and Spanish Red Cross emergency response units (ERUs) continue to reach communities in Balakot and Batagram, respectively, and have expanded mobile services to camps and villages in remote areas. More than 4,500 inpatients have been treated at the Federation multi-national field hospital in Abbottabad since it began operations, while the Qatar Red Crescent basic health centre has seen 2,500 patients in the remote region of Bagh, since it opened ten days ago. The Swedish/Austrian and German/Austrian water sanitation ERUs, located in Batagram and Balakot respectively, continue to deliver an average of 130,000 to 150,000 litres of water each day, providing potable water to about 39,000 people.

Coordination

Red Cross and Red Crescent Movement

Daily meetings are held at the PRCS headquarters, and between the ICRC and the Federation to discuss a range of operational issues. A date has now been agreed for a meeting with donor national societies – this will be held in Islamabad the week of 16 January to discuss the operation to date and plans for the recovery phase. An invitation will be sent out by the PRCS in the coming days. In the field, the ICRC coordination delegate based in the sub-delegation in Muzzafarabad and the Federation deputy head of operations (DHoO) in Mansehra continue to meet to share resources and enhance operations on a practical level. The Federation DHoO is working hard with his PRCS counterpart in North West Frontier Province to establish a national society presence in Mansehra and look at opportunities to build the local capacity of PRCS.

The Federation logistics team has maintained a close working relationship with the ICRC to maximize the efficiency of joint operations. However, these joint operations are due to end in mid-December and both teams have discussed the best way to phase over the relevant resources and management responsibility to the Federation in Mansehra. Cooperation between the Federation and the ICRC will also continue on a case by case basis, for instance with the ICRC providing fueling and loading support for the Federation helicopter in Abbottabad. The logistics team is also liaising and coordinating actions with the UNJLC and other key actors to ensure the Federation logistics operation uses all information and resources as efficiently and effectively as possible.

External partners

There has been good coordination with the Pakistan government, including the military, as well as with the United Nations and other players. The Federation has been present in all relevant meetings of the UN cluster groups and other key coordination meetings in Islamabad and the field. The Federation is continuing to provide human resources and technical support to the cluster group on shelter.

Red Cross and Red Crescent action - objectives, progress, impact

1. Emergency relief (food and non-food)

Objective: the basic shelter and household needs of 81,000 earthquake-affected families (approximately 570,000 people) in northern Pakistan are met over the next six months, enabling them to start rebuilding their future.

Progress/Achievements

Red Cross Red Crescent relief is reaching out to more areas and more people, particularly those in inaccessible areas. To date, the Federation/PRCS has provided emergency relief to 203,518 quake survivors with over 25,000 tents, 171,000 blankets and 28,000 tarpaulins among the items distributed. The supply of winterized tents in the higher mountain areas (more than 4,000-5,000 feet) is no longer appropriate in view of the snowfall and here shelter repair kits will be distributed. The Federation/PRCS will continue to distribute winterized tents to the lower areas.

Besides shelter, the Federation is focusing on distributions of related items such as stoves, lamps, shawls, hygiene kits, mattresses, kerosene and kitchen sets to initially some 38,000 families in Garhi Habibullah, Balakot and Batagram.

Two months after the disaster, the Federation and the PRCS is continuing to deliver relief and carry out further assessments by air, dispatching self-sufficient regional disaster response teams (RDRTs) from South and Southeast Asia together with PRCS volunteers by helicopter to remote mountain areas.



An RDRT helicopter operations team member carries out assessments in the Kagan Valley to determine the needs of people living in remote and isolated mountain communities

Federation relief distributions as of 5 December

Location	Tents	Blankets	Tarpaulins	Sleeping bags	Quilts	Jerry Cans	Families
Garhi Habibullah	8,784	55,012	8,690	2,285	8,887	1,358	8,829
Balakot air/land	7,143	56,254	10,351	3,596	2,174	3,872	10,946
Batagram/Battal	8,794	59,124	8,819	2,848	6,440	1,132	8,829
Kohistan/Allai Valley	469	1,410	462	0	3,006	0	470
Total	25,190	171,800	28,322	8,729	20,507	6,362	29,074

In order to scale up distributions before the full impact of a harsh winter is felt, there is an urgent need to increase the number of relief teams from the current eight to 20 (150 people). The Federation has identified three ways of achieving this - by sourcing 100 staff and/or volunteers from PRCS, hiring a minimum of a further 20 RDRT members to join the current group, or recruiting internationally through Red Cross Red Crescent society network. The 20 teams would work for one month on an intensive winter distribution plan, which if successful could reach a further 30,000 families.

As of today, a full-time RDRT coordinator has joined the operation and will be the focal person for the RDRT support in Pakistan. The six-member RDRT team from Nepal Red Cross has agreed to extend their stay for an additional ten days, to maximize relief capacity for distributions before the year end and the South Asia regional delegation is continuing to source additional RDRT members to maintain this vital element of the relief operation.

2. Emergency health and care

Objective: Some 250,000 earthquake-affected people in northern Pakistan have access to appropriate quality health care, safe water and sanitation services in the next six months.

Progress/Achievements

Basic Health Care:

The Federation multi-national field hospital in Abbottabad continues to build up its capacity in a number of ways - in terms of the quality of care, the number of staff and the physical structures or support. The facility can now provide for a higher patient case load depending on needs in the months to come. Over 200 patients have been admitted and 132 operations performed since the hospital opened. The average daily occupancy rate after the first days has been 98 patients. Children have been immunized against polio, measles, diphtheria and hepatitis-B, while a number of adults have been immunized against tetanus.



Children's play tent at the Federation field hospital in Abbottabad

Nearly 80 patients have received psychosocial support at the field hospital, with two referrals made to a psychiatrist. Children's group play sessions continue on a regular basis, with a total attendance of 119 children at the sessions. During the reporting period, the play room was refurbished to include children's furniture and music. A physiotherapist from the Ayub Teaching Hospital has joined the hospital team and the high quality of care now being provided has led the Federation to cancel a request for an expatriate equivalent. The physiotherapy teams will soon be linked more closely to the work of the psychological team to ensure a more integrated level of care. Promotion of better bedside care continues with the training of locally registered nurses to take on more responsibilities.

Red Cross Red Crescent health figures as of 1 December

Health units	Locations	Beneficiaries
PRCS mobile medical teams (PAK)	Muzaffarabad, Lower Tandali, Jehlum Valley, Upper Chatter, Garhi Doppatta	22,754
PRCS mobile medical teams (NWFP)	Balakot, Garhi Habibullah	3,486
PRCS (Korean) mobile medical team	Besham (NWFP) (KRCS team has now left)	4,382
Federation (Spanish) basic health care unit	Balakot (NWFP)	3,231
Federation (French) basic health care unit	Batagram (NWFP)	4,750
Federation (Malaysian) medical unit	Balakot (NWFP) (team has now left)	1,182
Federation multi-national field hospital (Norwegian/Japanese) daily inpatients	Abbottabad (NWFP)	4,533
Federation (RDRT/German/Japanese) mobile medical teams	Kagan Valley (NWFP) (team has now left)	107
Qatar Red Crescent	Upper Dhuli, Bagh district (PAK)	2,500
Italian Red Cross field hospital	Mansehra	686
Saudi Red Crescent field hospital	Mansehra	*23,799
Turkish Red Crescent hospital	Muzaffarabad	11,680
Total		83,090

In Balakot, the activities of the Spanish Red Cross basic health care ERU have increased, in part due to the closing of the Chinese run hospital that had lately opened in the same area. On average the team attends to 100 patients per day, particularly cases relating to chronic pathologies rather than earthquake-related injuries. However, due to the

appearance of other new facilities in the area, the team is considering the possibility of moving the clinic to the old hospital in the middle of town.

In Batagram, the French Red Cross basic health ERU has had treated 314 outpatients during the week, mainly repeat dressings, injuries, scabies and other skin diseases. The mobile clinic has conducted assessments in Shamlai, about 18 km northeast of Batagram, with an estimated population of 4,000 families mostly living in tents and shelters. An Afghan NGO has agreed to establish a health centre there but, for the time being, the French Red Cross will continue to provide medical support. The ERU has been requested by the World Health Organization (WHO) to take over the medical services at Battagram I camp. This is currently run by another agency which however has limited facilities and equipment to sufficiently support the camp.

Water and sanitation:

The two water and sanitation emergency response units (ERUs) in Batagram and Balakot continue to deliver an average of 130,000 to 150,000 litres of water each day, providing potable water to about 39,000 people. Besides piped water networks, communities have access to seven 10,500 litre tanks erected in locations that are inaccessible to pipes. These tanks are filled daily by two Norwegian Red Cross-donated M6-trucks, provided by the Federation's transport support unit (TSU), and one hired tractor.

In Batagram, the German/Austrian Red Cross water and sanitation ERU has this week delivered an average of 30,000 litres of purified water each day to local communities and to the French Red Cross basic health care field unit. Two M6 trucks assist with the distributions. Assessments for the implementation of a water supply scheme are underway to cover remote areas – this is being led by a new Austrian Red Cross team member.

The hygiene promotion team has so far constructed 39 latrines in the Batagram area and another 25 will be completed this week. A total of 204 hygiene kits have been distributed and a further 50 kits allocated to the French Red Cross basic health care unit for targeted distribution both at the facility and for mobile outreach health activities. Two male volunteers have been identified and recruited to assist the team in health/hygiene education and water point assessment. The team has also identified three additional sites for latrine and bathing facilities, and spread personal hygiene messages prior to the distribution of kits. It has also completed the development of tools to improve hygiene promotion monitoring and reporting. The Federation is now considering running hygiene promotion activities in Batagram 1 camp.

In Balakot, three new Austrian Red Cross members have joined the Austrian/Swedish ERU team and will focus on the sanitation programme, specifically the construction of latrines and public bathrooms. Based on demand, the production of treated water has fluctuated between 135,000 and 240,000 liters per day. The team is looking at the possibility of supplying potable water to remote areas and has carried out assessments in eight remote quake-affected villages. 21 latrines have been constructed in the local tent villages and a further 20 latrines are scheduled for completion this week. Several three-stall bathrooms are also under construction. The hygiene promotion team has started the distribution of some 2,000 hygiene kits in local camps and villages.

Six volunteers from Balakot and Batagram attended a one-day joint Federation, UNICEF, Oxfam, WHO and Rural Water Supply and Sanitation Project (RWSSP) hygiene promotion masters training workshop in Batagram.

Constraints

Heavy rains during the weekend affected the construction of pit latrines. However, there is still an improvement in the pace of construction compared to the previous reporting period.

Psycho-social programme (PSP):

A complete curriculum for field officer training, including community mobilisation and participatory assessment, is being finalised this week. The process of recruiting the PSP programme manager, team leaders and field officers is underway. Unfortunately, there have been insufficient female applicants, especially in the Batagram area, and the Federation/Danish Red Cross will look into contacting wider networks to encourage female applicants.

An assessment of the Islamabad shelters has been conducted, however, the field has not yet identified where the PSP programme will be targeted. The Hattia camp for women and children is assessed to be well-managed by the government and there are few additional needs for the moment. Similarly, the H11 camp is covered by the Turkish

Red Crescent working with volunteer university psychology students. Two possible camps need more intensive assessment before a decision is taken. A Danish consultant is conducting a preparatory assessment of the programme and will explore possible links between PSP activities and the community-based health programme.

3. Logistics/IT/Telecommunication

Objective: The ongoing PRCS and Federation relief operation have efficient logistical, IT and telecommunication infrastructure in the operational areas.

Progress/Achievements

Logistics:

The Federation continues to handle air and sea freighted goods at the joint Federation/ICRC cargo receiving centre in Islamabad, with 123 flights received and more than 700 truck loads of relief goods and emergency response equipment dispatched so far. Together with PRCS, over 1,100 trucks loads of aid have been dispatched to date for distribution to earthquake survivors.

The joint logistics agreement between the Federation and ICRC will end mid-December, with the ICRC reducing activities in Islamabad and Abbottabad and concentrating its efforts in Muzzafarabad. However, the cooperation between the Federation and ICRC will continue on a case by case basis, for instance with the ICRC providing fueling and loading support for the Federation helicopter in Abbottabad. Furthermore, management of the warehouse in Mansehra, currently run by the British Red Cross ERU, will soon come directly under the Federation. After mid-January, the Federation will take over the full management and running of the warehouse from the ERU.

The contract for the Federation to rent and operate a helicopter is being finalized between the Geneva secretariat and the helicopter operator in Pakistan. One parking bay has been secured in the Abbottabad airfield through the United Nations Humanitarian Air Services (UNHAS). All 34 fleet vehicles have been insured locally and 30 drivers are now contracted to the Federation. Of the vehicles, 20 are running in Mansehra, four in Abbottabad and seven in Islamabad. The rest are awaiting transfer to other towns.

Four Norwegian Red Cross-donated M6 trucks have transported relief items including tents, blankets, tarpaulins, quilts and sleeping bags for distribution in Besham. An additional M6-truck moved one Rubb Hall (temporary warehouse) to Allai, escorted by the TSU convoy. The 62-km trip from Besham to Allai took over four hours because of poor road conditions. Eighteen M6-truck drivers have been contracted to date, including two light vehicle drivers. Additional truck drivers have been identified and will be trained and contracted as and when needed in the operation. The TSU has also employed two mechanics and one administrator and is in the process of employing a storekeeper, administrator and translator.

Donor national society logistics/procurement departments have been advised that all goods being imported via Karachi or other points of entry to Pakistan must go in transit to Islamabad where they can be customs cleared. Shipping agents need to be specifically instructed to arrange transit from Karachi Port to Islamabad, where the Federation will take over the customs formalities.

Telecom/IT:

Two VSAT units are now operational in the Mansehra office and base camp. Of the two existing BGANS, one has been designated for the Qatar Red Crescent operation in Bagh and one for the Federation's office in Besham. The traffic costs for the BGAN traffic in the operation so far is approximately CHF 40,000. The move to VSAT will thus reduce communication costs.

The MS Windows 2003 Server for backing up computer files has been set up in the Islamabad office and two additional servers have been ordered for the Mansehra office and PRCS headquarters. Workshops have been planned next week, to train Federation and PRCS staff on the installation, maintenance and administration of the server.

Hiring of radio operators is currently underway and a radio operations/duty officer/vehicle tracking system is being established, with the assistance of the fleet and security delegates. Further training of drivers and delegates will be carried out according to the Pakistan earthquake training curriculum.

Constraints

Due to programming problems HF radio transmission from vehicles travelling in remote areas has been difficult although reception has been very good. The problems will be addressed in the next few days. Technical problems have affected the use of the BGAN in Besham and the unit will be replaced in the coming days.

4. Communication – Advocacy and Public Information

Objective: The needs of the earthquake-affected population in Pakistan are advocated for and the Red Cross and Red Crescent’s interventions profiled through national and international media coverage.

Progress/Achievements

The information delegate facilitated media trips for two Swedish journalists and accompanied the Swiss Red Cross and six Swiss journalists to cover Red Cross Red Crescent activities in the field. The delegate also facilitated the visit of a BBC correspondent to Balakot and set up an interview with the Federation’s deputy head of operations. With more field visits expected in the coming weeks, a calendar is being prepared for media and donor national societies visiting Pakistan.

During the reporting period, interviews were given to Swedish National Radio, the Turkish IHA news agency and the Pakistan daily *Ummat*.

Outstanding Needs


- Response to the appeal is progressing slowly. There are contributions in the pipeline that will help coverage; however, donors are urged to continue to support the appeal. Cash contributions are still needed to allow the Red Cross and Red Crescent to fully mobilize its emergency operations and to remain flexible to changing needs as we move into winter.
- The detailed mobilization table is available and updated on [Disaster Management Information System \(DMIS\)](#). The Federation is still working on mobilizing specific relief items to respond to developing needs and it is important that donors coordinate with the Secretariat’s logistics department in Geneva regarding outstanding needs. Where possible, relief items are being procured locally.
- The following longer-term positions need to be sought internationally and regionally: head of support services, programme coordinator, liaison delegate, IT/telecommunication coordinator, health delegates, general surgeon, operating theatre and surgical ward nurses, and an additional water and sanitation delegate.

[Contributions list below; click here to return to the title page.](#)



Pakistan: Earthquake

Situation map
 Issued 25 November 2005

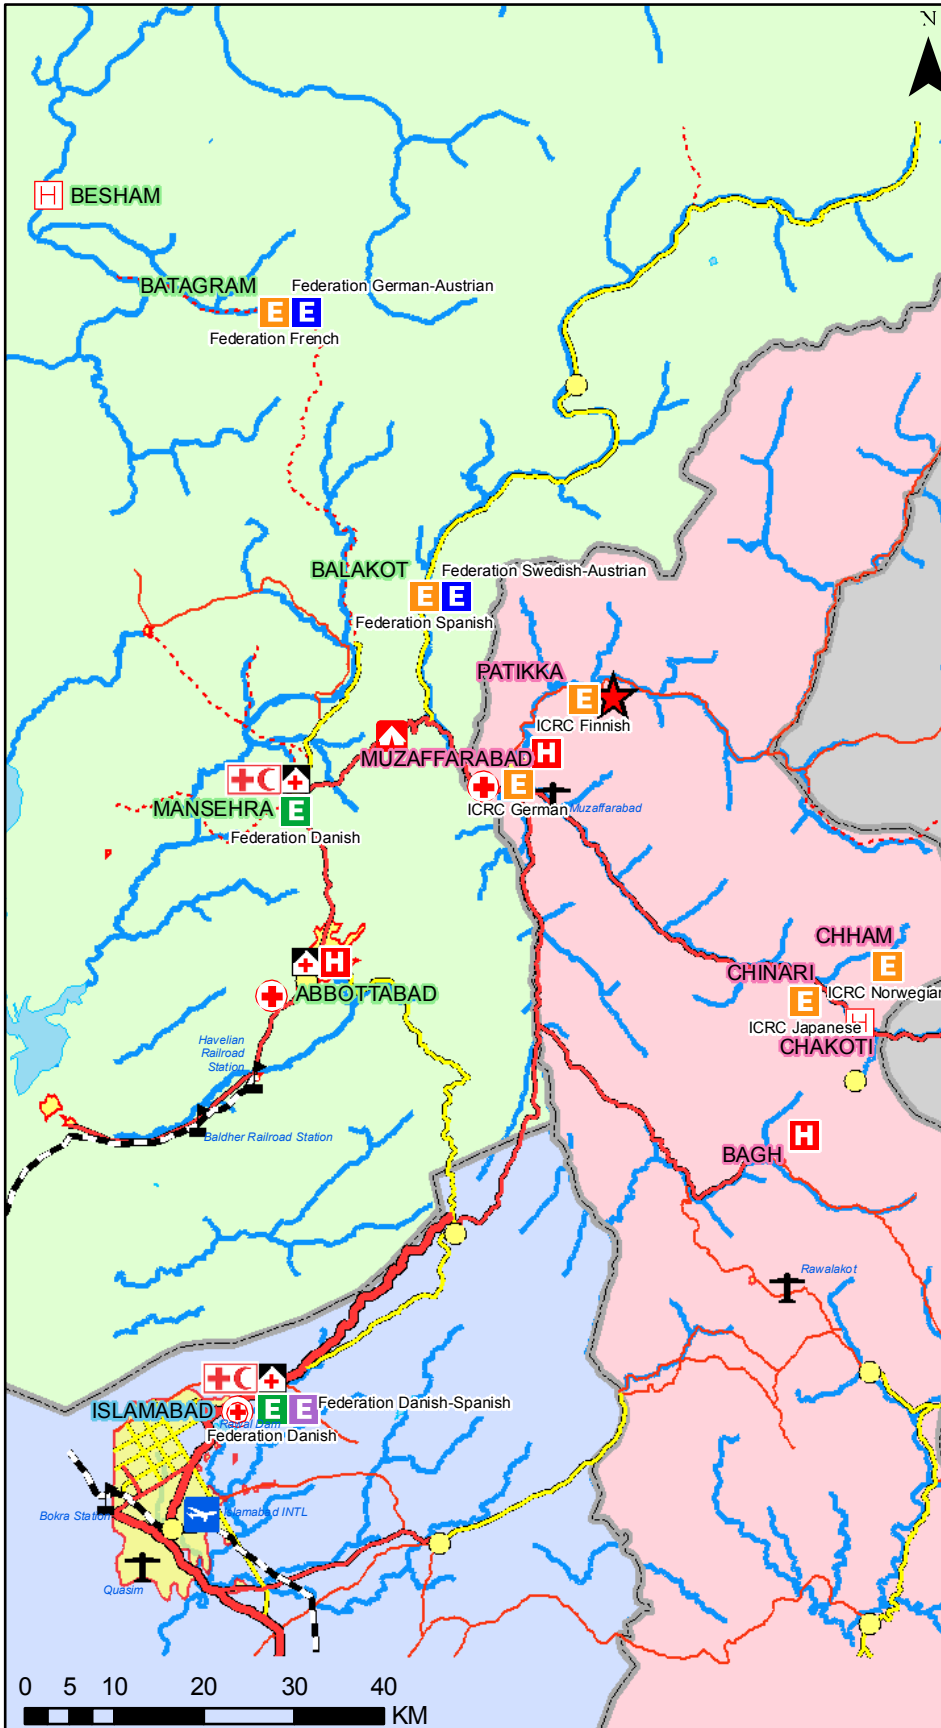

- Earthquake epicenter
- Federation delegation or hub
- Delegation
- Sub-delegation
- Federation and/or ICRC logistics center
- Emergency Response Unit (ERU)**
 - Basic Health Care (BHC)
 - IT/Telecom
 - Logistics
 - Water & Sanitation (WATSAN)
 - Federation base camp (provided by Danish RC)
 - Hospital
 - PRCS Basic Health Unit (BHU)
- Provinces**
 - Indian Jammu & Kashmir
 - North-west Frontier
 - Pakistan-administered Kashmir
 - Punjab
- Administrative boundaries
- Capital
- City
- City extension
- Railroads
- Highway, Hard, All weather
- Main road, Hard, All weather
- Secondary road, Loose, All weather
- Local road, Loose, Dry weather
- Track, Loose, Dry weather
- Airport
- Airfield
- railroad station
- Main rivers
- Lakes

The maps used do not imply the expression of any opinion on the part of the International Federation of Red Cross and Red Crescent Societies or National Societies or the ICRC concerning the legal status of a territory or of its authorities.

Map data sources: ESRI, Keyobs, Federation, ICRC

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

07/12/2005

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
-------	----------	----------	------	-----------	------	---------

CASH

REQUESTED IN APPEAL CHF ----->				152,033,929	TOTAL COVERAGE 63.3%	
ADC FOUNDATION		10,000	USD	12,805	31.10.05	
AMERICAN - RC		850,000	USD	1,099,900	17.10.05	
AMERICAN - RC		1,000,000	USD	1,280,500	01.11.05	
AMERICAN - PRIVATE DONORS				62,329	25.10.05	
AUSTRALIAN - GOVT		3,000,000	AUD	2,956,500	10.10.05	TENTS, BLANKETS, TARPAULINS, KITCHEN SETS, AIRFREIGHT
AUSTRALIAN - RC		500,000	AUD	480,500	19.10.05	MEDICAL SUPPLIES, VACCINES, CHOLERA KITS
AUSTRALIAN - RC		500,000	AUD	480,500	25.10.05	NEW EMERGENCY HEALTH KITS
AUSTRALIAN - RC				300,000	15.11.05	56 NEW EMERGENCY HEALTH KITS
BRITISH - RC		250,000	GBP	569,500	09.10.05	
BRITISH - GOVT/DIFD		1,470,588	GBP	3,344,117	27.10.05	
BRITISH - RC		250,000	GBP	568,500	17.11.05	
BRITISH - GOVT/DEC		214,663	GBP	488,143	18.11.05	PROCUREMENT OF STOVES
BRITISH - GOVT/DEC		1,331,250	GBP	3,027,263	18.11.05	PROCUREMENT OF HYGIENE KITS
BRITISH - GOVT/DEC		692,250	GBP	1,574,176	18.11.05	PROCUREMENT OF SHELTER KITS
BRITISH - PRIVATE DONORS				2,786	03.11.05	
BRITISH PETROLEUM		500,000	USD	647,000	11.10.05	
CAMBODIAN - RC		15,000	USD	19,410	13.10.05	
CANADIAN - GOVT/CIDA/HAPS		990,000	CAD	1,093,455	13.10.05	
CANADIAN - GOVT/CIDA/HAPS		99,000	CAD	109,346	18.10.05	
CANADIAN - RC		1,000,000	CAD	1,088,200	19.10.05	PROCUREMENT 1300 WINTERISED TENTS
CANADIAN - RC		1,000,000	CAD	1,088,200	02.11.05	
CANADIAN - GOVT CIDA/HAPS		990,000	CAD	1,077,318	09.11.05	
CHINA - HONG KONG RC BRANCH		500,000	HKD	83,100	10.10.05	PROCUREMENT SHELTER KITS
CHINA - HONG KONG RC BRANCH		4,000,000	HKD	679,600	29.11.05	
CHINA - MACAU - RC BRANCH				25,000	10.10.05	PURCHASE OF MEDICINES, BLANKETS & TENTS
CROATIAN - RC		20,000	EUR	30,950	30.11.05	
CYPRUS - RC				13,354	12.10.05	
CZECH - RC		10,000	USD	12,940	25.10.05	
DANISH - RC				95,920	14.10.05	
DANISH - RC				492,769	20.10.05	
DANISH - RC				294,069	16.11.05	
DANISH - GOVT				196,842	28.11.05	
ECHO (05004)		810,747	EUR	1,262,333	13.10.05	
FINNISH - PRIVATE DONORS		700	EUR	1,083	12.10.05	
FRENCH - RC		400,000	EUR	618,200	07.11.05	
FRENCH - PRIVATE DONORS				467	21.10.05	
GERMAN - RC		500,000	EUR	778,500	27.10.05	
GERMAN - RC		500,000	EUR	772,750	21.11.05	PURCHASE WINTERISED TENTS
GERMAN - PRIVATE DONORS				148	18.10.05	
HELLENIC - RC				50,000	11.10.05	PURCHASE 10'000 BLANKETS
ICELANDIC - GOVT		75,000	USD	97,050	09.10.05	

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

07/12/2005

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
ICELANDIC - RC		17,000,000	ISK	357,000	14.11.05	
INDONESIA - PRIVATE DONOR				128	28.10.05	
IRISH - GOVT		300,000	EUR	467,100	13.10.05	
IRISH - GOVT		350,000	EUR	540,925	28.10.05	
IRISH - RC		100,000	EUR	154,550	16.11.05	
IRISH - RC		500,000	EUR	772,750	25.11.05	PROCUREMENT OF HYGIENE KITS
ITALIAN - GOVT		200,000	EUR	311,400	17.10.05	
ITALIAN - RC		150,000	EUR	231,825	10.10.05	+ FOR INDIA, EUR 50'000 (DM , see AA047), FOR RELIEF SUPPLIES
JAPANESE - RC		262,513	USD	339,692	11.10.05	
JAPANESE -RC		2,800,000	USD	3,585,400	25.10.05	PROCUREMENT OF 10000 FAMILY TENTS, 10000 KEROSENE LAMPS, 10000 KEROSENE STOVE, 50000 BLANKETS
JAPANESE - RC		150,000,000	JPY	1,662,000	09.11.05	
KOREA, REPUBLIC - RC		50,000	USD	64,700	10.10.05	
LATVIAN - GOVT		100,000	USD	129,400	13.10.05	
LIBYAN - RC				10,000	10.10.05	
LICHTENSTEIN - PRIVATE DONOR				300,000	28.10.05	
LUXEMBOURG - GOVT		200,000	EUR	311,400	24.10.05	
MACEDONIA, FYR - RC		3,000	EUR	4,671	28.10.05	
MONACO - RC		30,000	EUR	46,710	17.10.05	
NETHERLANDS - GOVT		160,428	EUR	247,941	13.10.05	
NETHERLANDS - RC		213,904	EUR	330,588	03.11.05	
NETHERLANDS - RC		534,759	EUR	826,471	10.11.05	
NETHERLANDS - PRIVATE DONORS				825	28.10.05	
NEW ZEALAND - RC		100,000	NZD	89,600	20.10.05	
NEW ZEALAND - GOVT		400,000	NZD	358,400	25.10.05	
NORWEGIAN - GOVT/RC		10,000,000	NOK	1,975,000	09.11.05	RELIEF ACTIVITIES INCL. CHILDREN & VULNERABLE GROUPS
NORWEGIAN - GOVT/RC		5,500,550	NOK	1,086,359	09.11.05	
OPEC FUND F.INTERNATIONAL DEV.		600,000	USD	768,300	13.10.05	+ INDIA (DM, 05AA047) AND AFGHANISTAN (DM, 05AA045), USD 200'000 EACH FOR RELIEF SUPPLIES
PHILIP MORRIS		30,000	USD	38,415	24.10.05	
PHILIPPINES - RC		10,000	USD	12,805	03.11.05	
POLAND - PRIVATE DONORS				3,235	17.10.05	
PRIVATE DONORS ON LINE				369,748	17.11.05	
SAUDI ARABIA - PRIVATE DONOR		10,344	USD	13,245	16.11.05	
SINGAPORE - GOVT & RC				100,000	26.10.05	PROCUREMENT OF RELIEF ITEMS
SINGAPORE - GOVT & RC				100,000	09.11.05	PROCUREMENT EMERGENCY RELIEF & MEDICAL
SINGAPORE - PRIVATE DONOR		50,000	EUR	77,850	11.10.05	
SLOVENIAN - GOVT		14,981	EUR	23,153	17.11.05	

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

07/12/2005

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
SOUTH AFRICA - PRIVATE DONOR		1,000	USD	1,280	27.10.05	
SPANISH - PRIVATE DONORS				4,467	14.11.05	
SWEDISH - GOVT through RC		2,000,000	SEK	334,000	11.10.05	
SWEDISH - GOVT through RC & RC		15,400,000	SEK	2,571,800	14.10.05	
SWEDISH - RC		25,000,000	SEK	4,050,000	08.11.05	
SWISS - RC				100,000	28.11.05	
SWISS - PRIVATE DONORS				14,800	12.10.05	
UNITED ARAB EMIRATES -RC		10,000	USD	12,805	01.11.05	
USA - COCA-COLA		1,000,000	USD	1,294,000	11.10.05	
WHO STAFF- VERF				4,000	09.11.05	
SUB/TOTAL RECEIVED IN CASH				50,974,261	CHF	33.5%

KIND AND SERVICES (INCLUDING PERSONNEL)

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
in kind list updated					07.12.05	
AMERICAN - RC				3,717,570		28000 BUCKETS, 70000 BLANKETS , 3000 TARPULINS, 5000 FAMILY TENTS, 18000 KITCHEN SETS, 1000 WINTERISED FAMILY TENTS, 18000 HYGIENIC PARCELS, 2000 TENTS GAMMAX, 92900 BLANKETS QUILTS, 1 HELICOPTER ACMI LEASE
AUSTRIAN - RC				824,000		21000 HYGIENIC PARCELS, 7 EMERGENCY HEALTH KITS, 300 FAMILY TENTS, 76000 BLANKETS,
AUSTRIAN - RC				463,650		ERU WATER TREATMENT & SUPPLY LINE, PERSONNEL
BELGIAN - RC/FL				1,320,816		60000 BEDSHEET, 11720 BLANKETS, 45000 BLANKETS QUILT, 20060 JERRYCANS, 1525 WINTERISED FAMILY TENTS, 3500 KITCHEN SETS,
BELGIAN - RC/FR				401,850		12500 BLANKETS, 1250 KITCHEN SETS, 1478 FAMILY TENTS, 1250 TARPULINS
BRITISH - RC				3,602,650		600 KITCHEN SETS, 6000 WINTERISED FAMILY TENTS, 2000 JERRYCANS 10L., 17850 JERRYCANS 20L., 504000 WATER PURIFICATION TABLETS, 25000 HURRICANE LAMPS, 600 FAMILY TENTS, 41300 TARPULINS 4X6M, 300 TARPULINS 4X60M., 21700 BLANKETS, 50 KITS TAPSTAND & PIPEWORK WAT/SAN
CANADIAN - RC				2,578,516		3000 WINTERISED FAMILY TENTS, 2000 GAMMAX TENTS, 3300 BLANKETS HIGH LOFT, 12000 BLANKETS 80%, 5 EMERGENCY HEALTH KITS, 94 SHEETING TARPULINS, 11000 TARPULINS

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

07/12/2005

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
DANISH - RC				685,320		1, BASE CAMP, 30 EMERGENCY HEALTH KITS, 50 DELEGATE HEALTH KITS, 6000 KITCHEN SETS, 9000 TARPAULINS
DANISH - RC				563,850		ERU TELECOM & LOGISTICS UNITS
EGYPTIAN - RC				14,000		2000 BLANKETS, 20 FAMILY TENTS
FINNISH - RC				2,893,900		10'000 KEROSENE STOVES, 5500 HURRICANE LAMPS, 59 DOUBLE FLY TENTS, 6357 WINTERISED FAMILY TENTS
FRENCH - RC				299,004		2856 KITCHEN SETS, 13940 JERRYCANS, 1440 HURRICANE LAMPS, 15000 SHAWLS, 2300 TARPAULINS
FRENCH - RC				415,580		ERU BASIC HEALTH CARE UNIT (ECHO FUNDED)
GERMAN - RC				778,000		ERU SPECIALISED WATSAN MODULE (ECHO FUNDED)
GERMAN - RC				2,500,000		10000 SLEEPING BAGS, 30000 TARPAULINS, 10000 HURRICANE LAMPS, 10000 BLANKETS, 4000 WINTERISED FAMILY TENTS, 200 HOSPITAL BEDS,
IRISH - RC				936,500		7300 BLANKETS, 2250 WINTERISED FAMILY TENTS
LUXEMBURG - RC				116,000		6000 BLANKETS, 10 EMERGENCY HEALTH KITS
NEPAL - RC				5,000		1000 BLANKETS
NETHERLANDS - RC				4,268,746		573 FAMILY TENTS, 27 EMERGENCY HEALTH KITS, 20000 TARPAULINS, 51516 BLANKETS 80 %, 30000 BLANKETS 50%, 7000 KEROSENE HEATERS, 182900 BEDSHEETS, 72000 BLANKETS QUILTS, 45000 HYGIENIC PARCELS, 2427 WINTERISED TENTS, 16000 KITCHEN SETS.
NORWEGIAN - RC				2,296,133		11320 BLANKETS, 3 CHOLERA KITS, 1 LABORATORY MODULE, VARIOUS MEDICAL ITEMS, 4655 SLEEPING BAGS, 95 SURGICAL SUPPLY KITS, 1 MOTHER AND CHILD CARE MODULE, 1620 TARPAULINS, 5 TENT ALFA, 27 TENTS DELTA, 120 TENTS GAMMAX, 21 TENTS 90M2, 50 FAMILY TENTS 16M2, 8 TENTS WAREHOUSE, 40 TRUCKS M6, 4 WATER PURIFICATION UNITS, 2 WATERTANKS 10M3, 2 WATERTANK 5M3, 1 X-RAY MODULE
NORWEGIAN - RC				730,000		ERU REFERRAL HOSPITAL

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

07/12/2005

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
QATAR - RC				3,039,272		20000 AMOXYCILLIN, 6299 FAMILY TENTS, 1170 BEDS RIGID FRAME, 6582 BEDSHEETS, 46396 BLANKETS QUILT, 48480 BLANKETS 80%, 2200 BODY BAGS , 700 BUCKETS, 55072 HYGIENIC PARCELS, 2000 JERRYCANS 10L, 1200 JERRYCANS 20 L., 40 FIRST AID KITS FOR CAR, 1001 KITCHEN SETS, 300 HURRICANE LAMPS, 925 SHAWLS, 92 VARIOUS MEDICINE, DATES, LENTILS, ASSORTED FOOD
SINGAPORE - RC				52,340		13900 FOOD RATION MRS,
SLOVENIAN - RC				463,650		5 MEDICAL ITEMS VARIOUS, 10000 SLEEPING BAGS
SPANISH - RC				119,225		8125 BLANKETS, 504 SLEEPING BAGS, 2400 TARPAULINS, 150 FAMILY TENTS
SPANISH - RC				415,580		1 ERU BASIC HEALTH CARE UNIT (ECHO FUNDED)
SWEDISH - RC				593,220		ERU WAT-SAN, MASS SANITATION MODULE UNIT
SWEDISH - RC				230,448		904 WINTERISED TENTS, 3000 SLEEPING BAGS
SWISS - RC				1,185,373		9485 AMOXYCILLIN, 4500 TARPAULINS, 200 FAMILY TENTS, 2 EMERGENCY HEALTH KITS, 6140 BLANKETS, 80%, 20000 BLANKETS 50%, 1562 KEROSENE HEATERS, 2500 KITCHEN SETS, 2000 WINTERISED TENTS
VARIOUS DONORS	DELEGATES	12		144,000	12.10.05	
VARIOUS DONORS				9,555,421		ESTIMATED INTERNATIONAL TRANSPORT/INSURANCE COSTS (30% OF TOTAL VALUE OF RELIEF ITEMS)
SUB/TOTAL RECEIVED IN KIND/SERVICES				45,209,614	CHF	29.7%

ADDITIONAL TO APPEAL BUDGET

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
SUB/TOTAL RECEIVED				0	CHF	
