

# OPERATIONS UPDATE



International Federation of Red Cross and Red Crescent Societies  
Fédération Internationale des Sociétés de la Croix-Rouge et du Croissant-Rouge  
Federación Internacional de Sociedades de la Cruz Roja y de la Media Luna Roja  
الاتحاد الدولي لجمعيات الصليب الأحمر والهلال الأحمر

## PAKISTAN: EARTHQUAKE

1 February 2006

The Federation's mission is to improve the lives of vulnerable people by mobilizing the power of humanity. It is the world's largest humanitarian organization and its millions of volunteers are active in over 183 countries.

### In Brief

Appeal No. 05EA022; Operations Update no. 22; Period covered: 5-26 January 2006; Appeal coverage: 78.9%;

[<click here to go directly to the attached Contributions List, also available on the public website>](#)

[<click here to link directly to the map>](#)

#### Appeal history:

- Preliminary Emergency Appeal (launched as South Asia: Earthquake) on 9 October 2005 for CHF 10.8 million (USD 8.4 million or EUR 7 million) for four months to assist 30,000 families (some 120,000 beneficiaries).
- Operations Update No. 3 of 12 October 2005 increased the Preliminary Appeal budget to CHF 73,262,000 (USD 56,616,692 or EUR 47,053,307) to assist up to 150,000 families (some 750,000 beneficiaries) for six months, as an increasingly serious situation has unfolded.
- Operations Update No. 5 of 17 October 2005 revised down the number of targeted families to 70,000 (some 500,000 beneficiaries), based on the newly assessed delivery capacity and average family size of seven.
- Revised Emergency Appeal launched on 25 October 2005 for CHF 152 million (USD 117 million or EUR 98 million) to assist 81,000 families (some 570,000 beneficiaries) for six months.
- Disaster Relief Emergency Funds (DREF) allocated: CHF 200,000.

Outstanding needs: CHF 32,076,917; to date over CHF 119 million has been received, of which over CHF 66 million is in cash and over 53 million is in-kind contributions. More pledges are in the pipeline and will be reflected in the next operations update; updates are now being issued on a weekly basis. Additional support – particularly in cash – is still urgently needed.

Related Emergency or Annual Appeals: [South Asia Regional Annual Appeal 05AA051](#)

**Operational Summary:** The Federation and Pakistan Red Crescent Society (PRCS) scaled up relief operations in the remote and difficult to reach areas of Kohistan and the Allai Valley in northern Pakistan has managed to deliver assistance to target number of beneficiaries highlighted in the appeal. However, the teams, including some 100 PRCS volunteers and transportation (commercial trucks, Norwegian Red Cross M6 trucks and helicopters), are still working hard to deliver shelter materials and other non-food items to 25,000 quake-affected families before the onset of heavy snows. These teams are also working hard to identify any gaps or other urgent unmet needs and are currently replacing any remaining summer tents with winterized tents.

The health programme has expanded services beyond Balakot, Besham, Garhi Habibullah and Batagram with mobile health teams reaching communities in remote Shangla district. To date, over 183,255 people have received health services from the Federation, Pakistan Red Crescent Society (PRCS) and other Red Cross / Red Crescent partners in country. Scaling up of the health programme will include increased

immunisation coverage, in cooperation with the Ministry of Health and with the PRCS. The Federation's transport support unit continues to truck water to distribution points in and around Balakot and Batagram, helping the Swedish/Austrian and German/Austrian water sanitation ERUs deliver water to communities in those areas. Further assessments have been carried out to look at the urgent hygiene and sanitation needs in affected areas. For both health and water and sanitation, a key issue for the coming weeks will be planning for the handover of the Emergency Response Units (ERUs) and hospital facilities.

*For further information specifically related to this operation please contact:*

- *In Islamabad: Khalid Kibriya (Secretary-General), Pakistan Red Crescent Society; email: [hilal@isb.comsats.net.pk](mailto:hilal@isb.comsats.net.pk), Phone: +92.51.925.0404; Fax: +92.51.925.0408*
- *In Islamabad: Azmat Ulla (Head of Delegation); email: [azmat.ulla@ifrc.org](mailto:azmat.ulla@ifrc.org); Phone: +92.300.850.3317; Fax: +92.51.443.0745; Ted Itani (Deputy Head of Operations); email: [pakistanEODeputyHoO@ifrc.org](mailto:pakistanEODeputyHoO@ifrc.org); Mobile: +92.302.561.2191 (Pakistan)*
- *In Geneva: Jagan Chapagain (South Asia Regional Officer), email: [jagan.chapagain@ifrc.org](mailto:jagan.chapagain@ifrc.org); Phone: +41.22.730.4316; Fax: +41.22.733.0395; Christine South (Pakistan Desk Officer); email: [christine.south@ifrc.org](mailto:christine.south@ifrc.org); Phone: +41.22.730.4529; Penny Elghady (Asia Pacific Department); email: [penny.elghady@ifrc.org](mailto:penny.elghady@ifrc.org); Phone: +41.22.730.4864.*
- *For logistics/mobilization and coordination of consignments, in-kind donations and shipping instructions please contact: Mauricio Bustamante (Logistics Department); email: [mauricio.bustamante@ifrc.org](mailto:mauricio.bustamante@ifrc.org); Phone: +41.22.730.4852; Mobile: +41.79.308.9820; Fax: +41.22.730.4906.*

*All International Federation assistance seeks to adhere to the [Code of Conduct for the International Red Cross and Red Crescent Movement and Non-Governmental Organizations \(NGOs\) in Disaster Relief](#) and is committed to the [Humanitarian Charter and Minimum Standards in Disaster Response](#) in delivering assistance to the most vulnerable. For support to or for further information concerning Federation programmes or operations in this or other countries, or for a full description of the national society profile, please access the Federation's website at <http://www.ifrc.org>*

## Background

An earthquake with a magnitude of 7.6 on the Richter scale, centred 95 km northeast of Pakistan's capital, Islamabad, struck at 08:50 local time (03:50 GMT) on 8 October 2005, with tremors felt across the region from Kabul to Delhi. The quake has decimated northern Pakistan and northern India. In Pakistan alone, enormous numbers of people have been killed and injured. More than 3.5 million people have been made homeless. The immensity of the disaster is such that it remains one of the deadliest in the region in living memory.

## Situation

During the past weeks the weather has been reasonably good and intermittent sunny dry weather has enabled the scaled up relief operation to continue as planned. However, bad weather is still a constant threat to the operation, with heavy rains during the past few days causing muddy conditions in the camps. As a result, landslides have blocked mountain roads but the Pakistan army is working hard to clear access roads as best as possible.

**Relief items being delivered.**



During the reporting period, an American missile strike on a village in the remote Waziristan region of Pakistan led to demonstrations in some of the major cities of Pakistan. This required a higher level of security alertness and some restrictions on movement in the remote areas. The Federation continues to monitor the situation and is prepared to take additional precautions.

## Operational developments

The scaled-up relief effort continues to be the main focus of the operation and it is proceeding well due to favorable weather. This has allowed the PRCS / Federation teams to reach over 81,000 families with a range of non-food items, thus meeting the original target beneficiary numbers of the appeal. Over 50,000 families have received the complete package, which includes a tent, blankets, quilts, stoves, cooking sets, hygiene parcels, collapsible jerry cans. Increasingly, shelter materials and repair kits are also being provided to families, according to clear criteria, to help them start rebuilding their own shelters.



This period has seen greater consolidation of the delegation team in both Islamabad and Mansehra, with a slow down in the high turnover of staff. One of the major challenges since the beginning of the operation has been to find suitable delegates for an extended period. People have now been identified for the majority of key positions for the coming months. The team in Mansehra has also been reinforced for this phase of the relief operation, as well as for the transition to the recovery, rehabilitation and reconstruction.

There is also a new four-person recovery team working out of the delegation in Islamabad. This team comprises experts in early recovery, shelter, livelihoods and community development. The team will carry out a series of field assessments to build on the findings of the preliminary assessments and will work closely with the PRCS to ensure coherence with the national society's own priorities and capacity. The team will also ensure links to the current and planned assessments in the health field and to the ICRC's assessment and plans for Pakistan-administrated Kashmir. The aim for the team is to prepare a draft plan of action by mid to late February to cover the extended relief and transition into the early recovery phase.

## Cooperation

### Red Cross and Red Crescent Movement

During the reporting period the PRCS, supported by the Federation, held a Partnership Meeting in Islamabad at PRCS headquarters. The meeting took place from 16 to 18 January and included a one-day field visit. The field day included a visit to Mansehra for a briefing from the operations team and a visit to Balakot to view the extent of the damage, as well as to see the Spanish Red Cross basic health care ERU and the Austrian/Swedish Red Cross water and sanitation ERU. The visit enabled participants to gain an overview of the current operation and to see first hand some of the challenges of the recovery, rehabilitation and reconstruction phase. Plans to travel to Chakoti and Muzaffarabad in Pakistan-administrated Kashmir had to be cancelled due to bad weather.

The meeting was attended by representatives from 23 partner national societies as well as from the ICRC, and representatives from the Pakistan government. Representatives from the American, Belgian (Flemish and Francophone), British, Canadian, Chinese (including Hong Kong branch), Danish, Finnish, French, German, Irish, Italian, Japanese, Korea, Kuwaiti, Netherlands, New Zealand, Norwegian, Qatari, Saudi, Swedish, Turkish Red Cross/Red Crescent societies and from the Taiwanese Red Cross organisation participated in the meeting as key supporters of the operation.

During the meeting participants gained an understanding of the priorities and capacity of the PRCS, and were able to discuss in more detail the recovery assessments and planning in the areas of shelter, livelihood and health. Participants sought clarifications and posed questions and suggestions to help move forward the planning for the mid to longer-term reconstruction and recovery phase, however, they also stressed the need to still focus on any outstanding needs in the current relief operations before the end of winter.

The Federation welcomed the constructive dialogue that was demonstrated during the meeting and is now working on pulling together the next phase of the planning. This includes:

- Working closely with PRCS to ensure cohesion between the national society's priorities and the findings of the recovery assessments;
- Next steps by the recovery team to carry out rapid assessments in the field in the coming two weeks to verify the recovery assessment findings and identify extended relief needs;
- Working closely with partner national societies to ensure joint or integrated assessments where appropriate and to identify the areas of possible engagement or support;
- Identifying the need for additional resources in both the mid and longer-term and drawing that together in a plan and budget to inform an extended appeal.

Documentation on the meeting and an update on next steps have been sent out to partner national societies following the meeting. Discussions on possible service agreements are underway between the Federation and bilateral partner national societies in the country.

The framework of the meeting also allowed PRCS and the Federation to thank the partner national societies for their major contribution to the operation so far and to appreciate the range and scale of the both the in-kind and cash contributions to the appeal that have allowed the operation to meet its targets.

### **External partners**

During the reporting period, the Federation has continued maintain links with the main interagency coordination meetings in both Islamabad and Mansehra and contact with key external actors. The new operational liaison delegate arrived in the field during the reporting period and will play a major role in maintaining and optimizing the links to the cluster system and the main external stakeholders. The Federation continued its important contribution to the ongoing information management support to the shelter cluster led by International Organization for Migration (IOM) during the period.

## **Red Cross and Red Crescent action - objectives, progress, impact**

### **1. Emergency relief (food and non-food)**

**Objective: the basic shelter and household needs of 81,000 earthquake-affected families (approximately 570,000 people) in northern Pakistan are met over the next six months, enabling them to start rebuilding their future.**

### **Progress/Achievements**

The operation has now reached the objective of providing basic shelter and household needs to 81,000 earthquake-affected families (approximately 570,000 people) in northern Pakistan. But it is clear that there is still a need for further assistance during the immediate winter period and the Federation will continue to work in the affected areas.

There will be a reduced but continuing need for RDRTs until the end of winter in order to help with unforeseen distributions and to monitor the situation of the beneficiaries. The monitoring system will be crafted in the coming

days in coordination with other sectors (health, water and sanitation and relief). RDRT members will also be critical in strengthening local capacity in the coming weeks. Currently there are 28 RDRT members on the ground. They come from a large variety of countries, including Bangladesh, Malaysia, Nepal, and Romania as well as elsewhere in Europe. The current RDRTs will be repatriated by late February. Consultations are ongoing to examine follow-on RDRT deployment for short-term support.

Consultations are also underway to begin work with the communities rather than for the communities. Field relief teams are examining simple activities that could be carried out during distributions, such as advising on the safe erection and usage of tents, or informing the beneficiaries on how to react to after-shocks. The regional DM delegate is obtaining regional CDBP materials to support this work. Instructions on the erection of tents will help in avoiding their collapse due to heavy snowfall. Summer tents used as an interim measure are currently being replaced.

The relief teams are now focused on addressing the remaining needs in the remote high altitude regions in Kohistan. This work is being achieved by using a combination of using M6 trucks and helicopters to ensure access in all weather. The Pakistan army is also working to keep access roads open in wet weather, as well as to assist in the distribution of relief goods.

The new all terrain vehicles (ATVs) from the Norwegian Red Cross have now arrived and have been deployed to the field. They will be undergoing trials in the mountainous areas around Besham and where possible will be used for relief distributions, monitoring and follow up. The purpose of the deployment is also to test the ATV capacity for use in future emergencies.

The next stage of the operation will be to monitor and revisit families to check their status and to meet any outstanding needs. At present there appears to be no major gaps in the coverage, but there are still individual pockets where relief has not reached the beneficiaries. This phase will also include the supply of 10 sheets of corrugated iron (CGI) and repair kits (shared between two families) to support shelter construction through the winter months and beyond. These goods will be supplied in cooperation with the appropriate authorities of the Government of Pakistan and in line with certain earthquake resistant criteria (e.g. concrete or aggregate floor and wooden frame). The relief teams are working to identify groups of families or communities where this support can be delivered. An additional 20,000 repair kits have already been distributed.

The last of the pipeline goods are now entering the country and will feed into ongoing distributions. This includes the additional 20,000 tents purchased by the Federation. This will supply gaps in the remote areas of Allai, Shangla and Kohistan and will also be used to continue the ongoing replacement of the earlier non-winterized tents. Discussions are ongoing in the shelter cluster regarding the need for further winterized tents in other locations and the Federation may look into supporting this need.

As the teams continue to work, they are also looking into other needs, including capacity building of the PRCS staff and volunteers working on the rolling assessments and distributions.

#### Federation relief distributions as of 31 January 2006

Location	No. of Families	Tents	Blankets	Tarpaulins	B. Sheets	Quilts
Shumlai	2,000	0	0	0	14,080	0
Battal/Chattar/Hi	8,552	710	3,540	16,646	0	30,362
Allai	7,227	581	36,715	13,110	0	16,963
Garhi Habibulah	14,058	13,102	78,807	16,821	5,430	27,778
Balakot	20,163	9,257	65,014	14,898	4,074	19,347
Batagram/Battal	8,658	8,305	56,898	9,440	140	14,948
Siran Valley	7,675	7,382	32,579	9,475	23,097	32,856
Kohistan	12,695	11,949	74,750	23,762	700	38,903
<b>TOTAL</b>	<b>81,028</b>	<b>51,286</b>	<b>348,303</b>	<b>104,152</b>	<b>47,521</b>	<b>181,157</b>

Location	S. Bags	Jerry Cans	Kitchen Sets	Hygiene Kits	Stoves	Lamps
Shumlai	0	0	2,000	0	0	0
Battal/Chattar/Hil	24	7,889	7,841	7,839	0	7,841
Allai	306	6,278	6094	5709	3,043	0
Garhi Habibullah	2,429	4,428	4,970	4,038	2,608	1,754
Balakot Air/Land	4,910	7,887	4,494	6,811	2,891	6,340
Batagram/Battal	1,747	502	1,630	1,636	1,515	70
Siran Valley	2,124	4,297	5,656	5,773	3,638	4,071
Kohistan	277	19,734	11,769	11,134	8,254	8,134
<b>TOTAL</b>	<b>11,817</b>	<b>51,015</b>	<b>44,454</b>	<b>42,940</b>	<b>21,949</b>	<b>28,210</b>

## 2. Emergency health and care

**Objective: Some 250,000 earthquake-affected people in northern Pakistan have access to appropriate quality health care, safe water and sanitation services in the next six months.**

### Progress/Achievements

The health programme is continuing to provide ongoing health care to those in need. Since the start of the operation 173,857 patients have been seen by Federation, PRCS and other Red Cross / Red Crescent partners. In the health area a key issue for the coming weeks is planning for the handover of the ERU and hospital facilities.

As part of this process, the Abbottabad field hospital is working on its plan to hand over the facility, in part to the Ayub Medical Centre (AMC) once the staff of the AMC have been trained in its use and the remaining patients have been discharged. The hospital has been functional since 26 October and has admitted 260 patients and performed 205 operations. The average bed occupancy rate throughout the operation has been approximately 70 per cent. A small new team has just arrived on site to manage the handover process.

In Balakot, the Spanish ERU team continues to provide health care to the affected population. It has provided its services including medical treatment, minor surgery, health education, antenatal care and immunization to 6,122 beneficiaries to date. On average, the unit has seen around one hundred patients every day. The ERU will be in operation until early February, after which time it will be handed over to the PRCS. Mobile health units will be established in Balakot using ERU facilities as a basis for the delivery of health care to surrounding rural areas. Discussions are ongoing with the PRCS as to their management of the unit and its equipment.

The French ERU in Battagram is also continuing to provide basic health care to the population. So far 10,487 beneficiaries have received treatment in similar areas as those provided in Balakot. In addition two mobile teams provide out-reach services to inaccessible areas such as Banna in Allai, Bateela, Pachto, Reshhang in Battagram and Koshir districts. They have also begun training locally recruited health workers and one female RDRT doctor has joined the ERU to provide

**The French ERU team providing Basic Health Care to beneficiaries in Battagram.**



better medical services for women. In addition to the female doctor, two local doctors and nurses are working closely with the team. Again discussions are underway to decide how best to phase out from the ERU phase and it is planned that French Red Cross will continue to run this unit bilaterally for the coming period.

The Basic Health Units supported by PRCS and the Federation have also continued to provide services such as general medical care, minor surgical procedures, obstetrics and gynecology, pediatric medicine, orthopedics as well as dermatology. On average 300 patients are seen every day.



#### Red Cross Red Crescent health figures as of 31 January 2006

Health units	Locations	Beneficiaries
PRCS mobile health unit	Pakistan administered Kashmir (various locations)	44,037
PRCS mobile health unit	NWFP (including Balakot, Garhi Habibullah)	6,723
PRCS/Korean Red Cross mobile health	NWFP (including Mansehra base camp, Besham)	4,382
Spanish Red Cross ERU	Balakot	6,716
French Red Cross ERU	Banna Alai, Batagram, Bateela, Pachto, Rashang	11,007
RDRT/ Malaysian Red Crescent medical team	Mansehra base camp and Mang/Mountains	1,182
Federation multinational field hospital	Abbottabad	13,706
Italian Red Cross field hospital	Mansehra	686
Qatar Red Crescent	Bagh (Dholi)	14,818
Saudi Red Crescent field hospital	Mansehra	47,880
Turkish Red Crescent Society	Muzzafarabad	32,118
<b>TOTAL</b>		<b>183,255</b>

The Qatar Red Crescent 40-bed basic health unit at Upper Duly has been functioning since 20 November and has provided consultations to 11,823 beneficiaries. The team is also providing primary health services in remote areas using mobile teams. They have been proactive in ensuring good communication and coordination with the Federation.

By the third week of 2006, the Turkish Red Crescent had seen nearly 29,500 patients, of which 492 were in-patients. In addition nearly 2,000 patients were seen by their mobile clinics. This total includes 22 new admissions and 19 surgical interventions.

In Mansehra, the Saudi Red Crescent continues to run its field hospital, with 30 beds for in-patient care and operating facilities and a high dependency unit available. It also provides out patient care. To date the hospital has seen a total of 47,880 consultations. It will remain open until April 2006. The field hospital was provided with three New Emergency Health Kits by the Federation in recent weeks.

### Constraints

There is an urgent and ongoing need for female health care professionals to provide appropriate medical care for women's health needs.

### Water and Sanitation:

The work of the two water and sanitation ERUs continues to proceed on target. In Batagram, the German/Austrian ERU team is treating and storing potable waters, and is providing purified water to the surrounding camps and to the French Red Cross basic health ERU in Batagram (10,000 beneficiaries). The team is also continuing to truck and distribute 40,000 litres of water each day to surrounding communities. During the period, the team completed the restoration of the water supply to the basic health unit in Singli Paen and supported the rehabilitation of the water system in this village and some other remote villages around Batagram.

In Balakot, the Austrian/Swedish team continues to treat and produce potable water at a rate of 125,000 to 200,000 litres each day, supplying an estimated 22,000 beneficiaries.

Hygiene promotion continues to be a vital element of the water and sanitation program. Sanitation work (construction of latrines and bathrooms) continue in both ERU locations at a rate of 30 latrines per week per ERU. Hygiene kits were distributed during this week to women in different areas of Balakot, while hygiene promotion lectures on the proper usage of the kits was given by a Federation delegate based in Batagram. In total 1,714 hygiene kits were distributed, including to sixty individuals identified with scabies, and 6,020 beneficiaries received hygiene education. Two new hygiene promotion assistants have been identified in Balakot and further interviews will take place next week, to help support the hygiene promotion team.

The Federation conducted a one-day orientation workshop in Mansehra for volunteers drawn from different technical sectors, including eight from water and sanitation. Also, PRCS/Federation volunteers attended a joint (Federation, UNICEF and WHO) training on environmental health and sanitation in Batagram. The Federation provided two delegates as facilitators.

### Red Cross Red Crescent water and sanitation figures as of 22 January 2006

Location	Beneficiaries	Water in Litres (Purified on Daily Basis)	No. of Latrines
Balakot	22,000	200,000	174
Batagram	10,000	40,000	102
Maira Camp	5,000	16,000	5
<b>TOTAL</b>	<b>35000</b>	<b>256,000</b>	<b>281</b>

As with the health facilities, the main concern is to prepare the strategy and process for handing over the ERUs to the PRCS over the coming weeks. The focus is on identifying, engaging and training local staff to take over the operation and maintenance of the ERUs when they are handed over. The provision of PRCS qualified personnel and volunteers is a primary requirement to enable PNS and Federation to proceed with transition and handover and is also essential to reinforce the capacity of PRCS. In this regard, a meeting is planned to be held in Muzaffarabad next week with the chairman of the NWFP provincial branch, the German Red Cross representative, the ICRC and the Federation to discuss the handover of the German/Austrian water and sanitation ERU.

### Psycho-social programme (PSP):

During discussions last week between PRCS, the Federation and ECHO on an extension of the PSP program, all partners agreed with the Danish Red Cross proposition that the PSP programme should be linked into existing health services in the targeted areas. A project proposal for a 12 month extension will be produced in the coming weeks and submitted to ECHO for funding.

Different psycho-education materials have been developed and will be ready for distribution in the coming weeks. Furthermore brochures developed by the Turkish Red Crescent on stress management will be reprinted and used as awareness information for PRCS/DRC PSP programme.

All four teams are working on psycho-educational sessions and social activities for women and children at four camps (H-11 Islamabad, Havelian Camp, Garhi Habibullah and Maira Camp near Batagram/Besham). Supervision by Rozan (a local non governmental organisation) staff, will take place in all four areas next week. Supervision in the field will include training of volunteers.

The Turkish Red Crescent PSP teams participated in a conference on “Social Gender and Human Issues” as a panellist and made a presentation on the code of conduct for PSP support units during disasters. Some 25 teachers working in the Muzzafarabad Gojra Government Girls’ School received “staff support” training. 15 staff and 20 volunteers of PRCS working in Muzzafarabad received a briefing on PSP work from the TRCS. Training plans were made for further psychosocial first aid, staff support and community participation for PRCS staff and volunteers.

Qatar Red Crescent organized a PSP workshop to recognize psychological aspects of trauma and help the helpers in taking care of oneself in trauma. The total number of people reached was 129. The program was adapted to suit the time available and the background of the participants. All participants received certificates at the end of the programme.

### **3. Logistics/IT/Telecommunication**

**Objective: The ongoing PRCS and Federation relief operation have effective logistical, IT and telecommunication infrastructure in the operational areas.**

#### **Progress/Achievements**

##### ***IT:***

The Federation IT personnel installed a FDU docking unit for Thuraya phones, to enable their use from the radio room inside the buildings to reduce calling charges. It is cheaper to call from between Thuraya sets than from Nera (Inmarsat) to Thuraya.

The Federation is setting up a system that will send out daily security and road reports through e-mail so that the Delegation will be able to monitor the movement of Federation personnel in a more effective manner than before. This system will be operated from the radio room in Mansehra.

During Eid, the IT department visited Besham to check and fix the satellite phone (Nera), the Bgan internet connection and the computers in the Federation office. The visit was successful and everything was working properly. Because of difficult internet access during the winter due to landslides, snow and frequent problems with the landlines, the IT department recommended an upgrade of the system (to a 128 kbps Ku satellite). The department is in the process of renewing the radio frequency license for VHF and HF networks. The Federation also plans to organize training sessions for car drivers in order to properly teach them how to use the radio systems.

The Federation is waiting for customs clearance on the equipment that has been shipped from Geneva. The equipment has already arrived in Islamabad and includes VHF and HF radios as well as laptop computers.

##### ***Logistics:***

The operation is now more than three months old and is mostly on track. The received by the Federation on 14 January 2006 containing two snow mobiles, four belt wagons and 12 all terrain vehicles (ATVs), were sent from Islamabad and are now located in the TSU Workshop in Baffa and in the base camp in Batrasi. These vehicles will be insured before their trials can be started.

The release of 13 other imported vehicles from the customs is in progress. The clearing procedure for vehicles is now entirely handled by the ICRC to facilitate obtaining the “no objection certificate” (NOC) and the exemption certificate.

The future of the air operations is being discussed to determine whether the rental of the MI8 helicopter should be extended and if so for how long. Thus far the MI8 has provided excellent support to the relief operation – to the distribution of goods and the movement of staff.

Danish Logistic ERU is training new delegates and newly recruited national staff in preparation for handover before their departure on or around 10 February. The logistics department is working on shifting the warehouse facilities to Mansehra, as the warehouse in Islamabad is also to be handed over in the near future.

As a pilot, prefabricated shelters provided by the Netherlands Red Cross will be tested at different altitudes and with various communities to determine their value in the current and future relief operations. Their arrival, along with the relevant support technicians, is expected in the coming weeks.

The Federation received relief goods from a total of 191 aircrafts from various countries. It has sent 1,881 trucks of relief goods to the affected areas. The TSU has deployed 40 trucks that are being used by various components of the Movement, including the ICRC.

#### **4. Communication – Advocacy and Public Information**

**Objective: The needs of the earthquake-affected population in Pakistan are advocated for and the Red Cross and Red Crescent's interventions profiled through national and international media coverage.**

##### **Progress/Achievements**

An information pack was prepared for the partnership meeting and was distributed to all PNS representatives as well as visitors from the South Asia regional delegation (SARD)/Geneva. The pack comprised a press release, a video on the Movement's work, a power point presentation, and photographs from the field.

A Netherlands Red Cross media representative, together with a media crew visited Pakistan during the first week of January. They were given briefings in Islamabad and Mansehra. They covered the relief activities of the Federation and interviewed two Netherlands Red Cross delegates (relief/health coordinators). The Netherlands Red Cross media team is still on the ground and their trip is being facilitated by the relief coordinator.

Some 12 Turkish media members visited Pakistan to cover Turkish Red Crescent activities during Eid. They were well briefed prior to their trip to the field and were given suggested story angles. Their air transportation was also facilitated and their news pieces were published in 35 newspapers and broadcasted TV channels.

An article on PSP activities was prepared as requested by PSP teams of the Federation and Qatar Red Crescent. The article and the related photos were shared with PRCS in order to be distributed to the national media. The same article is now being used for the Federation website and the Red Cross / Red Crescent magazine as agreed with the media department.

A press release was issued on 15 January 2006 and a 15 minute video news release (VNR) was prepared and sent to the Geneva media unit. It is due to be released during the last week of January. The focus is "Red Cross speeding up efforts in Pakistan as the winter sets in". It will be distributed to APTN and other big TV channels.

The next press release will be on the all terrain vehicles (ATVs) of the Norwegian Red Cross, undergoing trials at various sites in the earthquake affected zone. The Norwegian Red Cross communications focal point has been contacted to get more information and supporting documents.

##### **Outstanding Needs**

- Response to the appeal is progressing steadily. However, donors are urged to continue to make cash contributions towards the Appeal to allow the Red Cross and Red Crescent to fully mobilize its emergency operations and to remain flexible to changing needs in the coming three months.
- The detailed mobilization table is available and updated on the Federation's [Disaster Management Information System](#) (DMIS) at page

<https://www-secure.ifrc.org/dmis/admin/logistics/docs/MobTab%20PK%20060117b.doc>. Currently, most relief items have been covered, however, new needs may come out of current assessments in the field and will be reflected in the mobilization table. It is important that donors continue to coordinate with the Secretariat's logistics department in Geneva regarding outstanding needs.

- The following longer-term positions are sought (internationally and regionally): programme coordinator and recovery coordinator.

***[Contributions list and map below; click here to return to the title page.](#)***

# Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

## PLEDGES RECEIVED

01/02/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
-------	----------	----------	------	-----------	------	---------

### CASH

REQUESTED IN APPEAL CHF ----->				152,033,929	TOTAL COVERAGE 78.9%	
AMERICAN - RC		850,000	USD	1,099,900	17.10.05	
AMERICAN - RC		1,000,000	USD	1,280,500	01.11.05	
AMERICAN - RC		362,100	USD	475,075	08.12.05	HELICOPTER OPERATIONS ONE MONT
AMERICAN - RC		1,500,000	USD	1,968,000	29.12.05	CORRUGATED IRON SHEETS
AMERICAN - RC		1,500,000	usd	1,968,000	30.01.06	
AUSTRALIAN - GOVT		3,000,000	AUD	2,956,500	10.10.05	TENTS, BLANKETS, TARPAULINS, KITCHEN SETS, AIRFREIGHT
AUSTRALIAN - RC		500,000	AUD	480,500	19.10.05	MEDICAL SUPPLIES, VACCINES, CHOLERA KITS
AUSTRALIAN - RC		500,000	AUD	480,500	25.10.05	NEW EMERGENCY HEALTH KITS
AUSTRALIAN - RC				300,000	15.11.05	56 NEW EMERGENCY HEALTH KITS
AUSTRIAN - RC		50,000	EUR	77,825	03.01.06	
AUTONOMOUS PROV. BOLSANO		50,000	EUR	77,825	08.01.06	
BRITISH - RC		250,000	GBP	569,500	09.10.05	
BRITISH - GOVT/DIFD		1,470,588	GBP	3,344,117	27.10.05	
BRITISH - RC		250,000	GBP	568,500	17.11.05	
BRITISH - GOVT/DEC		214,663	GBP	488,143	18.11.05	PROCUREMENT OF STOVES
BRITISH - GOVT/DEC		1,331,250	GBP	3,027,263	18.11.05	PROCUREMENT OF HYGIENE KITS
BRITISH - GOVT/DEC		692,250	GBP	1,574,176	18.11.05	PROCUREMENT OF SHELTER KITS
BRITISH - RC		500,000	GBP	1,129,500	20.12.05	CORRUGATED IRON
BRITISH - PRIVATE DONOR		405	GBP	918	05.01.06	
BRITISH - PRIVATE DONORS				15,857	03.11.05	
BRITISH PETROLEUM		500,000	USD	647,000	11.10.05	
BRITISH PETROLEUM FOUNDATION		75,726	USD	99,353	22.12.05	
CAMBODIAN - RC		15,000	USD	19,410	13.10.05	
CAMBODIAN - PRIVATE DONOR		100	USD	131	01.11.05	
CANADIAN - GOVT/CIDA/HAPS		990,000	CAD	1,093,455	13.10.05	
CANADIAN - GOVT/CIDA/HAPS		99,000	CAD	109,346	18.10.05	
CANADIAN - RC		1,000,000	CAD	1,088,200	19.10.05	PROCUREMENT 1300 WINTERISED TENTS
CANADIAN - RC		1,000,000	CAD	1,088,200	02.11.05	
CANADIAN - GOVT CIDA/HAPS		990,000	CAD	1,077,318	09.11.05	
CANADIAN - RC		750,000	USD	984,000	09.12.05	HELICOPTER OPERATIONS 2 MONTHS
CHINA - HONG KONG RC BRANCH		500,000	HKD	83,100	10.10.05	PROCUREMENT SHELTER KITS
CHINA - HONG KONG RC BRANCH		4,000,000	HKD	679,600	29.11.05	
CHINA - HONG KONG RC BRANCH		2,000,000	HKD	330,600	23.12.05	PURCHASE OF WINTERISED TENTS
CHINA - MACAU - RC BRANCH				25,000	10.10.05	PURCHASE OF MEDICINES, BLANKETS & TENTS
CHINA - MACAU - RC BRANCH				15,000	09.12.05	PURCHASE OF MEDICINES

# Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

## PLEDGES RECEIVED

01/02/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
CROATIAN - RC		20,000	EUR	30,950	30.11.05	
CYPRUS - RC				20,867	12.10.05	
CYPRUS - RC		25,000	USD	32,800	31.01.06	
CZECH - RC		10,000	USD	12,940	25.10.05	
DANISH - RC				95,920	14.10.05	
DANISH - GOV'T through RC				492,769	20.10.05	
DANISH - GOV'T through RC				294,069	16.11.05	
DANISH - GOV'T through RC				196,842	28.11.05	
ECHO (05004)		810,747	EUR	1,262,333	13.10.05	
ECUADORIAN - RC		5,702	USD	7,481	25.01.06	
FINNISH - PRIVATE DONORS		700	EUR	1,083	12.10.05	
FRENCH - RC		400,000	EUR	618,200	07.11.05	
FRENCH - PRIVATE DONORS				1,952	21.10.05	
GERMAN - RC		500,000	EUR	778,500	27.10.05	
GERMAN - RC		500,000	EUR	772,750	21.11.05	PURCHASE WINTERISED TENTS
GERMAN - PRIVATE DONORS				148	18.10.05	
HELLENIC - RC				50,000	11.10.05	PURCHASE 10'000 BLANKETS
ICELANDIC - GOV'T		75,000	USD	97,050	09.10.05	
ICELANDIC - RC		17,000,000	ISK	357,000	14.11.05	
INDONESIA - PRIVATE DONOR				128	28.10.05	
IRISH - GOV'T		300,000	EUR	467,100	13.10.05	
IRISH - GOV'T		350,000	EUR	540,925	28.10.05	
IRISH - RC		100,000	EUR	154,550	16.11.05	
IRISH - RC		500,000	EUR	772,750	25.11.05	PROCUREMENT OF HYGIENE KITS
IRISH - RC		350,000	EUR	541,625	13.12.05	PURCHASE WINTERISED TENTS
IRISH - RC		400,000	EUR	622,600	13.12.05	
IRISH - PRIVATE DONOR				1,035	17.01.06	
ITALIAN - GOV'T		200,000	EUR	311,400	17.10.05	
ITALIAN - RC		150,000	EUR	231,825	10.10.05	+ FOR INDIA, EUR 50'000 (DM , see AA047), FOR RELIEF SUPPLIES
JAPANESE - RC		262,513	USD	339,692	11.10.05	
JAPANESE - RC		2,800,000	USD	3,585,400	25.10.05	PROCUREMENT OF 10000 FAMILY TENTS, 10000 KEROSENE LAMPS, 10000 KEROSENE STOVE, 50000 BLANKETS
JAPANESE - RC		150,000,000	JPY	1,662,000	09.11.05	
KOREA, REPUBLIC - RC		50,000	USD	64,700	10.10.05	
LATVIAN - GOV'T		100,000	USD	129,400	13.10.05	
LIBYAN - RC				10,000	10.10.05	
LICHTENSTEIN - PRIVATE DONOR				300,000	28.10.05	
LITHUANIAN - RC				3,567	13.01.06	
LUXEMBOURG - GOV'T		200,000	EUR	311,400	24.10.05	
LUXEMBOURG - RC		40,000	EUR	61,900	21.12.05	PROCUREMENT OF CORRUGATED IRON SHEETS
MACEDONIA, FYR - RC		3,000	EUR	4,671	28.10.05	

# Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

## PLEDGES RECEIVED

01/02/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
MONACO - RC		30,000	EUR	46,710	17.10.05	
NETHERLANDS - GOVT		160,428	EUR	247,941	13.10.05	
NETHERLANDS - RC		213,904	EUR	330,588	03.11.05	
NETHERLANDS - RC		534,759	EUR	826,471	10.11.05	
NETHERLANDS - RC		855,615	EUR	1,324,064	28.11.05	
NETHERLANDS - RC		213,904	EUR	331,016	19.12.05	
NETHERLANDS - PRIVATE DONORS				825	28.10.05	
NETHERLANDS - PRIVATE DONOR				500	19.12.05	TENTS
NEW ZEALAND - RC		100,000	NZD	89,600	20.10.05	
NEW ZEALAND - GOVT		400,000	NZD	358,400	25.10.05	
NEW ZEALAND - GOVT		250,000	NZD	231,125	28.11.05	
NORWEGIAN - GOVT/RC		10,000,000	NOK	1,975,000	09.11.05	RELIEF ACTIVITIES INCL. CHILDREN & VULNERABLE GROUPS
NORWEGIAN - GOVT/RC		5,500,550	NOK	1,086,359	09.11.05	
NORWEGIAN - RC		1,748,067	NOK	339,125	15.12.05	TSU
OPEC FUND F.INTERNATIONAL DEV.		600,000	USD	768,300	13.10.05	+ INDIA (DM, 05AA047) AND AFGHANISTAN (DM, 05AA045), USD 200'000 EACH FOR RELIEF SUPPLIES
PHILIP MORRIS		30,000	USD	38,415	24.10.05	
PHILIPPINES - RC		10,000	USD	12,805	03.11.05	
POLAND - PRIVATE DONORS				3,235	17.10.05	
PRIVATE DONORS ON LINE				421,403	17.11.05	
PRIVATE DONORS ON LINE				4,117	26.01.06	
SAUDI ARABIA - PRIVATE DONOR		10,344	USD	13,245	16.11.05	
SINGAPORE - GOVT & RC				100,000	26.10.05	PROCUREMENT OF RELIEF ITEMS
SINGAPORE - GOVT & RC				100,000	09.11.05	PROCUREMENT EMERGENCY RELIEF & MEDICAL
SINGAPORE - PRIVATE DONOR		50,000	EUR	77,850	11.10.05	
SLOVENIAN - GOVT		14,981	EUR	23,153	17.11.05	
SLOVENIAN - GOVT		27,737	EUR	42,924	07.12.05	
SOUTH AFRICA - PRIVATE DONOR		1,000	USD	1,280	27.10.05	
SPANISH - PRIVATE DONORS				4,467	14.11.05	
SWEDISH - GOVT through RC		2,000,000	SEK	334,000	11.10.05	
SWEDISH - GOVT through RC & RC		15,400,000	SEK	2,571,800	14.10.05	
SWEDISH - RC		25,000,000	SEK	4,050,000	08.11.05	
SWEDISH - RC		20,000,000	SEK	3,250,000	15.12.05	
SWISS - RC				100,000	28.11.05	
SWISS - PRIVATE DONORS				14,850	12.10.05	
SWISS - PRIVATE DONOR				25,000	09.12.05	
TAIWAN RED CROSS ORGANISATION		59,000	USD	77,408	05.12.05	PROCUREMENT OF MEDICAL SUPPLIES
TRINIDAD & TOBAGO - RC				3,370	30.12.05	
UNITED ARAB EMIRATES -RC		10,000	USD	12,805	01.11.05	
USA - COCA-COLA		1,000,000	USD	1,294,000	11.10.05	
SWISS WHO/VERF STAFF				4,000	09.11.05	

# Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

## PLEDGES RECEIVED

01/02/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
USA - ADC FOUNDATION		10,000	USD	12,805	31.10.05	
USA - ALTRIA KRAFT		50,000	USD	65,600	15.12.05	
USA - APPLIED MATERIALS		34,684	USD	45,505	15.12.05	
USA - EMC		36,000	USD	47,232	15.12.05	
USA - ENTERPRISE FOUNDATION		250,000	USD	328,000	15.12.05	
USA - HARRIS FOUNDATION		100,000	USD	131,200	15.12.05	
USA - INTEL FOUNDATION		500,000	USD	656,000	15.12.05	
USA - LEHMAN BROTHERS		165,279	USD	216,846	15.12.05	
USA - PRIVATE DONORS				86,289	25.10.05	
USA - PRIVATE DONORS		1,276	USD	1,674	09.12.05	
USA - SAMYATEX		2,500	USD	3,280	15.12.05	
SUB/TOTAL RECEIVED IN CASH				66,593,216	CHF	43.8%

## IN-KIND AND SERVICES

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
in kind list updated					31.1.06	
AMERICAN - RC				5,669,973		30518 BEDSHEETS, 28000 BUCKETS, 70000 BLANKETS, 3000 TARPULINS, 5000 FAMILY TENTS, 18000 KITCHEN SETS, 3200 WINTERISED FAMILY TENTS, 18000 HYGIENIC PARCELS, 50000 SHAWLS, 2000 TENTS GAMMAX, 152900 BLANKETS QUILTS, SHIPPING/TRANSPORT
AUSTRIAN - RC				2,019,212		21000 HYGIENIC PARCELS, 7 EMERGENCY HEALTH KITS, 300 FAMILY TENTS, 1800 WINTERISED FAMILY TENTS, 76000 BLANKETS, 18000 BLANKETS QUILT, SHIPPING/TRANSPORT
AUSTRIAN - RC				463,650		ERU WATER TREATMENT & SUPPLY LINE, PERSONNEL
BELGIAN - RC/FL				3,251,428		60000 BEDSHEET, 11720 BLANKETS, 95305 BLANKETS QUILT, 20060 JERRYCANS, 2275 WINTERISED FAMILY TENTS, 3500 KITCHEN SETS, 20000 CORRUGATED IRON SHEET, SHIPPING/TRANSPORT
BELGIAN - RC/FR				546,759		12500 BLANKETS, 1250 KITCHEN SETS, 1552 FAMILY TENTS, 1250 TARPULINS, SHIPPING/TRANSPORT
BRITISH - RC				2,755,426		600 KITCHEN SETS, 6000 WINTERISED FAMILY TENTS, 2000 JERRYCANS 10L., 20060 JERRYCANS 20L., 504000 WATER PURIFICATION TABLETS, 25000 HURRICANE LAMPS, 600 FAMILY TENTS, 41300 TARPULINS 4X6M, 300 TARPULINS 4X60M., 21700 BLANKETS, 50 KITS TAPSTAND & PIPEWORK WAT/SAN

# Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

## PLEDGES RECEIVED

01/02/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
CANADIAN - RC				3,585,575		3000 WINTERISED FAMILY TENTS, 2000 GAMMAX TENTS, 3300 BLANKETS HIGH LOFT, 12000 BLANKETS 80%, 5 EMERGENCY HEALTH KITS, 94 SHEETING TARPULINS, 11000 TARPULINS, TRANSPORT/SHIPPING
DANISH - RC				1,025,320		1.5, BASE CAMP, 30 EMERGENCY HEALTH KITS, 50 DELEGATE HEALTH KITS, 8000 KITCHEN SETS , 9000 TARPULINS, 750 WINTERISED FAMILY TENTS
DANISH - RC				563,850		ERU TELECOM & LOGISTICS UNITS
EGYPTIAN - RC				78,716		2000 BLANKETS, 20 FAMILY TENTS , TRANSPORT/SHIPPING
FINNISH - RC				3,871,778		10000 KEROSENE STOVES, 5500 HURRICANE LAMPS, 6607 WINTERISED FAMILY TENTS, 10000 CORRUGATED IRON SHEET, TRANSPORT/SHIPPING
FRENCH - RC				582,247		4791 KITCHEN SETS, 20910 JERRYCANS, 1440 HURRICANE LAMPS, 15000 SHAWLS, 2300 TARPULINS, TRANSPORT/ SHIPPING
FRENCH - RC				261,791		ERU BASIC HEALTH CARE UNIT (ECHO FUNDED)
GERMAN - RC				787,278		ERU SPECIALISED WATSAN MODULE (ECHO FUNDED)
GERMAN - RC				5,906,761		10000 SLEEPING BAGS, 30000 TARPULINS, 10000 HURRICANE LAMPS, 10000 BLANKETS, 8000 WINTERISED FAMILY TENTS, 200 HOSPITAL BEDS, 1 MOBILE KITCHEN, TRANSPORT/SHIPPING
IRISH - RC				936,500		7300 BLANKETS, 2250 WINTERISED FAMILY TENTS
LUXEMBURG - RC				215,594		6000 BLANKETS, 10 EMERGENCY HEALTH KITS,
NEPAL - RC				5,000		1000 BLANKETS
NETHERLANDS - RC				4,757,846		573 FAMILY TENTS, 27 EMERGENCY HEALTH KITS, 20000 TARPULINS, 51516 BLANKETS 80 %, 30000 BLANKETS 50%, 7000 KEROSENE HEATERS, 182900 BEDSHEETS, 72000 BLANKETS QUILTS, 45000 HYGIENIC PARCELS, 2427 WINTERISED TENTS, 16000 KITCHEN SETS, 10 SUPPL.UNITS OF NEHK,

# Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

## PLEDGES RECEIVED

01/02/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
NORWEGIAN - RC				2,902,452		11320 BLANKETS, 1 DIATHERMY, 2 DOCTORS OFFICE MODULES, 9 HEATERS, 3 CHOLERA KITS, 1 LABORATORY MODULE, VARIOUS MEDICAL ITEMS, 2 PROPAC ECG MONITORS, 7355 SLEEPING BAGS, 95 SURGICAL SUPPLY KITS, 2 MOTHER AND CHILD CARE MODULE, 1620 TARPULINS, 5 TENTS ALFA, 29 TENTS DELTA, 870 TENTS GAMMAX 24M2, 21 TENTS 90M2, 50 FAMILY TENTS 16M2, 8 TENTS WAREHOUSE, 40 TRUCKS M6, 4 WATER PURIFICATION UNITS, 2 WATERTANKS 10M3, 2 WATERTANK 5M3, 1 X-RAY MODULE
NORWEGIAN - RC				730,000		ERU REFERRAL HOSPITAL
QATAR - RC				2,312,371		20000 AMOXYCILLIN, 6158 FAMILY TENTS, 1170 BEDS RIGID FRAME, 6582 BEDSHEETS, 34881 BLANKETS QUILT, 45960 BLANKETS 50%, 2200 BODY BAGS, 700 BUCKETS, 44 GENERATORS, 12569 HYGIENIC PARCELS, 1998 JERRYCANS 10L, 1200 JERRYCANS 20 L., 40 FIRST AID KITS FOR CAR, 1001 KITCHEN SETS, 300 HURRICANE LAMPS, 925 SHAWLS, 92 VARIOUS MEDICINE, DATES, LENTILS, ASSORTED FOOD
SINGAPORE - RC				1,123,621		13900 FOOD RATION MRS, SHIPPING/TRANSPORT
SLOVENIAN - RC				404,690		5 MEDICAL ITEMS VARIOUS, 10000 SLEEPING BAGS
SPANISH - RC				119,225		8125 BLANKETS, 504 SLEEPING BAGS, 2400 TARPULINS, 150 FAMILY TENTS
SPANISH - RC				415,580		1 ERU BASIC HEALTH CARE UNIT (ECHO FUNDED)
SWEDISH - RC				593,220		ERU WAT-SAN, MASS SANITATION MODULE UNIT
SWEDISH - RC				303,442		904 WINTERISED TENTS, 3000 SLEEPING BAGS, TRANSPORT/ SHIPPING
SWISS - RC				2,681,514		4000 AMOXYCILLIN, 40000 BEDSHEETS, 4500 TARPULINS, 200 FAMILY TENTS, 2 EMERGENCY HEALTH KITS, 12500 BLANKETS QUILT, 6140 BLANKETS, 80%, 20000 BLANKETS 50%, 1562 KEROSENE HEATERS, 2500 KITCHEN SETS, 10000 SHAWLS, 18000 CORRUGATED IRON SHEETS, 2000 WINTERISED TENTS, TRANSPORT/SHIPPING
SWEDEN	DELEGATES			37,200		
SWISS RC	DELEGATES			18,400		
GREAT BRITAIN	DELEGATES			8,400		
FINLAND	DELEGATES			50,600		

# Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

## PLEDGES RECEIVED

01/02/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
CANADA	DELEGATES			10,600		
NETHERLANDS	DELEGATES			18,400		
VARIOUS DONORS				4,349,377		ESTIMATED INTERNATIONAL TRANSPORT/INSURANCE COSTS (30% OF TOTAL VALUE OF RELIEF ITEMS)
SUB/TOTAL RECEIVED IN KIND/SERVICES				53,363,796	CHF	35.1%


## ADDITIONAL TO APPEAL BUDGET

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
SUB/TOTAL RECEIVED				0	CHF	



# Pakistan: Earthquake

Situation map  
 Issued 25 November 2005

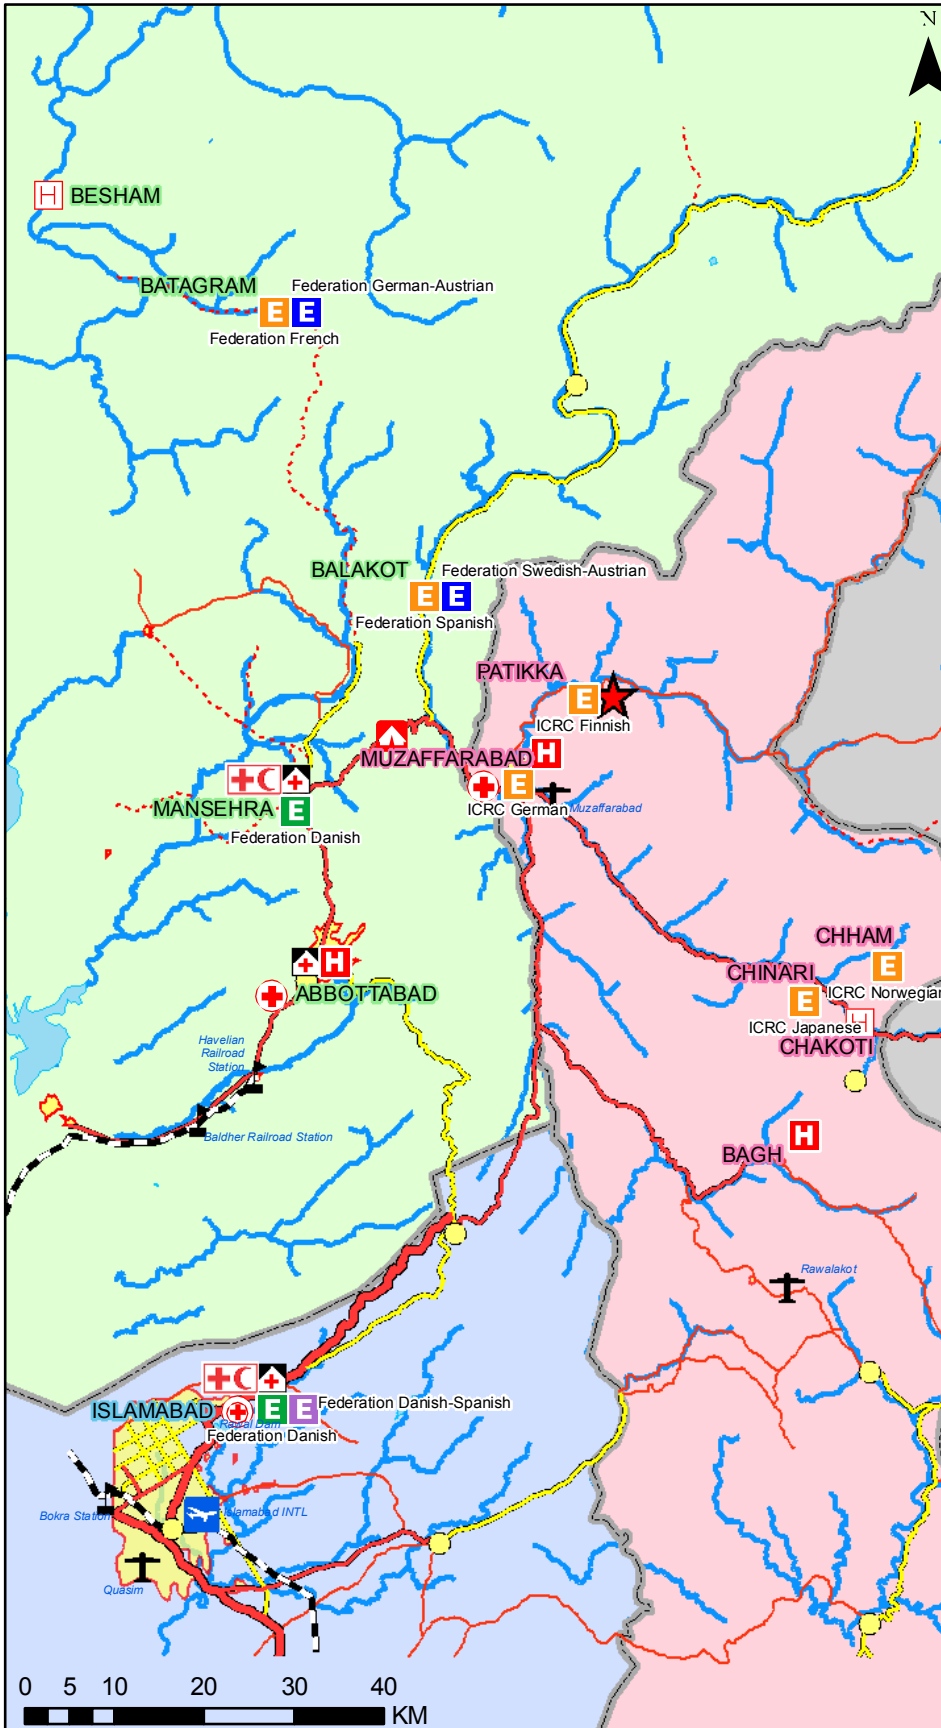

- Earthquake epicenter
- Federation delegation or hub
- Delegation
- Sub-delegation
- Federation and/or ICRC logistics center
- Emergency Response Unit (ERU)**
  - Basic Health Care (BHC)
  - IT/Telecom
  - Logistics
  - Water & Sanitation (WATSAN)
  - Federation base camp (provided by Danish RC)
  - Hospital
  - PRCS Basic Health Unit (BHU)
- Provinces**
  - Indian Jammu & Kashmir
  - North-west Frontier
  - Pakistan-administered Kashmir
  - Punjab
- Administrative boundaries
- Capital
- City
- City extension
- Railroads
- Highway, Hard, All weather
- Main road, Hard, All weather
- Secondary road, Loose, All weather
- Local road, Loose, Dry weather
- Track, Loose, Dry weather
- Airport
- Airfield
- railroad station
- Main rivers
- Lakes

The maps used do not imply the expression of any opinion on the part of the International Federation of Red Cross and Red Crescent Societies or National Societies or the ICRC concerning the legal status of a territory or of its authorities.

Map data sources: ESRI, Keyobs, Federation, ICRC
