

OPERATIONS UPDATE



International Federation of Red Cross and Red Crescent Societies
Fédération Internationale des Sociétés de la Croix-Rouge et du Croissant-Rouge
Federación Internacional de Sociedades de la Cruz Roja y de la Media Luna Roja
الاتحاد الدولي لجمعيات الصليب الأحمر والهلال الأحمر

PAKISTAN: EARTHQUAKE

28 March 2006

The Federation's mission is to improve the lives of vulnerable people by mobilizing the power of humanity. It is the world's largest humanitarian organization and its millions of volunteers are active in over 183 countries.

In Brief

Appeal No. 05EA022; Operations Update no. 24; Period covered: 15 February to 15 March 2006; Appeal coverage: 83.4%; ([click here to go directly to the attached Contributions List, also available on the website](#)).

Appeal history:

- Preliminary Emergency Appeal (launched as South Asia: Earthquake) on 9 October 2005 for CHF 10.8 million (USD 8.4 million or EUR 7 million) for four months to assist 30,000 families (some 120,000 beneficiaries).
- Operations Update No. 3 of 12 October 2005 increased the Preliminary Appeal budget to CHF 73,262,000 (USD 56,616,692 or EUR 47,053,307) to assist up to 150,000 families (some 750,000 beneficiaries) for six months, as an increasingly serious situation has unfolded.
- Operations Update No. 5 of 17 October 2005 revised down the number of targeted families to 70,000 (some 500,000 beneficiaries), based on the newly assessed delivery capacity and average family size of seven.
- Revised Emergency Appeal launched on 25 October 2005 for CHF 152 million (USD 117 million or EUR 98 million) to assist 81,000 families (some 570,000 beneficiaries) for six months.
- Disaster Relief Emergency Funds (DREF) allocated: CHF 200,000

Outstanding needs: To date CHF 126.7 million has been received, of which CHF 72.6 million is in cash and CHF 54.1 million is in-kind contributions. Additional pledges – especially in cash – are still needed to fully cover the operational costs.

Related Emergency or Annual Appeals: [South Asia Regional Annual Appeal 05AA051](#)

Operational Summary:

A further 15,000 families have been assisted with emergency relief items in the past month, bringing the total number assisted to almost 106,000 (approximately 740,000 people). This exceeds the target of 81,000 families by almost 30 per cent. The main focus of assistance has been on emergency shelter (tents, tarpaulins), durable shelter (corrugated galvanized iron (CGI) sheets, shelter repair kits), provision of health services and water and sanitation activities.

The emergency relief phase is winding down and the Federation is in the process of launching a revised emergency and recovery plan of action covering the period 2006-2008. While the emergency phase is ending, the Red Cross and Red Crescent is fully aware of ongoing emergency relief needs and will continue the provision of these services in the short term. Provision is being made to assist a further 20,000 families with emergency shelter and a 10,000 with durable shelters if required during future emergencies.

The government of Pakistan is beginning to shut down the various tent camps over the coming weeks. There are approximately 250,000 people living in camps across the North West Frontier Province (NWFP) and Pakistan-administered Kashmir. The plan is to have closed all camps consisting of fewer than 50 sites (currently housing a total of approximately 102,000 people) by 31 March. The Pakistan Red Crescent Society (PRCS)/Federation is to conduct an assessment in March and April, to examine the status of returnees and those unable to leave camps, and tailor assistance to meet the needs of the most vulnerable within the confines of the PRCS/Federation capacity. In April, there are also plans to host a joint assessment to further detail the planning for the recovery

and reconstruction programmes and to benefit from the expertise of various partner national society representatives to ensure a more integrated approach to future programming.

For further information specifically related to this operation please contact:

- In Islamabad: Khalid Kibriya (Secretary-General), Pakistan Red Crescent Society; email: hilal@isb.comsats.net.pk, Phone: +92 51 925 0404; Fax: +92 51 925 0408
- In Islamabad: Azmat Ulla (Head of Delegation); email: Azmat.ulla@ifrc.org; Office phone: +92 51 925 0416 Mobile: +92 300 850 3317; Fax: +92.51.443.0745; Ted Itani (Head of Operations); email: ted.itani@ifrc.org; Mobile: +92 302 561 2191;
- In Geneva: : Christine South (Pakistan Desk Officer); email christine.south@ifrc.org; Phone: +41 22 730 4529; Jagan Chapagain (South Asia Regional Officer), email: jagan.chapagain@ifrc.org; Phone: +41 22 730 4316; Fax: +41 22 733 0395;

All International Federation assistance seeks to adhere to the [Code of Conduct for the International Red Cross and Red Crescent Movement and Non-Governmental Organizations \(NGOs\) in Disaster Relief](#) and is committed to the [Humanitarian Charter and Minimum Standards in Disaster Response](#) in delivering assistance to the most vulnerable. For support to or for further information concerning Federation programmes or operations in this or other countries, or for a full description of the national society profile, please access the Federation's website at <http://www.ifrc.org>

Background

An earthquake with a magnitude of 7.6 on the Richter scale, centred 95 km northeast of Pakistan's capital, Islamabad, struck at 08:50 local time (03:50 GMT) on 8 October 2005, with tremors felt across the region from Kabul to Delhi. The quake decimated large areas northern Pakistan and northern India. A total of 73,000 people died in Pakistan while a further 128,000 were injured¹. More than 3.5 million people were made homeless.

Operational developments

With winter ending the emphasis is switching from emergency relief to recovery and rehabilitation. The feared second wave of deaths did not occur for a variety of reasons. The hardiness and resilience of the affected population was absolutely vital to their survival and cannot be underestimated. In addition, the combined efforts of the various elements of the relief operation also worked well together, with essential food, shelter and other non-food items reaching a significant number of earthquake survivors to support them through the winter. PRCS and the Federation have contributed to this response, and with a further 15,000 families assisted in the past month, have now assisted more than 105,000 families (approximately 740,000 people). This exceeds the target 81,000 families by almost 30 per cent.



Women taking part in ECHO-supported Red Cross and Red Crescent psycho-social support activities in a tent camp in Garhi Habibullah. (Photo: Finnish Red Cross)

There has been continued seismic activity in affected region in the past month. There have been five earthquakes in northern Pakistan in the past 30 days ranging in magnitude from 3.6 to 5.1 on the Richter scale. Fortunately, only one death and no significant damage has been reported.

The government of Pakistan is rolling out a camp closure policy in an effort to encourage people to return to their homes if they are able. There are approximately 250,000 people living in 783 camps across NWFP and Pakistan-administered Kashmir. All camps of under 50 sites are due to be closed by 31 March. Families who lost their homes are to be given a cash grant of PKR 175,000 (approximately CHF 3,840) in three instalments based on a progress payment system. The expectation is that families will use this to rebuild homes, through what is termed an 'owner-driven solution'. The larger camps (consisting of over 50 sites each) are to be closed shortly as well. The government has indicated that no assistance will be provided for those who continue to live in camps except

¹ Pakistan Federal Relief Commission

in the most vulnerable cases. It is keen to avoid camps becoming permanent sites, as occurred with Afghan refugees following the mass influx in 2001.

The breakdown of people living in camps is as follows:²

Camps of 50 sites or more (Camp management cluster)						
	Pakistan-administered Kashmir		North West Frontier Province		Total	
	Population	Camps	Population	Camps	Population	Camps
Planned	13,469	9	42,385	15	55,854	24
Spontaneous	72,804	87	18,649	42	91,453	129
Total	86,273	96	61,034	57	147,307	153

Camps/settlements of under 50 sites						
	Pakistan-administered Kashmir		North West Frontier Province		Total	
	Population	Camps	Population	Camps	Population	Camps
Number	2,059	14	100,422	616	102,481	630
Total	2,059	14	100,422	616	102,481	630

While emergency relief activities are winding down, the Red Cross and Red Crescent is mindful of those families who will continue to require ongoing emergency assistance. Provision is being made to continue relief (such as durable and emergency shelters) for up to 30,000 families and contingency stocks of other items will be stored in readiness. Affected people face numerous challenges in returning to their homes. In some cases the land where their homes once stood is still unstable, others face disputes with landowners. In the case of urban centres such as Balakot and Muzaffarabad, large amounts of rubble still need to be cleared before reconstruction can start.

The health situation remains stable with no significant increase in medical problems. The main causes for consultations in the past week have been acute respiratory infections (26 per cent), acute watery diarrhoea (7 per cent), fever (4 per cent) and injuries (4 per cent).³ The PRCS/Federation mobile medical teams operating around Balakot and Besham reported a significant increase in patient numbers over the past few weeks (going from approximately 200 to 700 patients per week). This is due in part to people returning from camps, and a growing awareness and confidence among the communities to utilize the facilities.

The PRCS/Federation recovery team consisting of livelihood, shelter, gender professionals and a recovery coordinator has been working since January to design the next phase of the operation. This will be outlined in the revised emergency and recovery appeal, which will detail operations through to the end of 2008. Improving the operational capacity of PRCS staff and volunteers at all levels will be integral to this appeal plan. A vital ongoing aspect of the recovery planning is to assess the evolving needs of returning families and to identify and assist the most vulnerable within the confines of the capacity of the PRCS/Federation. A multi-disciplinary assessment team is being formed and it is planned to conduct more detailed, joint assessments in later March and through April.

A new Federation warehouse compound is being established in Mansehra and will consist of 10 Rubb halls. It is scheduled to be fully operational by the end of March and will hold the goods for the ongoing relief distributions. As a result of the increased capacity in Mansehra, the Federation warehouse in Islamabad is being shut down.

The Federation base camp in Mansehra/Batrasi, which has operated since late October 2005, is scheduled to be closed in mid-April. The facility, which had the capacity to house 100 people, is being shut as the operation moves into the rehabilitation phase and the number of personnel decreases. Remaining staff will be housed in local accommodation.

Security: During the last month there have been various demonstrations and issues voiced out in some local media over the cartoon row. Although the situation impeded the PRCS/Federation relief operation during the reporting period, distributions and other activities continued as circumstances allowed.

² UNHCR Pakistan situation report 48, 9 March 2006

³ Pakistan Ministry of Health/World Health Organization (WHO) weekly morbidity and mortality report 13 March 2006.



A PRCS volunteer conducting an assessment of a family in Tandah Village (NWFP) living in a Red Cross and Red Crescent supplied tent.

The visit of the US president in the first week of March resulted in tight security restrictions in Islamabad. As a result, the Federation delegation in Islamabad closed for two days (3 and 4 March) and all field movements were restricted, but limited relief operations continued.

Recent bad weather including heavy rain has caused landslides and blockage of roads in the Balakot, Besham and Banna areas. One Federation M6 truck carrying relief items went off the Thakot - Banna road and was totally destroyed, falling down a 300 metre ravine. Thankfully the driver was able jump out of the vehicle before it fell.

with the army and agree to armed escorts for Federation staff or convoys travelling in the area. The Federation is making it clear to the authorities that armed escorts are not appropriate and that this is agreed by the central military command in Islamabad.

There are concerns over various requests from the local army commander in Banna district, seeking to register Federation international staff

A full-time Federation security delegate is now based in Mansehra to support the field operations of PRCS, the Federation, and partner national society teams operating within the earthquake-affected area.

Coordination

A new liaison delegate began his mission in the reporting period, representing the Federation at weekly United Nations Office for the Coordination of Humanitarian Affairs (UN OCHA) cluster coordination meetings, the inter-agency coordination meeting and the logistics cluster meeting. Technical Federation staff members also attend OCHA cluster meetings covering shelter, health, and water and sanitation. The liaison delegate attends the ad hoc government meetings of the government's Earthquake Relief, Rehabilitation and Reconstruction (ERRA), who are responsible for the coordination and planning of the transition to rehabilitation and reconstruction. There have been four meetings in the past month.

Internally, the head of delegation is attending the weekly PRCS chairperson's meeting which involves management staff, board members and some heads of department. The liaison delegate attends the weekly PRCS/Federation staff meeting in Mansehra. There is daily informal contact between the Federation, PRCS and the ICRC, while the Federation and the ICRC hold fortnightly management meetings.

The Federation has signed a cooperation agreement with the Qatar Red Crescent Society. The agreement formalizes administration and service arrangements, including the provision of office space and support. Similar agreements are being negotiated with the American, Belgian, Danish, French and German Red Cross societies, who are all working or seeking to work bilaterally in Pakistan. A new Movement partners meeting structure is being planned. Hosted by the Federation, weekly meetings will be held involving all in-country partner national societies, PRCS and the ICRC, to discuss issues and optimize coherence between the partners.


Red Cross and Red Crescent action - objectives, progress, impact

1. Emergency relief (food and non-food)

Objective: the basic shelter and household needs of 81,000 earthquake-affected families (approximately 570,000 people) in northern Pakistan are met over the next six months, enabling them to start rebuilding their future.

Progress/Achievements

In the past month a further 15,000 families have received emergency relief, bringing the total assisted as of 15 March to 105,801. This represents more than 740,000 people (based on a calculation of seven people per family). This is almost 30 per cent above the target of 81,000 families. Some of them have received a secondary distribution but are not counted twice.

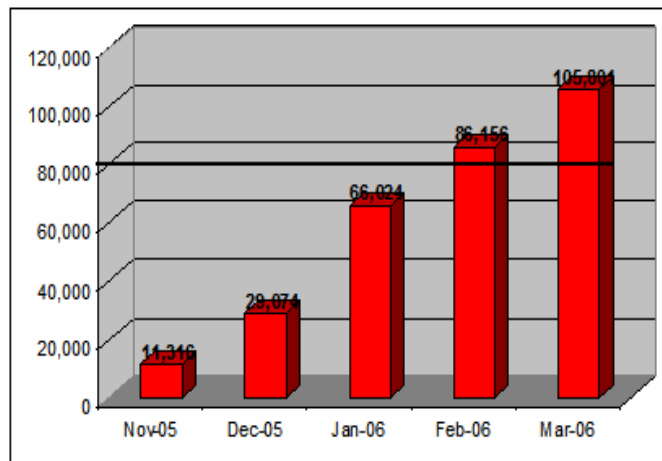

The cumulative number of families assisted with emergency relief has now exceeded the original goal of 81,000 by 30%.

shelter repair kits. CGI sheets are provided only to those families who have finalized their wooden, earthquake-resistant structures. The shelter repair kit consists of a rope, spade, axe, hammer, nails (four different sizes), nail covers, iron hooks, and a sickle. By the end of February, CGI sheets and shelter repair kits had been pre-positioned in the Meira camp for airlift to Pashto, Dirkut and Upper Tandool in the Allai Valley. The airlifts have taken longer than planned due to weather disruptions to the helicopter flights. However the last delivery of the pre-positioned stock was completed during the second week of March. In total, 10,000 CGI sheets and 1,000 shelter repair kits have been airlifted to the Allai Valley during the reporting period, where 1,000 beneficiary families from high lying communities have been assessed and are ready to receive the materials to complete their shelters.

At the outset of the operation, each assisted family received a tent, tarpaulin and seven blankets. Later, relief items were added to the package as they became available. The makeup of the relief package also changed in response to changing circumstances, beneficiary feedback. For example, as some items became unavailable from mid-January, jerry cans, kerosene lamps, tarpaulins, blankets and kitchen sets were not included, while others items, such as shawls, quilts and bed sheets were added. UNICEF recently supplied the Federation with 55,589 blankets to alleviate a shortfall. UNICEF also assisted with the provision of tarpaulins and high quality quilts.

A major component of the relief effort is the distribution of CGI sheets (10 per family) and

Two relief teams have already completed distributions to assessed families while the remaining teams will finish not later than the third week of March. The distribution of CGI sheets and shelter repair kits is more difficult than other relief items due to their bulk and weight: 10 CGI sheets and one shelter kit distributed to each family weighs 172 kg.

Distributions in Satbani, Balakot were completed with the assistance of Norwegian Red Cross all-terrain vehicles and belt-wagons. In total, 300 families received CGI sheeting, shelter repair kits, blankets, quilts, hygiene parcels, sheets, shawls and wood burning stoves.

The Oghi/Siran Valley relief team carried out assessments prior to distributing 2,242 tents to beneficiaries living in small temporary camps consisting of fewer than 50 families. PRCS volunteers replaced damaged tents with new winterized ones and assisted the Norwegian Refugee Council in distributing clothing parcels. These camps were previously identified by the inter-agency assessment team, in which PRCS volunteers participated, as being in need of assistance. The relief team also assessed the need for wheelbarrows in Bedadi, Shinkhari, where communities have started repairing their houses and preparing their fields for crops. The distribution of these items has just commenced.

A temporary shortage of shelter kits forced the postponement of some planned distributions. However supplies have improved and there are no availability problems anticipated in the short term. In addition to the present distribution to 20,000 families, the Federation/PRCS will distribute an additional 4,000 CGI sheets and 4,000 shelter repair kits to needy families in the mountains of the high-lying areas of Talhatti in Gari Habibullah. Assessments began on 15 March and distributions will take place as soon as the commodities become available

(they are manufactured in Karachi and then transported to earthquake affected areas). Distributions are planned to take place from late March until mid-April.

A summary of the cumulative relief distributions by the Federation as at 15 March is as follows.

	Shumlai	Battal/Chattar/ Hillkot	Allai	Garhi Habibullah	Balakot	Batagram/ Battal	Sirian Valley	Kohistan	Total
Families assisted	2000	12,626	7,227	16,964	24,059	14,086	13,984	14,855	105,801
Tents	0	710	581	13,566	9,559	9,488	11,567	12,233	57,704
Blankets	0	8,725	36,715	89,666	78,628	74,352	68,892	74,750	431,728
Tarpaulins	0	20,722	13,110	18,438	17,392	13,648	12,621	24,596	120,527
CGI sheets	0	12,480	0	20,120	32,550	18,352	21,981	14,750	120,233
Shelter repair kits	0	1,248	0	2,012	3,255	1,824	2,189	1,463	11,991
Sleeping bags	0	24	306	3,309	5,624	5,664	4,524	277	19,728
Quilts	0	40,350	16,963	43,792	38,711	40,824	74,195	40,891	295,726
Jerry cans	0	9,698	6,278	5,367	8,360	1,662	4,475	19,734	55,574
Kitchen sets	2,000	9,777	6,094	6,251	5,336	3,552	7,152	12,053	52,575
Hygiene kits	0	10,588	5,709	6,643	9,511	6,072	12,000	13,582	64,105
Stoves	0	433	3,043	4,742	5,985	4,415	9,948	10,013	38,579
Sheets	14,080	4,795	0	21,021	24,965	21,689	66,611	6,679	159,840
Lamps	0	9,573	0	2,657	7,819	193	4,383	8,134	32,759
Buckets	0	0	0	0	1,354	0	0	0	1,354
Shawls	0	2,512	4,860	6,806	14,597	11,867	29,612	6,730	76,984

2. Emergency health and care

Objective: Some 250,000 earthquake-affected people in northern Pakistan have access to appropriate quality health care, safe water and sanitation services in the next six months.

To date more than 234,000 people have received some form of medical assistance as a result of Red Cross and Red Crescent activities. With large numbers of people on the move as they return to affected areas with the end of the winter, there is an increased risk of medical problems. WHO is scaling up immunization activities and is involved with UNICEF in Besham/Balakot, conducting mass measles immunizations for children between nine months and 15 year of age. This to prevent sporadic cases of observed measles which could spread to epidemic proportions.



Distribution of ECHO-supplied hygiene kits in Balakot (NWFP) by Red Cross and Red Crescent staff.

Red Cross and Red Crescent health interventions have scaled down in some areas compared to previous months with emergency health needs subsiding. The Abbotabad field hospital was closed on 16 February and arrangements have been made for the packing and storage of equipment for future use in the national society's NWFP branch. A total of 45 staff members were employed to conduct the dismantling and packing process. In total, during the three-and-a-half months of operation, the Abbotabad field hospital achieved the following:

- 273 admissions;
- 205 surgical procedures;
- 67 patients were given outpatient support;
- 2,438 psycho-social support sessions were conducted;
- 83 laboratory tests and 191 X-rays conducted; and
- 3,395 patients received physiotherapy treatment.

A study is being carried out to understand the patients' perception regarding the field hospital. Patients have been interviewed and data collected and the results of the study will be published in an operations update in the near future.

The two mobile health teams in Besham and Balakot continue to make regular visits to clinic sites. Since early February attendance at each clinic has risen from approximately 200 patients weekly to 700 a week. The increase is due to a variety of reasons, including that people are beginning to return from camps to the affected areas, and the increase of awareness in the communities regarding the role and value of the clinics. An encouraging trend is the increase in the number of women and girls using the clinics. To begin with, patients were approximately 70 per cent men and 30 per cent women, but the breakdown now is virtually equal. Plans have also been made and communities informed regarding the integration of immunization services within the mobile health clinics' activities.

Community assessments have been carried out in Besham in Kuzbakhot with a view to establishing an additional clinic. Meetings have been held with a local NGO interested in setting up mobile clinics for the areas surrounding Besham and Balakot, with the objective of ensuring there is no duplication of effort. The NGO was given information on the areas where the Federation is carrying out its operation and on its future plans to expand.

The drug store in Besham is now stocked with most of the required drugs to supply the mobile clinics and is regularly monitored. With strict monitoring of the drug utilization, the store can serve as the pilot for helping the programme establish a realistic stock requirement for mobile clinic activities in the future.

The handover of the Spanish Red Cross Emergency Response Unit (ERU) in Balakot to PRCS was completed in February. The facility will become a basic health unit run by PRCS medical and support staff. The decision was taken to reduce the number of doctors for the facility from two to one due to lower patient demand. Until the end of February, the facility had 575 patients (an average of approximately 40 daily). The most common problems diagnosed were upper and lower respiratory problems (22 per cent), muscle and joint pain (16 per cent), scabies (14 per cent), and digestive problems (8 per cent). These numbers are similar to previous months and there is no discernable increase in any particular medical problem.

The French Red Cross medical team in Batagram continues to deliver mobile health care services and training and has treated a total of 14,623 patients to date. The team comprises 20 people made up of Federation and French Red Cross international staff. A technician for the 'Expanded Programme for Immunization' (EPI) joined the team to enhance the immunization coverage in the area of operation. There has been a notable increase in the patients at all the basic health units in the Batagram area, with the exception of Gari Nawab Said. There has been a particular increase in the number of diarrhoeal cases and scabies patients.

The Turkish Red Crescent's Abbas hospital in Muzaffarabad has to date treated a total of 50,028 patients (15,000 in the past four weeks) and performed more than 400 surgical operations. An emergency service was opened at the hospital on 9 March.

The Qatar Red Crescent field hospital in Dhuli (near Bagh) has treated 6,844 patients in the last four weeks bringing the total patients seen to 22,474 since it began operating in November. There is a steady increase in the number of inpatient admissions and new software has been developed to record accurate inpatient data registration. The total number of people vaccinated since the beginning of the programme has reached 1,823. Health education activities are also continuing - several education sessions have been conducted with large groups during the distribution of hygiene kits and chlorine tablets.

The summary of Federation, PRCS and bilateral partner national society health interventions to date is as follows.

Health facility	Location	Beneficiaries
PRCS mobile health units	Pakistan-administered Kashmir (various locations)	53,460
PRCS mobile health units	NWFP (including Balakot, Gari Habibullah)	7,187
PRCS/Korean Red Cross mobile health unit	NWFP (including Mansehra base camp, Besham)	4,382
PRCS/Federation temporary facility (formerly Federation Spanish Red	Balakot	7,182

Cross ERU)		
French Red Cross ERU	Banna Alai, Batagram, Bateela, Pachto, Rashang	15,166
RDRT/Malaysian Red Crescent team	Mansehra base camp and Mang/mountains	1,182
Federation multinational field hospital	Abbottabad	14,623
Italian Red Cross field hospital	Mansehra	686
Qatar Red Crescent field hospital	Bagh (Dholi)	22,474
Saudi Red Crescent field hospital	Mansehra	58,224
Turkish Red Crescent field hospital	Muzaffarabad	50,028
TOTAL		234,594

Water and Sanitation

Water and sanitation activities continue serving the communities in Balakot and Batagram and the Meira camp, and are expanding into the Allai Valley. These activities are now focusing more on the transition to recovery.

In Balakot, the Austrian/Swedish Red Cross ERU was handed over to the Federation on 1 March 2006. However, the Swedish Red Cross continues to provide two water and sanitation delegates to support the purification of 210,000 litres of water for more than 15,000 beneficiaries each day. In Batagram, the German/Austrian Red Cross team continues to service 10,000 people, supplying 45,000 litres a day.

In Batagram, the German/Austrian Red Cross teams are aiming to build 50 latrines per week and have now completed 341 (completing 162 in the past month). An additional 85 latrines have been completed in the reporting period in Balakot, bringing the total to 264 for that region.

The teams have constructed/rehabilitated a total of 20 water tanks to date. During the reporting period the team in Batagram constructed 63 bathing facilities, while the number in Balakot remains at 29. A key aspect of the bathing facility operation is to provide private areas for women. Discussions have been held with women in the community to ensure the bathing areas meet their needs.

The hygiene promotion team has continued distributing hygiene parcels. To date a total of 10,753 kits (one per family) have been distributed to 54,634 beneficiaries (36,845 in Balakot and 17,789 in Batagram). There were some problems with the content and quality of the hygiene parcels during the reporting period (some items did not meet beneficiary needs or were of the wrong quality). This is being fully looked into by the delegation and the relief / logistics team on the ground.

Water and sanitation figures as of 8 March 2006

Location	No. beneficiaries access to purified water	litres purified daily	No. of latrines	No. of bathing facilities	No. hygiene kits distributed
Balakot	15,000	210,000	264	29	7,369
Batagram	10,000	45,000	341	63	3,384
Meira Camp	5,000	8,000	5	-	-
TOTAL	30,000	263,000	610	92	10,753

Psycho-social support (PSP)

In addition to the physical harm suffered as a result of the earthquake, immense psychological distress has been caused to the affected population. The experience of such severe shock and loss can have very serious psychological and psycho-social consequences, both in the short and long term. This makes a return to normal life and the reestablishment of livelihoods more difficult and reduces quality of life in the long term. Health facilities have noted an increased number of patients with psychosomatic complaints. The level of mental distress is increasing and some cases are bordering on Post Traumatic Distress Syndrome (PTDS). This is verified by psychologists and psychiatrists working in the affected areas.

The current psycho-social programme run by the Danish Red Cross on behalf of the Federation is supported by the Humanitarian Aid Department of the European Commission (ECHO) and will run till 15 May 2006. The PRCS has recruited 18 staff and mobilized more than 100 volunteers from amongst the communities, who have been

trained in psychosocial activities and community mobilization methods. The programme activities are covering four camps and will be expanded into surrounding communities in the near future.

The PSP team in Besham identified 96 cases of depressed people who were referred to the International Organization for Migration (IOM) and the Cuban medical unit for further treatment. They also have plans to train six community volunteers to work in Meira camp. In total, since the operation began, the PSP team, with the help of trained social workers and other team members, has reached about 10,000 people.

The Turkish Red Crescent psycho-social programme is also continuing and is conducting sewing courses at the Turkish Tent Camp in Islamabad. Fifteen sessions were also provided to 130 people on coping with stress. In Muzaffarabad, a total of 1,000 children have been reached utilizing playing groups to help identify and bring out cases of stress. Interventions to provide support in schools were launched with 21 trained volunteers.

3. Logistics/IT/Telecommunication

Overall Objective: The ongoing PRCS and Federation relief operation have effective logistical, IT and telecommunication infrastructure in the operational areas.

IT

The IT team has completed the conversion to a new email system for all Federation staff at the Islamabad office and training on the various features will be conducted shortly. Standard daily support activities are continuing to support the network and other systems.

Telecommunications

Maintenance and adjustment of the radio systems at the Mansehra office and other related activities have been carried out. Installation of a high-frequency (HF) base station at the Federation's Islamabad office, in order to establish a reliable communication with the Mansehra radio room and mobiles on the road, has been completed. Coverage tests have been conducted with the radio room in Mansehra in order to have better information about the actual operational range of the HF network. The radio room is issuing daily weather and road reports in coordination with the security delegate to help deal with landslides and the unstable road conditions – the radio room is also in charge of distributing security-related reports. Programming and setup was done for six radio systems in the new cars just arrived from Dubai and very-high-frequency (VHF) and HF systems were installed in the PSP vehicles. VHF handhelds are available with the IT department for the teams going into the field.

Logistics

The logistics team has located a new warehouse compound in Mansehra. This compound will have 10 Rubb halls as storage facilities. The new compound will serve the earthquake operation as a main logistics hub and as a long term storage facility. This warehouse compound is scheduled to be fully operational by the end of March and will serve the more decentralized Rubb hall distribution points. As a result of the increased capacity in Mansehra, the Federation is closing the warehouse facilities in Islamabad and Baffa.

Since the beginning of operation Federation has sent 2,605 truckloads of relief goods to the affected areas. However, the logistics team has now adjusted the transport capacity on the ground to match the current needs of the operation. The number of commercial trucks has been reduced, though the Federation's trucks, belt wagons and all terrain vehicles are still being used to serve the operation. The last Federation helicopter distributions were successfully made in mid March and the Federation will use other means to distribute the necessary shelter materials and other items.

4. Communication – advocacy and public information

Objective: The needs of the earthquake-affected population in Pakistan are advocated for and the Red Cross and Red Crescent's interventions are profiled through national and international media coverage.

During the reporting period, representatives from various national societies, such as the British, Finnish, Norwegian, and Turkish Red Cross and Red Crescent societies, visited affected areas. Most of the delegations

were accompanied by journalists. Visitors were briefed and their trips to the field were facilitated by the Federation.

To accompany the British Red Cross visit, headed by the chief executive of the national society, a detailed information pack was prepared. The contents of this pack will also be used to support for the six-month commemoration media package.

The president as well as the executive committee and governing board members of the Turkish Red Crescent Society, accompanied by 45 journalists, made a brief visit in early March. The Turkish Red Crescent delegation discussed future plans and cooperation with the PRCS and the Federation. The Federation movement coordinator and the information delegate accompanied the Turkish contingent on a field trip to various affected areas in Pakistan administered Kashmir. The information delegate also gave interviews to several Turkish media outlets, including CNN TURK, NTV, TRT and Hurriyet daily newspaper.

The Norwegian Red Cross' head of communications and a video/photo specialist also visited the region to observe and film the trials of the Norwegian Red Cross supplied all-terrain vehicles and belt wagons. The team was briefed and their travel was facilitated by the Federation. The press release on the ATVs can be found at <http://www.ifrc.org/docs/News/pr06/1006.asp>.

Two articles on the psychological impact of the earthquake have been produced and are to be published in the forthcoming issue of the Red Cross and Red Crescent (RCRC) magazine and on the Federation's website. A similar article on the topic has been produced for local national newspapers, with a focus on informing the beneficiaries and public at large on the psychological effects of the earthquake and on ways to cope with them. A psycho-social support brochure has been designed by the PSP team, with support from the information delegate.

A communications coordinator, based in Islamabad, commenced a one year mission at the beginning of March. He will have responsibility for overseeing the communications strategy, reporting on operations and coordination of monitoring and evaluation.

Outstanding Needs

The appeal to date is 83.4 per cent covered. The current emergency appeal will be revised and extended to cover recovery and reconstruction programmes through until the end of 2008. There will be a need for cash to fully cover these costs, once the appeal is launched. Donors are urged to support the revised appeal to allow the Red Cross and Red Crescent to support changing needs during the transition from relief to recovery.

The following longer-term positions urgently need to be recruited internationally and regionally:- deputy head of delegation (based in Islamabad), head of field office (based in Mansehra), and disaster management delegate (Mansehra).

[Contributions list below; click here to return to the title page.](#)

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

29/03/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
-------	----------	----------	------	-----------	------	---------

CASH

REQUESTED IN APPEAL CHF ----->				152,000,000	TOTAL COVERAGE 83.4%	
AMERICAN - RC		850,000	USD	1,099,900	17.10.05	
AMERICAN - RC		1,000,000	USD	1,280,500	01.11.05	
AMERICAN - RC		362,100	USD	475,075	08.12.05	HELICOPTER OPERATIONS ONE MONTH
AMERICAN - RC		1,500,000	USD	1,968,000	29.12.05	CORRUGATED IRON SHEETS
AMERICAN - RC		1,500,000	usd	1,968,000	30.01.06	
AUSTRALIAN - GOVT		3,000,000	AUD	2,956,500	10.10.05	TENTS, BLANKETS, TARPULINS, KITCHEN SETS, AIRFREIGHT
AUSTRALIAN - RC		500,000	AUD	480,500	19.10.05	MEDICAL SUPPLIES, VACCINES, CHOLERA KITS
AUSTRALIAN - RC		500,000	AUD	480,500	25.10.05	NEW EMERGENCY HEALTH KITS
AUSTRALIAN - RC				300,000	15.11.05	56 NEW EMERGENCY HEALTH KITS
AUSTRIAN - RC		50,000	EUR	77,825	03.01.06	
AUTONOMOUS PROV. BOLSANO		50,000	EUR	77,825	08.01.06	
BARBADOS - RC		1,015	USD	1,305	07.02.06	
BRITISH - RC		250,000	GBP	569,500	09.10.05	
BRITISH - GOVT/DIFD		1,470,588	GBP	3,344,117	27.10.05	
BRITISH - RC		250,000	GBP	568,500	17.11.05	
BRITISH - GOVT/DEC		214,663	GBP	488,143	18.11.05	PROCUREMENT OF STOVES
BRITISH - GOVT/DEC		1,331,250	GBP	3,027,263	18.11.05	PROCUREMENT OF HYGIENE KITS
BRITISH - GOVT/DEC		692,250	GBP	1,574,176	18.11.05	PROCUREMENT OF SHELTER KITS
BRITISH - RC		500,000	GBP	1,129,500	20.12.05	CORRUGATED IRON
BRITISH - RC		490,197	GBP	1,114,732	06.02.06	
BRITISH - RC		200,000	GBP	459,000	14.02.06	HYGIENE KITS
BRITISH - PRIVATE DONOR		405	GBP	918	05.01.06	
BRITISH - PRIVATE DONORS				15,857	03.11.05	
BRITISH PETROLEUM		500,000	USD	647,000	11.10.05	
BRITISH PETROLEUM FOUNDATION		75,726	USD	99,353	22.12.05	
CAMBODIAN - RC		15,000	USD	19,410	13.10.05	
CAMBODIAN - PRIVATE DONOR		100	USD	131	01.11.05	
CANADIAN - GOVT/CIDA/HAPS		990,000	CAD	1,093,455	13.10.05	
CANADIAN - GOVT/CIDA/HAPS		99,000	CAD	109,346	18.10.05	
CANADIAN - RC		1,000,000	CAD	1,088,200	19.10.05	PROCUREMENT 1300 WINTERISED TENTS
CANADIAN - RC		1,000,000	CAD	1,088,200	02.11.05	
CANADIAN - GOVT CIDA/HAPS		990,000	CAD	1,077,318	09.11.05	
CANADIAN - RC		750,000	USD	984,000	09.12.05	HELICOPTER OPERATIONS 2 MONTHS
CHINA - HONG KONG RC BRANCH		500,000	HKD	83,100	10.10.05	PROCUREMENT SHELTER KITS

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

29/03/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
CHINA - HONG KONG RC BRANCH		4,000,000	HKD	679,600	29.11.05	
CHINA - HONG KONG RC BRANCH		2,000,000	HKD	330,600	23.12.05	PURCHASE OF WINTERISED TENTS
CHINA - MACAU - RC BRANCH				25,000	10.10.05	PURCHASE OF MEDICINES, BLANKETS & TENTS
CHINA - MACAU - RC BRANCH				15,000	09.12.05	PURCHASE OF MEDICINES
CROATIAN - RC		20,000	EUR	30,950	30.11.05	
CYPRUS - RC				20,867	12.10.05	
CZECH - RC		10,000	USD	12,940	25.10.05	
DANISH - RC				95,920	14.10.05	
DANISH - GOVT through RC				492,769	20.10.05	
DANISH - GOVT through RC				294,069	16.11.05	
DANISH - GOVT through RC				196,842	28.11.05	
DANISH - PRIVATE DONORS				4,783	03.02.06	
ECHO (05004)		810,747	EUR	1,262,333	13.10.05	
ECUADORIAN - RC		5,702	USD	7,481	25.01.06	
FINNISH - PRIVATE DONORS		700	EUR	1,083	12.10.05	
FRENCH - RC		400,000	EUR	618,200	07.11.05	
FRENCH - PRIVATE DONORS				1,952	21.10.05	
GERMAN - RC		500,000	EUR	778,500	27.10.05	
GERMAN - RC		500,000	EUR	772,750	21.11.05	PURCHASE WINTERISED TENTS
GERMAN - PRIVATE DONORS				148	18.10.05	
HELLENIC - RC				50,000	11.10.05	PURCHASE 10'000 BLANKETS
ICELANDIC - GOVT		75,000	USD	97,050	09.10.05	
ICELANDIC - RC		17,000,000	ISK	357,000	14.11.05	
INDONESIA - PRIVATE DONOR				128	28.10.05	
IRISH - GOVT		300,000	EUR	467,100	13.10.05	
IRISH - GOVT		350,000	EUR	540,925	28.10.05	
IRISH - RC		100,000	EUR	154,550	16.11.05	
IRISH - RC		500,000	EUR	772,750	25.11.05	PROCUREMENT OF HYGIENE KITS
IRISH - RC		350,000	EUR	541,625	13.12.05	PURCHASE WINTERISED TENTS
IRISH - RC		400,000	EUR	622,600	13.12.05	
IRISH - RC		250,000	EUR	391,250	06.03.06	PURCHASE CORRUGATED IRON SHEET
IRISH - PRIVATE DONOR				1,035	17.01.06	
ITALIAN - GOVT		200,000	EUR	311,400	17.10.05	
ITALIAN - RC		150,000	EUR	231,825	10.10.05	+ FOR INDIA, EUR 50'000 (DM , see AA047), FOR RELIEF SUPPLIES
JAPANESE - RC		262,513	USD	339,692	11.10.05	
JAPANESE - RC		2,800,000	USD	3,585,400	25.10.05	PROCUREMENT OF 10000 FAMILY TENTS, 10000 KEROSENE LAMPS, 10000 KEROSENE STOVE, 50000 BLANKETS
JAPANESE - RC		150,000,000	JPY	1,662,000	09.11.05	
JAPANESE - GOVT		2,800,000	USD	3,599,400	15.02.06	PROCUREMENT & DISTRIBUTION OF WINTERIZED TENTS, SHAWLS
KOREA, REPUBLIC - RC		50,000	USD	64,700	10.10.05	
LATVIAN - GOVT		100,000	USD	129,400	13.10.05	
LIBYAN - RC				10,000	10.10.05	

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

29/03/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
LICHTENSTEIN - PRIVATE DONOR				300,000	28.10.05	
LITHUANIAN - RC				3,567	13.01.06	
LUXEMBOURG - GOVT		200,000	EUR	311,400	24.10.05	
LUXEMBOURG - RC		40,000	EUR	61,900	21.12.05	PROCUREMENT OF CORRUGATED IRON SHEETS
MACEDONIA, FYR - RC		3,000	EUR	4,671	28.10.05	
MONACO - RC		30,000	EUR	46,710	17.10.05	
NETHERLANDS - GOVT		160,428	EUR	247,941	13.10.05	
NETHERLANDS - RC		213,904	EUR	330,588	03.11.05	
NETHERLANDS - RC		534,759	EUR	826,471	10.11.05	
NETHERLANDS - RC		855,615	EUR	1,324,064	28.11.05	
NETHERLANDS - RC		213,904	EUR	331,016	19.12.05	
NETHERLANDS - PRIVATE DONORS				825	28.10.05	
NETHERLANDS - PRIVATE DONOR				500	19.12.05	TENTS
NEW ZEALAND - RC		100,000	NZD	89,600	20.10.05	
NEW ZEALAND - GOVT		400,000	NZD	358,400	25.10.05	
NEW ZEALAND - GOVT		250,000	NZD	231,125	28.11.05	
NORTH CYPRUS - M.GOKHAN KODAK		25,000	USD	32,800	31.01.06	
NORWEGIAN - GOVT/RC		10,000,000	NOK	1,975,000	09.11.05	RELIEF ACTIVITIES INCL. CHILDREN & VULNERABLE GROUPS
NORWEGIAN - GOVT/RC		5,500,550	NOK	1,086,359	09.11.05	
NORWEGIAN - RC		1,748,067	NOK	339,125	15.12.05	TSU
OPEC FUND F.INTERNATIONAL DEV.		600,000	USD	768,300	13.10.05	+ INDIA (DM, 05AA047) AND AFGHANISTAN (DM, 05AA045), USD 200'000 EACH FOR RELIEF SUPPLIES
PHILIP MORRIS		30,000	USD	38,415	24.10.05	
PHILIPPINES - RC		10,000	USD	12,805	03.11.05	
POLAND - PRIVATE DONORS				3,235	17.10.05	
PRIVATE DONORS ON LINE				804,873	17.11.05	
PRIVATE DONORS ON LINE				39,341	26.01.06	
PRIVATE DONORS ON LINE				10,640	02.02.06	
SAUDI ARABIA - PRIVATE DONOR		10,344	USD	13,245	16.11.05	
SAUDI ARABIA - PRIVATE DONOR		3,200	USD	4,227	27.03.06	
SINGAPORE - GOVT & RC				100,000	26.10.05	PROCUREMENT OF RELIEF ITEMS
SINGAPORE - GOVT & RC				100,000	09.11.05	PROCUREMENT EMERGENCY RELIEF & MEDICAL
SINGAPORE - PRIVATE DONOR		50,000	EUR	77,850	11.10.05	
SLOVENIAN - GOVT		14,981	EUR	23,153	17.11.05	
SLOVENIAN - GOVT		27,737	EUR	42,924	07.12.05	
SOUTH AFRICA - PRIVATE DONOR		1,000	USD	1,280	27.10.05	
SPANISH - PRIVATE DONORS				4,467	14.11.05	
SWEDISH - GOVT through RC		2,000,000	SEK	334,000	11.10.05	
SWEDISH - GOVT through RC & RC		15,400,000	SEK	2,571,800	14.10.05	
SWEDISH - RC		25,000,000	SEK	4,050,000	08.11.05	
SWEDISH - RC		20,000,000	SEK	3,250,000	15.12.05	

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

29/03/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
SWISS - RC				100,000	28.11.05	
SWISS - PRIVATE DONORS				14,850	12.10.05	
SWISS - PRIVATE DONOR				25,000	09.12.05	
TAIWAN RED CROSS ORGANISATION		59,000	USD	77,408	05.12.05	PROCUREMENT OF MEDICAL SUPPLIES
TRINIDAD & TOBAGO - RC				3,370	30.12.05	
UNITED ARAB EMIRATES -RC		10,000	USD	12,805	01.11.05	
USA - COCA-COLA		1,000,000	USD	1,294,000	11.10.05	BILATERAL PAKISTAN RC
SWISS WHO/VERF STAFF				4,000	09.11.05	
USA - ADC FOUNDATION		10,000	USD	12,805	31.10.05	
USA - ALTRIA KRAFT		50,000	USD	65,600	15.12.05	
USA - APPLIED MATERIALS		34,684	USD	45,505	15.12.05	
USA - EMC		36,000	USD	47,232	15.12.05	
USA - ENTERPRISE FOUNDATION		250,000	USD	328,000	15.12.05	
USA - HARRIS FOUNDATION		100,000	USD	131,200	15.12.05	
USA - INTEL FOUNDATION		500,000	USD	656,000	15.12.05	
USA - LEHMAN BROTHERS		165,279	USD	216,846	15.12.05	
USA - PRIVATE DONORS				86,289	25.10.05	
USA - PRIVATE DONORS		1,276	USD	1,674	09.12.05	
USA - PRIVATE DONORS		7,851	USD	10,371	13.02.06	
USA - SAMYATEX		2,500	USD	3,280	15.12.05	
SUB/TOTAL RECEIVED IN CASH				72,607,618	CHF	47.8%
IN-KIND AND SERVICES						
DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
in kind list updated					21.03.06	
AMERICAN - RC				5,669,973		30518 BEDSHEETS, 28000 BUCKETS, 70000 BLANKETS, 3000 TARPAULINS, 5000 FAMILY TENTS , 18000 KITCHEN SETS, 3200 WINTERISED FAMILY TENTS, 18000 HYGIENIC PARCELS, 50000 SHAWLS, 2000 TENTS GAMMAX, 152900 BLANKETS QUILTS, SHIPPING/TRANSPORT
AUSTRIAN - RC				2,019,212		21000 HYGIENIC PARCELS, 7 EMERGENCY HEALTH KITS, 300 FAMILY TENTS, 1800 WINTERISED FAMILY TENTS, 76000 BLANKETS, 18000 BLANKETS QUILT, SHIPPING/TRANSPORT
AUSTRIAN - RC				463,650		ERU WATER TREATMENT & SUPPLY LINE, PERSONNEL
BELGIAN - RC/FL				3,251,428		60000 BEDSHEET, 11720 BLANKETS, 95305 BLANKETS QUILT, 20060 JERRYCANS, 2275 WINTERISED FAMILY TENTS, 3500 KITCHEN SETS, 20000 CORRUGATED IRON SHEET, SHIPPING/TRANSPORT

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

29/03/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
BELGIAN - RC/FR				546,759		12500 BLANKETS, 1250 KITCHEN SETS, 1552 FAMILY TENTS, 1250 TARPAULINS, SHIPPING/ TRANSPORT
BRITISH - RC				2,770,126		600 KITCHEN SETS, 6000 WINTERISED FAMILY TENTS, 2000 JERRYCANS 10L., 20060 JERRYCANS 20L., 504000 WATER PURIFICATION TABLETS, 25000 HURRICANE LAMPS, 600 FAMILY TENTS, 42300 TARPAULINS 4X6M, 300 TARPAULINS 4X60M., 21700 BLANKETS, 50 KITS TAPSTAND & PIPEWORK WAT/SAN
CANADIAN - RC				3,585,575		3000 WINTERISED FAMILY TENTS, 2000 GAMMAX TENTS, 3300 BLANKETS HIGH LOFT, 12000 BLANKETS 80%, 5 EMERGENCY HEALTH KITS, 94 SHEETING TARPAULINS, 11000 TARPAULINS, TRANSPORT/SHIPPING
DANISH - RC				1,025,320		1.5, BASE CAMP, 30 EMERGENCY HEALTH KITS, 50 DELEGATE HEALTH KITS, 8000 KITCHEN SETS, 9000 TARPAULINS, 750 WINTERISED FAMILY TENTS
DANISH - RC				563,850		ERU TELECOM & LOGISTICS UNITS
EGYPTIAN - RC				78,716		2000 BLANKETS, 20 FAMILY TENTS, TRANSPORT/SHIPPING
FINNISH - RC				3,871,778		10000 KEROSENE STOVES, 5500 HURRICANE LAMPS, 6607 WINTERISED FAMILY TENTS, 10000 CORRUGATED IRON SHEET , TRANSPORT/SHIPPING
FRENCH - RC				582,247		4791 KITCHEN SETS, 20910 JERRYCANS, 1440 HURRICANE LAMPS, 15000 SHAWLS, 2300 TARPAULINS, TRANSPORT/ SHIPPING
FRENCH - RC				261,791		ERU BASIC HEALTH CARE UNIT (ECHO FUNDED)
GERMAN - RC				787,278		ERU SPECIALISED WATSAN MODULE (ECHO FUNDED)
GERMAN - RC				5,915,846		10000 SLEEPING BAGS, 30380 TARPAULINS, 10000 HURRICANE LAMPS, 10000 BLANKETS, 8000 WINTERISED FAMILY TENTS, 200 HOSPITAL BEDS, 1 MOBILE KITCHEN, TRANSPORT/SHIPPING
IRISH - RC				936,500		7300 BLANKETS, 2250 WINTERISED FAMILY TENTS
LUXEMBURG - RC				215,594		6000 BLANKETS, 10 EMERGENCY HEALTH KITS,
NEPAL - RC				5,000		1000 BLANKETS
NETHERLANDS - RC				4,771,896		573 FAMILY TENTS, 27 EMERGENCY HEALTH KITS, 20000 TARPAULINS, 51516 BLANKETS 80 %, 30000 BLANKETS 50%, 7000 KEROSENE HEATERS, 288520 BEDSHEETS, 72000 BLANKETS QUILTS, 45000 HYGIENIC PARCELS, 2427 WINTERISED TENTS, 16000 KITCHEN SETS, 10 SUPPL.UNITS OF NEHK,

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

29/03/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
NORWEGIAN - RC				2,902,452		11320 BLANKETS, 1 DIATHERMY, 2 DOCTORS OFFICE MODULES, 9 HEATERS, 3 CHOLERA KITS, 1 LABORATORY MODULE, VARIOUS MEDICAL ITEMS, 2 PROPAC ECG MONITORS, 7355 SLEEPING BAGS, 95 SURGICAL SUPPLY KITS, 2 MOTHER AND CHILD CARE MODULE, 1620 TARPULINS, 5 TENTS ALFA, 29 TENTS DELTA, 870 TENTS GAMMAX 24M2, 21 TENTS 90M2, 50 FAMILY TENTS 16M2, 8 TENTS WAREHOUSE, 40 TRUCKS M6, 4 WATER PURIFICATION UNITS, 2 WATERTANKS 10M3, 2 WATERTANK 5M3, 1 X-RAY MODULE
NORWEGIAN - RC				730,000		ERU REFERRAL HOSPITAL
QATAR - RC				2,312,371		20000 AMOXYCILLIN, 6158 FAMILY TENTS, 1170 BEDS RIGID FRAME, 6582 BEDSHEETS, 34881 BLANKETS QUILT, 45960 BLANKETS 50%, 2200 BODY BAGS, 700 BUCKETS, 44 GENERATORS, 12569 HYGIENIC PARCELS, 1998 JERRYCANS 10L, 1200 JERRYCANS 20 L., 40 FIRST AID KITS FOR CAR, 1001 KITCHEN SETS, 300 HURRICANE LAMPS, 925 SHAWLS, 92 VARIOUS MEDICINE, DATES, LENTILS, ASSORTED FOOD
SINGAPORE - RC				1,123,621		13900 FOOD RATION MRS, SHIPPING/TRANSPORT
SLOVENIAN - RC				404,690		5 MEDICAL ITEMS VARIOUS, 10000 SLEEPING BAGS
SPANISH - RC				119,225		8125 BLANKETS, 504 SLEEPING BAGS, 2400 TARPULINS, 150 FAMILY TENTS
SPANISH - RC				415,580		1 ERU BASIC HEALTH CARE UNIT (ECHO FUNDED)
SWEDISH - RC				339,900		ERU WAT-SAN, MASS SANITATION MODULE UNIT
SWEDISH - RC				391,762		904 WINTERISED TENTS, 3000 SLEEPING BAGS, TRANSPORT/ SHIPPING
SWISS - RC				2,681,514		4000 AMOXYCILLIN, 40000 BEDSHEETS, 4500 TARPULINS, 200 FAMILY TENTS, 2 EMERGENCY HEALTH KITS, 12500 BLANKETS QUILT, 6140 BLANKETS, 80%, 20000 BLANKETS 50%, 1562 KEROSENE HEATERS, 2500 KITCHEN SETS, 10000 SHAWLS, 18000 CORRUGATED IRON SHEETS, 2000 WINTERISED TENTS, TRANSPORT/SHIPPING
AUSTRALIA	DELEGATES			90,800		
AUSTRIA	DELEGATES			17,800		
CANADA	DELEGATES			24,600		
DENMARK	DELEGATES			68,800		

Pakistan - earthquake

ANNEX 1

APPEAL No. 05EA022

PLEDGES RECEIVED

29/03/2006

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
FINLAND	DELEGATES			50,600		
GERMANY	DELEGATES			8,800		
GREAT BRITAIN	DELEGATES			76,400		
ICELAND	DELEGATES			65,000		
NETHERLANDS	DELEGATES			76,600		
NEW ZEALAND	DELEGATES			6,200		
NORWAY	DELEGATES			460,600		
SWEDEN	DELEGATES			59,600		
SWISS RC	DELEGATES			100,600		
VARIOUS DONORS				4,349,377		ESTIMATED INTERNATIONAL TRANSPORT/INSURANCE COSTS (30% OF TOTAL VALUE OF RELIEF ITEMS)
SUB/TOTAL RECEIVED IN KIND/SERVICES				54,199,431	CHF	35.6%

ADDITIONAL TO APPEAL BUDGET

DONOR	CATEGORY	QUANTITY	UNIT	VALUE CHF	DATE	COMMENT
SUB/TOTAL RECEIVED				0	CHF	
